



ROTARIANS AGAINST MALARIA

LONG -LASTING INSECTICIDAL NET DISTRIBUTION REPORT - ORO PROVINCE 2025

Sohe & Ijivitari districts

Carried Out in Partnership with National Malaria Control Program,

Oro Provincial Health Authority and Church Health Services

With Support from The Global Fund



8th August 2025 to 22nd October 2025

Table of Contents

EXECUTIVE SUMMARY	3
Rotarians Against Malaria and LLIN Distributions in Papua New Guinea	6
National Malaria Stratification Framework and Application in Oro Province	8
Coordination and Guidance from the National Malaria Control Programme and Oro Provincial Health Authority	10
Schedule of LLIN Activities – Oro Province	13
Methodology – Micro-Planning, Household Survey and LLIN Allocation	15
Household Survey and Data Collection.....	17
Village Validation and LLIN Allocation.....	17
Survey Coverage Limitations	17
LLIN Household Distribution Process	18
Distributions and Beneficiary Verification.....	18
LLIN Coding and Commodity Accountability.....	19
Distribution in Remote Communities.....	19
Logistics and Supply Chain Management.....	20
LLIN distribution in Oro Province - Results and Analysis.....	Error! Bookmark not defined.
District-Level Results	21
Local Level Government Analysis.....	22
Population Analysis	23
Household Coverage Analysis	24
Overall Programme Performance	24
Nets Donated to Health Facilities.....	24
Budget Performance Analysis-	25
Outstanding Fly-Off Operations and Impact on Budget Performance	28
Communication Infrastructure Analysis.....	29
Lessons Learned	31
Acknowledgements.....	32
 Annex One	 Pictures of different stages of LLIN distributions
Annex Two	Detailed distribution data of Ijivitari district
Annex Three	Detailed distribution data of Sohe district

EXECUTIVE SUMMARY

Malaria remains one of the most significant public health challenges in Papua New Guinea (PNG) and continues to be a leading cause of illness, outpatient attendance, hospital admissions, and preventable deaths, particularly in lowland, coastal, riverine, swamp, and tropical forest environments where climatic and ecological conditions support year-round mosquito breeding and sustained malaria transmission. Despite significant progress achieved through coordinated malaria control interventions over the past two decades, malaria continues to impose a substantial burden on vulnerable populations, particularly children under five years of age, pregnant women, and rural communities with limited access to healthcare services.

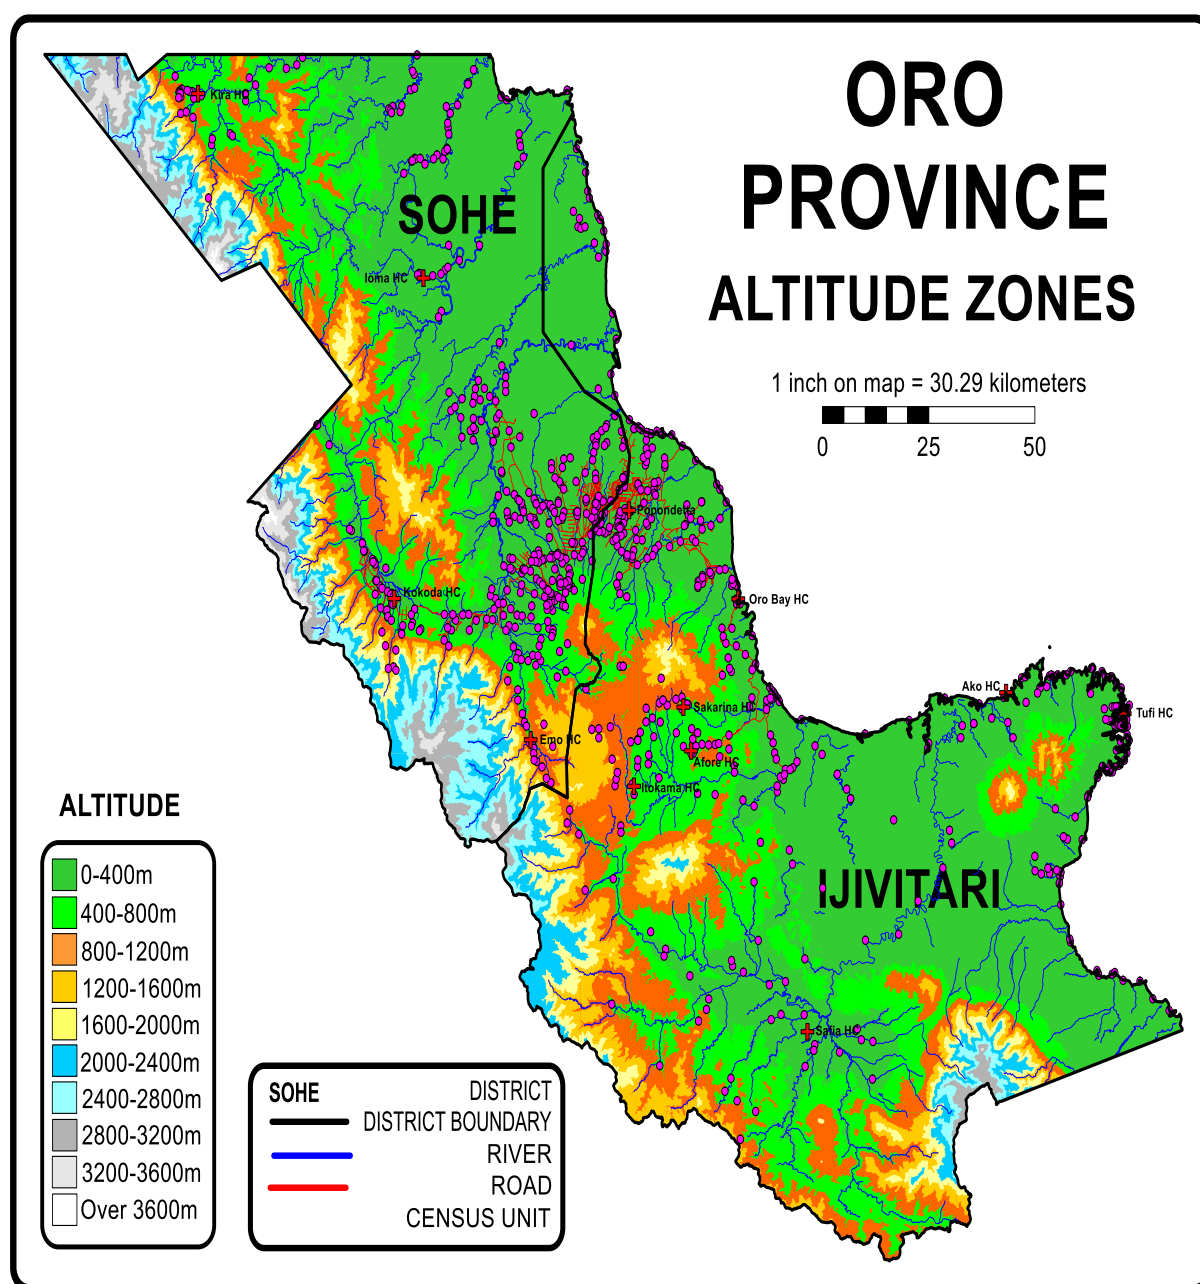


Figure 1 Altitude map of Oro Province

Oro Province remains one of Papua New Guinea's malaria-endemic provinces due to its tropical climate, extensive rainfall, dense forests, river systems, coastal environments, and widespread rural populations. The province's environmental conditions provide ideal breeding habitats for *Anopheles* mosquitoes, the primary vectors responsible for malaria transmission. Communities throughout Sohe and Ijivitari Districts continue to face elevated malaria risks due to their proximity to rivers, wetlands, forested areas, and coastal environments where mosquito breeding occurs throughout the year. Malaria not only affects individual health outcomes but also contributes to school absenteeism, reduced workforce productivity, increased healthcare costs, and loss of household income, making malaria prevention one of the most cost-effective public health investments in Papua New Guinea.

Long-Lasting Insecticidal Nets (LLINs) remain one of the most effective, evidence-based, and cost-efficient malaria prevention interventions available. LLINs provide both personal and community-wide protection by preventing mosquito bites and reducing mosquito populations through the insecticidal treatment incorporated into the netting. Numerous studies conducted globally and within Papua New Guinea have demonstrated that high LLIN ownership and utilisation significantly reduce malaria transmission, malaria-related illness, severe malaria cases, and malaria mortality. As a result, universal LLIN coverage remains a cornerstone of the National Malaria Control Programme's (NMCP) strategy to reduce malaria transmission and support Papua New Guinea's long-term malaria elimination goals.

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was implemented through a collaborative partnership between the National Department of Health (NDOH), National Malaria Control Programme (NMCP), Oro Provincial Health Authority (OPHA), District Health Services, Rotarians Against Malaria (RAM), Local Level Governments, health facilities, church organisations, community leaders, village volunteers, and development partners. The programme was funded through the Global Fund-supported National Malaria Control Programme and formed part of Papua New Guinea's ongoing strategy to maintain universal LLIN coverage across malaria-endemic regions of the country.



Figure 2 LLINs are being loaded to remote villages in Sahio Health Center

The primary objective of the programme was to conduct a comprehensive household-level survey to determine actual household populations and LLIN requirements, followed by the equitable distribution of LLINs to all eligible households throughout Oro Province. The programme was implemented across the two districts of Sohe and Ijivitari, covering coastal communities, riverine settlements, urban and peri-urban populations, plantation communities, mountainous villages, forested regions, and remote rural communities. Household survey activities commenced in August 2025 and were completed in October 2025. In Sohe District, survey activities were undertaken between 8 August and 14 October 2025, while LLIN distribution was conducted between 2 September and 17 October 2025. In Ijivitari District, survey activities were undertaken between 18 August and 11 October 2025, with LLIN distribution occurring between 30 August and 22 October 2025.

A total of 280,983 people from 53,281 households located in 779 villages were successfully surveyed during the family-level survey. Based on the survey results, a total of 143,135 Long-Lasting Insecticidal Nets (LLINs) were distributed throughout the province, achieving an overall distribution ratio of 50.9 LLINs per 100 people surveyed, consistent with National Malaria Control Programme guidelines and universal coverage objectives.

District-level implementation achieved strong coverage across both districts. In Sohe District, a total of 128,438 people from 24,356 households located in 389 villages were surveyed, resulting in the distribution of 66,456 LLINs, achieving a coverage ratio of 51.7 LLINs per 100 people. In Ijivitari District, a total of 152,545 people from 28,925 households located in 390 villages were surveyed, resulting in the distribution of 76,679 LLINs, achieving a coverage ratio of 50.3 LLINs per 100 people.

Implementation was undertaken across some of Oro Province's most challenging environments, including remote mountainous communities in Afore and Safia, isolated coastal settlements in Cape Nelson and Tufi, plantation communities, and densely populated urban settlements around Popondetta. Distribution teams utilised a combination of road transport, boats, and extensive trekking to reach hard-to-access communities. Despite logistical challenges associated with difficult terrain, transportation constraints, and adverse weather conditions, all planned activities within the accessible health facility catchments were successfully completed.

The programme was implemented efficiently and within the approved budget. The total operational budget for the Oro Province LLIN Family-Level Survey and Distribution Programme was PGK 492,723, while actual expenditure totalled PGK 487,488, resulting in an overall saving of PGK 5,235 and a budget utilisation rate of approximately 98.9 percent. Although expenditure on fuel and vehicle hire exceeded original estimates due to increased fuel prices and transport costs, savings achieved in aircraft hire, training, boat hire, stationery, and contingency expenditures offset these increases and enabled the programme to remain within budget.

The successful completion of the 2025 Oro Province LLIN Family-Level Survey and Distribution Programme has strengthened malaria prevention efforts throughout the province and contributed significantly to maintaining universal LLIN coverage among at-risk populations. By ensuring that more than 280,000 people have access to effective malaria prevention tools, the programme will contribute substantially to reducing malaria transmission, decreasing malaria-related illness and deaths, protecting vulnerable populations, and advancing Papua New Guinea's long-term goal of malaria elimination. The programme also demonstrates the

continued importance of strong partnerships between government agencies, Provincial Health Authorities, District Health Services, communities, development partners, and implementing organisations in achieving sustainable malaria control outcomes throughout Papua New Guinea.

Despite the successful completion of the main LLIN distribution programme, several remote fly-off communities within Oro Province could not be covered during the 2025 implementation period due to the exceptionally high cost of helicopter and fixed-wing aircraft charter services required to access these isolated locations. As a result, distribution activities for the Safia, Emo, and Kira Health Centre catchment areas have been deferred to a subsequent phase of operations planned for 2026. These areas comprise 83 villages, requiring approximately 4,950 LLINs to achieve full coverage.

These fly off – remote communities are located within some of the most geographically challenging parts of Oro Province, characterised by rugged mountainous terrain, dense rainforest, limited transport infrastructure, and the absence of road access, with many villages accessible only by helicopter, fixed-wing aircraft, or several days of trekking. The high cost of aviation support, limited aircraft availability, difficult landing conditions, unpredictable weather patterns, fuel logistics, and the complex coordination required across multiple fly-off locations have significantly increased operational complexity and delayed implementation. Rotarians Against Malaria (RAM), in collaboration with the National Malaria Control Programme, Oro Provincial Health Authority, and development partners, is actively pursuing additional funding and aviation support to enable these operations. Once the necessary resources are secured, these remaining communities will be included in a future distribution phase, ensuring full provincial coverage and strengthening malaria prevention efforts among some of Oro Province's most isolated and vulnerable populations.

Rotarians Against Malaria and LLIN Distributions in Papua New Guinea

Rotarians Against Malaria (RAM) was established in 1997 by the Port Moresby Rotary Club in response to the significant burden of malaria throughout Papua New Guinea. Since its establishment, RAM has evolved into one of the National Department of Health's (NDOH) principal implementing partners for malaria prevention and control, supporting the National Malaria Control Programme (NMCP) in the planning, coordination, implementation, monitoring, and evaluation of Long-Lasting Insecticidal Net (LLIN) distribution programmes throughout the country.

Working in partnership with Provincial Health Authorities, District Health Services, communities, and development partners, RAM has successfully implemented multiple rounds of LLIN distributions throughout Papua New Guinea with support from the Global Fund, Against Malaria Foundation (AMF), the Government of China, and other development partners. Through these partnerships, millions of LLINs have been distributed nationwide, contributing significantly to reductions in malaria prevalence and strengthening community protection against malaria transmission.

For more than two decades, RAM has worked closely with the National Department of Health, National Malaria Control Programme, Provincial Health Authorities, District Health Services, community leaders, church organisations, development partners, and local communities to strengthen malaria prevention and control efforts. Through successive rounds of LLIN

distribution, RAM has played a critical role in expanding access to malaria prevention services and ensuring that vulnerable populations are protected against malaria transmission.

Since the introduction of large-scale LLIN distribution programmes, Papua New Guinea has received substantial support from the Global Fund to Fight AIDS, Tuberculosis and Malaria, the Against Malaria Foundation (AMF), the Government of China, the World Health Organization (WHO), UNICEF, and other development partners. Through these partnerships, millions of LLINs have been procured and distributed across the country over multiple distribution rounds. These investments have contributed significantly to reducing malaria prevalence and strengthening household protection against malaria transmission throughout Papua New Guinea.

RAM has been at the forefront of implementing these national LLIN distribution programmes. Working closely with Provincial Health Authorities and District Health Services, RAM has successfully delivered LLINs to some of the country's most remote and difficult-to-access locations, including isolated islands, mountainous communities, riverine settlements, border communities, and remote inland villages. Through continuous improvements in operational planning, logistics management, volunteer training, monitoring systems, and community engagement, RAM has strengthened the effectiveness and accountability of LLIN distribution programmes nationwide.

The family-level survey approach adopted by RAM ensures that LLIN allocations are based on actual household populations rather than population projections, improving targeting, reducing wastage, and ensuring equitable access to LLINs across all communities.

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme forms part of Papua New Guinea's ongoing effort to maintain universal LLIN coverage and strengthen malaria prevention throughout malaria-endemic provinces. The programme was implemented through a partnership between the National Department of Health (NDOH), National Malaria Control Programme (NMCP), Oro Provincial Health Authority (OPHA), District Health Services, Rotarians Against Malaria (RAM), Local Level Governments, health facilities, church organisations, community leaders, and village volunteers.

The continued success of LLIN distribution programmes demonstrates the importance of strong partnerships between government agencies, Provincial Health Authorities, District Health Services, development partners, community leaders, volunteers, and implementing organisations such as RAM. Continued investment in LLIN replacement campaigns, community awareness, surveillance systems, and integrated malaria control interventions will remain essential for sustaining gains achieved to date and advancing Papua New Guinea's long-term vision of a malaria-free future.

National Malaria Stratification Framework and Application in Oro Province

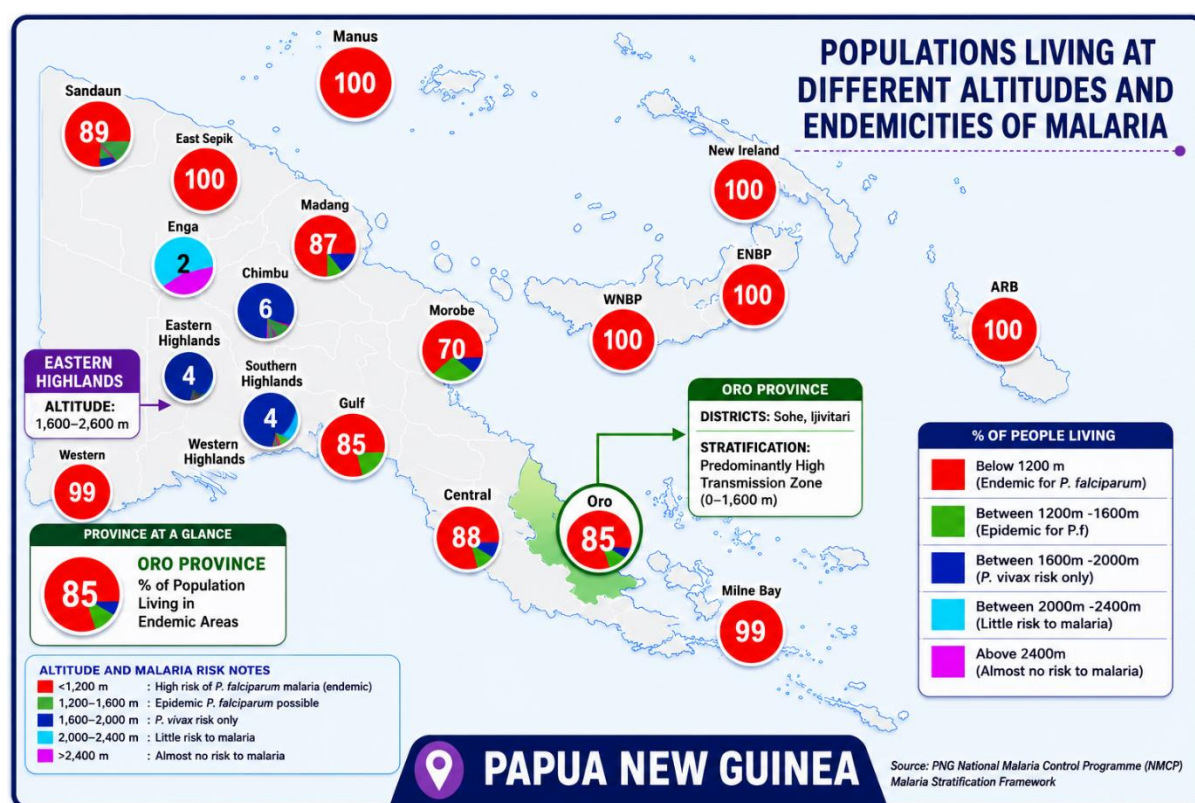


Figure 3 Malaria stratification in Papua New Guinea

The National Department of Health (NDOH) and National Malaria Control Programme (NMCP) apply a stratified approach to malaria prevention and control throughout Papua New Guinea to ensure that interventions are targeted according to malaria transmission risk. This approach recognises that malaria epidemiology varies considerably across the country due to differences in altitude, climate, ecology, population density, environmental conditions, and access to health services. Epidemiological stratification guides the allocation of resources, including Long-Lasting Insecticidal Nets (LLINs), to maximise the effectiveness and efficiency of malaria prevention interventions.

Malaria remains endemic throughout much of Oro Province, where extensive coastal plains, tropical rainforests, river systems, swamps, wetlands, and high annual rainfall create ideal conditions for mosquito breeding and year-round malaria transmission. The province is therefore considered one of Papua New Guinea's priority provinces for malaria prevention and control. The majority of the population resides within environments that support sustained malaria transmission, making LLIN distribution a critical component of provincial malaria control efforts.

High Transmission Zones (0–1,600 Metres)

Areas below 1,600 metres elevation are classified as high-transmission malaria zones and remain the highest priority for malaria prevention interventions. These areas experience favourable environmental conditions for mosquito breeding and sustained malaria

transmission, including warm temperatures, high rainfall, coastal environments, extensive river systems, wetlands, floodplains, and tropical forest ecosystems.

The vast majority of Oro Province falls within this high-transmission category. Most communities within Sohe and Ijivitari Districts, including Popondetta Urban, Oro Bay Rural, Cape Nelson Rural, Higaturu Rural, Tamata Rural, and Kokoda Rural Local Level Government (LLG) areas, are located below 1,600 metres elevation and experience persistent malaria transmission throughout the year. These communities account for the majority of the province's population and represent the principal focus of LLIN distribution activities and other malaria prevention interventions.

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme prioritised these high-risk populations where malaria burden remains highest and where environmental conditions continue to support year-round mosquito breeding and disease transmission.

Transitional Transmission Zones (1,600–2,000 Metres)

Communities located between 1,600 and 2,000 metres elevation are classified as transitional or unstable malaria transmission zones. Malaria transmission within these areas is generally lower and more variable than in the lowlands and is influenced by seasonal climatic conditions, environmental factors, and population movement from endemic areas.

Within Oro Province, portions of the mountainous communities located along the northern slopes of the Owen Stanley Range, particularly within the upper Kokoda and Afore regions, fall within this transitional transmission category. While malaria transmission is generally lower than in coastal and lowland areas, these communities remain vulnerable to periodic outbreaks and imported malaria cases due to population movement between endemic lowland communities and higher altitude settlements.

The rugged terrain, difficult access, and remoteness of these communities reinforce the importance of maintaining malaria prevention measures and ensuring continued access to LLINs and malaria awareness activities.

Low or Negligible Transmission Zones (Above 2,000 Metres)

Areas located above 2,000 metres elevation are generally considered unsuitable for sustained malaria transmission due to cooler temperatures and environmental conditions that limit mosquito survival and parasite development. Under NMCP policy, routine mass LLIN distribution is generally not prioritised within these communities unless epidemiological evidence suggests a specific malaria risk.

Only a very small proportion of Oro Province falls within this elevation range, primarily within isolated sections of the Owen Stanley Mountain ranges. These areas contain relatively small populations compared with the province's lowland and coastal communities and therefore contribute minimally to the overall malaria burden within the province.

Application of the Stratification Framework in the 2025 Oro Province LLIN Programme

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was implemented in accordance with the NMCP National Malaria Stratification Framework. Priority was given to populations residing within malaria-endemic coastal, lowland, riverine, swamp, plantation, forest, and wetland environments where malaria transmission remains highest. These areas

encompass the majority of communities within Sohe and Ijivitari Districts and account for most of the province's population.

The programme successfully surveyed 280,983 people residing in 53,281 households across 779 villages and distributed 143,135 LLINs throughout the province. Household-level population verification undertaken through the Survey books data collection ensured that LLIN allocations reflected actual household composition and sleeping arrangements rather than projected population estimates.

The programme achieved coverage across all major malaria-endemic communities within Oro Province, including coastal settlements in Cape Nelson and Oro Bay, plantation and peri-urban communities surrounding Popondetta, extensive rural populations within Higaturu and Tamata, and remote communities throughout Kokoda and Afore. Through this targeted approach, the programme strengthened household protection against malaria and supported the National Malaria Control Programme's objective of maintaining universal LLIN coverage within high-risk malaria transmission zones.

The successful application of the National Malaria Stratification Framework in Oro Province demonstrates the importance of evidence-based planning and targeted resource allocation in malaria control. By focusing interventions on populations most at risk of malaria transmission, the programme contributes directly to reducing malaria morbidity and mortality while supporting Papua New Guinea's long-term malaria elimination goals.

Coordination and Guidance from the National Malaria Control Programme and Oro Provincial Health Authority



Figure 4 Provincial planning meeting with CEO ORO PHA & Public Health Director

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was fully funded by the Global Fund and implemented through a coordinated partnership between the National

Department of Health (NDOH), National Malaria Control Programme (NMCP), Oro Provincial Health Authority (OPHA), District Health Services, Rotarians Against Malaria (RAM), Local Level Governments (LLGs), health facilities, church health services, community leaders, and village volunteers. This partnership provided the framework for planning, implementation, supervision, monitoring, and reporting throughout all phases of the programme and ensured that malaria prevention services were delivered effectively across both accessible and hard-to-reach communities throughout Oro Province.

At the provincial level, OPHA provided overall leadership, coordination, and oversight of programme implementation. Working closely with RAM and District Health Services, OPHA ensured that implementation reflected provincial health priorities, local epidemiological conditions, operational realities, community needs and local security risk assessment. Provincial Public Health officials actively participated in planning meetings, implementation reviews, supervision activities, and progress monitoring throughout the programme period.

A key component of programme preparation was the Provincial LLIN Planning and Coordination Meeting convened by OPHA prior to implementation. These planning sessions brought together representatives from OPHA, RAM, District Health Services, District Health Managers, health facility managers, church health services, and key stakeholders to review population estimates, village lists, malaria risk profiles, health facility catchments, LLIN requirements, implementation schedules, transport arrangements, and operational risks. Particular attention was given to the logistical challenges associated with reaching remote coastal communities, plantation settlements, forest communities, riverine villages, and mountainous communities throughout Sohe and Ijivitari Districts.

Following endorsement of implementation plans, OPHA communicated programme schedules, operational responsibilities, and reporting requirements to District Health Managers and health facility managers throughout Sohe and Ijivitari Districts. District Health Managers played a critical role in coordinating implementation activities within their respective districts and ensuring the active participation of government health facilities, church health services, health workers, and community structures.

District Health Services and Church Health Services supported community mobilisation, volunteer recruitment, local logistics planning, transport coordination, supervision, stock management, and integration of LLIN activities into routine public health operations. Government health centre staff, church health facilities, aid post personnel, community health workers, and district public health officers provided operational support throughout the programme and served as focal points for implementation within their respective catchment areas.

Health facility staff throughout Sohe and Ijivitari Districts played an important role in supporting volunteer training, household survey activities, community awareness campaigns, beneficiary verification, stock management, and LLIN distribution. Their local knowledge, community networks, and established relationships with village leaders significantly strengthened programme implementation, accountability, and community participation.

Throughout the implementation of the 2025 Oro Province LLIN Family-Level Census and Distribution Programme, Rotarians Against Malaria (RAM) Provincial Team Leaders were responsible for providing weekly implementation updates on the progress of LLIN operations across all health centre catchment areas. Progress reports were prepared for each health

facility and included the implementation status of key operational activities such as micro-planning, volunteer training, household survey, LLIN distribution, and any outstanding activities. The reports also identified the RAM LLIN officers assigned to each health centre and tracked progress against planned implementation schedules.



Figure 5 Orientation to Oro PHA staff on upcoming LLIN distributions

These weekly updates were shared with the Oro Provincial Health Authority (OPHA) to strengthen programme monitoring, coordination, and operational oversight. The reporting mechanism enabled OPHA and District Health Services to monitor implementation progress in real time, identify operational bottlenecks, and provide timely technical guidance where required. It also facilitated the sharing of important field information, including emerging tribal conflicts, security concerns, accessibility issues, adverse weather conditions, transport constraints, and other logistical challenges that could affect programme implementation. This collaborative monitoring approach enhanced communication between RAM and OPHA, supported informed decision-making, improved resource mobilisation, and contributed to the timely and effective implementation of LLIN distribution activities throughout Oro Province.

Logistics management was jointly coordinated by RAM, OPHA, District Health Services, District Health Managers, and health facility staff. LLIN stocks were transported from provincial storage facilities to district warehouses, health centres, aid posts, and community distribution points throughout the province. Due to Oro Province's diverse geography, transportation arrangements involved a combination of road transport, four-wheel-drive vehicles, coastal shipping, boats, outboard motor canoes, aircraft, and extensive trekking to reach isolated communities.

Particular logistical attention was required for remote communities located within the mountainous regions of Afore, Kokoda, Safia, Emo, and Kira catchment areas. While the majority of villages were successfully reached during the 2025 implementation period, several remote fly-off communities within Safia, Emo, and Kira Health Centre catchments could not be serviced due to the high cost of helicopter and fixed-wing aircraft charter services. These

locations comprise approximately 83 villages, requiring approximately 4,950 LLINs. RAM, OPHA, and NMCP are actively pursuing additional funding and aviation support to facilitate distribution to these communities during a subsequent phase of operations planned for 2026.

The successful implementation, except the remote – fly off areas- of the Oro Province LLIN Family-Level Survey and Distribution Programme demonstrates the value of strong partnerships between national, provincial, district, health facility, and community stakeholders. Through coordinated planning, shared responsibilities, effective communication, and innovative logistical solutions, NMCP, OPHA, RAM, District Health Services, government health workers, church health services, community leaders, volunteers, and local transport providers ensured that LLINs reached eligible households throughout Oro Province, including many of the province's most remote and difficult-to-access communities.

Schedule of LLIN Activities – Oro Province

Table 2: Distribution Schedule of Oro Province

<i>District</i>	<i>Population</i>	<i>Survey</i>		<i>Distribution</i>	
		<i>Start</i>	<i>Finish</i>	<i>Start</i>	<i>Finish</i>
<i>Sohe</i>	128,438	08.08.25	14.10.25	02.09.25	17.10.25
<i>Ijivitari</i>	152,545	18.08.25	11.10.25	30.08.25	22.10.25

As shown in Table 2, the 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was implemented in phases across Sohe and Ijivitari Districts. Household survey activities commenced in August 2025 and continued through October 2025, while LLIN distribution activities were progressively undertaken as survey data became available and logistical arrangements were completed. The phased implementation approach enabled the Oro Provincial Health Authority (OPHA), Rotarians Against Malaria (RAM), District Health Services, and health facilities to effectively manage personnel, resources, transport assets, and logistics across the province's diverse geographical environments.

Implementation commenced in Sohe District, which accounted for 128,438 people residing in 24,356 households across 389 villages. Household survey activities commenced on 8 August 2025 and were completed on 14 October 2025, while LLIN distribution activities were undertaken between 2 September 2025 and 17 October 2025. The district encompasses Kokoda Rural, Higaturu Rural, and Tamata Rural Local Level Governments and includes a mixture of plantation communities, lowland settlements, forest communities, and remote mountainous villages associated with the Kokoda region. The district distributed 66,456 LLINs, achieving a coverage rate of 51.7 LLINs per 100 people surveyed. The extended implementation period reflected the district's dispersed population, challenging terrain, and the considerable logistical effort required to reach remote communities located throughout the district.

Survey activities in Ijivitari District commenced on 18 August 2025 and were completed on 11 October 2025, while LLIN distribution activities were undertaken between 30 August 2025 and 22 October 2025. The district surveyed 152,545 people residing in 28,925 households across 390 villages and distributed 76,679 LLINs, achieving a coverage rate of 50.3 LLINs per 100 people surveyed. Implementation covered Oro Bay Rural, Cape Nelson Rural, Afore Rural, and

Popondetta Urban Local Level Governments. The district's operational environment included urban and peri-urban communities, extensive coastal settlements, oil palm plantation communities, forest villages, and remote mountainous communities within the Afore region. While implementation was completed within a relatively short timeframe, operational challenges were encountered due to difficult road access, remote coastal locations, adverse weather conditions, and the logistical complexity of servicing geographically dispersed communities.



Figure 6 Household survey volunteers training Saiho Health Center

To support implementation, LLIN bales, fuel, survey materials, and implementation teams were transported from provincial storage facilities to district warehouses, health centres, aid posts, and community distribution points throughout the province. Transport arrangements involved a combination of road transport, four-wheel-drive vehicles, boats, coastal transport, and extensive foot patrols to reach isolated villages located beyond established transport networks. Health facilities served as important operational hubs for volunteer training, stock management, community mobilisation, household verification, and LLIN distribution activities.

Despite the successful completion of the main provincial programme, several remote fly-off communities located within the Safia, Emo, and Kira Health Centre catchment areas could not be covered during the 2025 implementation period due to the exceptionally high cost of helicopter and fixed-wing aircraft charter services required to access these isolated locations. These areas comprise 83 villages, requiring approximately 4,950 LLINs to achieve full coverage.

The remote communities are located within some of the most geographically isolated parts of Oro Province and are characterised by rugged mountainous terrain, dense rainforest, limited transport infrastructure, and the absence of road access. Access to many villages is only possible through helicopter operations or fixed-wing aircraft support followed by extensive trekking. The high cost of aviation services, limited aircraft availability, adverse weather conditions, fuel logistics, and complex operational planning requirements significantly increased implementation costs and delayed the delivery of LLINs to these communities. RAM, in collaboration with NMCP and OPHA, is actively pursuing additional resources and aviation support to facilitate these operations. Once funding and aircraft support are secured, these communities will be incorporated into a subsequent phase of LLIN operations planned for 2026.

The successful completion of survey and distribution activities throughout Sohe and Ijivitari Districts demonstrates the effectiveness of strong provincial coordination, community participation, adaptive logistics planning, and collaboration between government health services, church health services, community leaders, volunteers, and implementation partners. Despite challenges associated with difficult terrain, remote settlements, transportation constraints, adverse weather conditions, and high operational costs, the programme successfully strengthened malaria prevention efforts throughout Oro Province and maintained progress towards achieving universal LLIN coverage across the province.

Methodology – Micro-Planning, Household Survey and LLIN Allocation

Micro-Planning and Programme Preparation

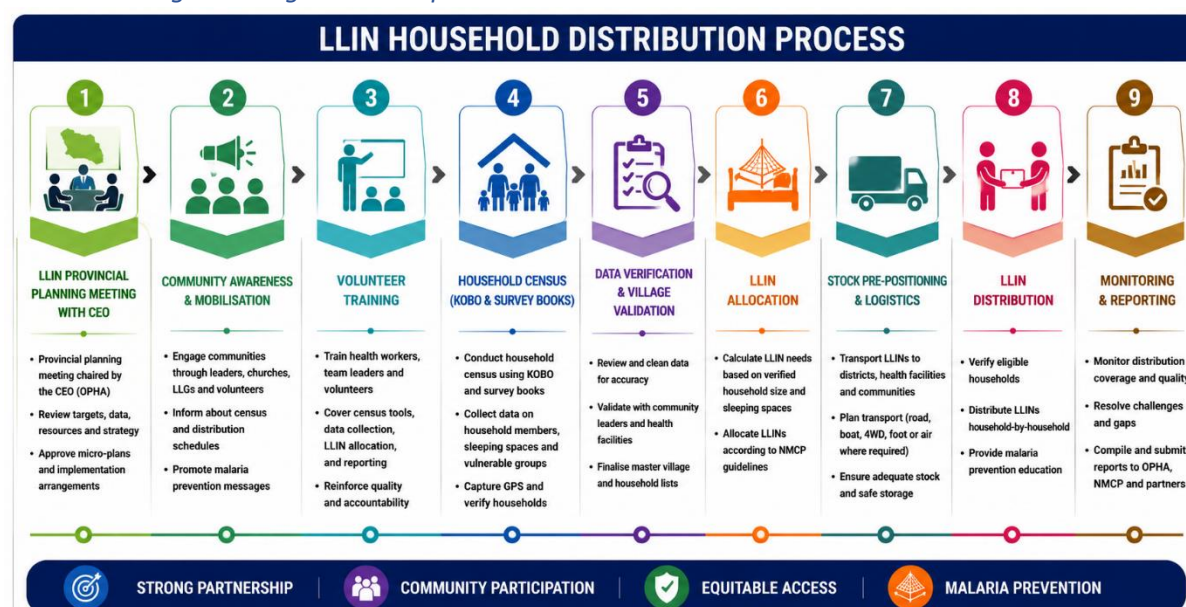


Figure 7 Process of LLIN distributions

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was implemented through a comprehensive micro-planning process jointly undertaken by Rotarians Against Malaria (RAM), the Oro Provincial Health Authority (OPHA), District Health Services, health facility staff, and community leaders. The objective of the planning process was to ensure accurate

household enumeration, efficient resource allocation, and equitable distribution of Long-Lasting Insecticidal Nets (LLINs) throughout the province.

A master village list covering all known settlements within Oro Province was developed using the 2000 National Population Survey, previous 2022 RAM household survey databases, Provincial Health Authority records, health facility catchment information, and village-level validation exercises. Population estimates, village locations, and health facility catchments were reviewed and verified through consultation with District Health Managers, health workers, Local Level Government representatives, and community leaders.

Detailed operational planning included village mapping, transport arrangements, volunteer deployment, workload allocation, implementation scheduling, logistics planning, stock management, and identification of distribution sites. Particular attention was given to geographically isolated communities located within Kokoda, Afore, Safia, Emo, and Kira catchments, where difficult terrain, limited transport infrastructure, and aviation requirements were anticipated.

Prior to implementation, extensive community awareness activities were undertaken through District Health Services, health facilities, church networks, ward councillors, village leaders, and community volunteers. Communities were informed of survey schedules, registration procedures, LLIN distribution arrangements, and key malaria prevention messages to maximise participation and community ownership



Figure 8 Sketch map of Kokoda Health Center's catchment area

Training was provided to District Health Teams, health workers, Community Team Leaders, and village volunteers. Training focused on household survey procedures, household data collection,

LLIN allocation guidelines, stock management, reporting requirements, malaria prevention messaging, and quality assurance processes.

Household Survey and Data Collection

All households were physically verified to confirm residency and household composition. Existing RAM household databases and previous survey records were used as reference materials; however, all household information was validated during field implementation to ensure that LLIN allocations reflected actual resident populations.

Household survey was undertaken by trained volunteers from same villages, monitored by RAM officers, District Health Teams, health workers, and community team leaders. Standardised information collected during registration included household composition, residency status, sleeping arrangements, communication access, and the presence of vulnerable groups, including children under five years of age, pregnant women, elderly persons, and persons living with disabilities.

Village Validation and LLIN Allocation

A province-wide master village list covering 779 villages was validated through consultation with District Health Services, health facilities, Local Level Governments, and community leaders. Survey findings were compared with previous RAM datasets and population estimates to identify settlement growth, population movements, and potential enumeration gaps.

Following verification, LLIN allocations were calculated in accordance with National Malaria Control Programme guidelines using verified household size and sleeping arrangements. Most households received between one and four LLINs depending on family composition and sleeping requirements. Verified survey data were also utilised for logistics planning, stock forecasting, and pre-positioning of LLIN stocks at provincial, district, health facility, and community levels.

Survey Coverage Limitations

While the programme successfully covered the majority of Oro Province, several remote fly-off communities within the Safia, Emo, and Kira Health Centre catchments could not be included during the 2025 implementation period due to the exceptionally high cost of helicopter and fixed-wing aircraft charter services required to access these isolated locations. These communities are located within rugged mountainous terrain characterised by dense rainforest, limited transport infrastructure, difficult landing conditions, and the absence of road access. Access to many villages is only possible through aviation support followed by extensive trekking over several hours or days. Funding limitations, aircraft availability, weather conditions, and the complexity of coordinating multiple fly-off locations prevented implementation during the reporting period.

The Oro Province LLIN Family-Level Survey methodology combined household data collection, household verification, community participation, and robust quality assurance processes to ensure accurate household enumeration and equitable LLIN allocation. This approach strengthened accountability, improved data quality, and ensured that LLINs were distributed according to verified household needs throughout Sohe and Ijivitari Districts.

LLIN Household Distribution Process

Social Mobilisation and Community Engagement



Figure 9 Household survey volunteers training at Oro Bay Health Center

Prior to LLIN distribution, an extensive social mobilisation and community awareness campaign was conducted throughout Sohe and Ijivitari Districts. Activities were coordinated by the Oro Provincial Health Authority (OPHA), District Health Services, health facilities, Local Level Governments, church organisations, ward councillors, village leaders, and community volunteers.

Communities were informed of household survey schedules, LLIN distribution dates, beneficiary eligibility requirements, designated distribution sites, and key malaria prevention messages. Households were encouraged to retain survey receipts and registration records for verification during distribution. These awareness activities improved community participation, strengthened preparedness, and facilitated efficient implementation throughout the province.

Given Oro Province's diverse geography, community leaders, church representatives, health workers, and volunteers played a critical role in mobilising communities, particularly within remote coastal settlements, plantation communities, forest villages, and mountainous locations throughout Kokoda, Afore, Cape Nelson, and other hard-to-reach areas.

Distributions and Beneficiary Verification

Distribution sites were established at health facilities, ward centres, schools, churches, and village-level locations based on population size, accessibility, and local operating conditions. This decentralised approach improved access for remote communities and reduced travel requirements for beneficiaries.

Distribution activities were jointly coordinated by RAM, District Health Services, health facility staff, and community leaders. Community representatives assisted with beneficiary mobilisation, crowd management, beneficiary verification, and oversight of distribution activities.

A structured verification system ensured that LLINs were distributed only to eligible households identified during the household survey process. Beneficiaries were verified using household survey books, survey receipts, and approved household registers. Where survey receipts had been lost or household representatives were absent, eligibility was confirmed using household registers maintained by RAM and health facilities.

Special provisions were made for elderly persons, persons living with disabilities, pregnant women, and other vulnerable households to ensure equitable access while maintaining programme accountability and transparency.

LLIN Coding and Commodity Accountability

To strengthen commodity accountability and traceability, all LLINs distributed within Oro Province – ORO 2025 were labelled with a provincial identification code prior to distribution. Coding was undertaken under the supervision of RAM and District Health Services personnel and enabled tracking of LLIN stocks throughout the distribution process.

This system reduced the risk of diversion, duplication, resale and unauthorised movement of LLINs while supporting post-distribution monitoring and verification activities. A total of 143,135 LLINs were coded and distributed throughout Oro Province, including 66,456 LLINs distributed in Sohe District and 76,679 LLINs distributed in Ijivitari District.

Distribution in Remote Communities

The 2025 Oro Province LLIN Distribution Programme was largely successful in delivering Long-Lasting Insecticidal Nets (LLINs) to the majority of accessible health facility catchment areas across Sohe and Ijivitari Districts. However, 83 remote villages within the Safia, Emo, and Kira Health Centre catchments remain outstanding due to the exceptionally high cost of helicopter and fixed-wing aircraft charter services required to access these isolated communities. Rotarians Against Malaria (RAM), in collaboration with the Oro Provincial Health Authority (OPHA) and provincial leaders, is actively engaging with the Provincial Government, including the Governor's Office, to mobilise logistical and financial support. Subject to securing the necessary aviation support, these remaining communities will be covered during the next phase of LLIN operations.

Particular logistical attention was required for communities located within Kokoda Rural and Afore Rural Local Level Governments, where difficult terrain, limited road access, and extended travel times significantly increased operational complexity. Distribution teams frequently undertook long-distance travel and foot patrols to reach villages located beyond established road networks. Despite these efforts, several remote fly-off communities located within the Safia, Emo, and Kira Health Centre catchment areas could not be reached during the 2025 implementation period due to the exceptionally high cost of helicopter and fixed-wing aircraft

charter services required to access these isolated locations. These communities are located within rugged mountainous terrain characterised by dense rainforest, difficult landing conditions, limited transport infrastructure, and the absence of road access. Access to many villages requires aviation support followed by extensive trekking over several hours or days. RAM, in collaboration with the National Malaria Control Programme and Oro Provincial Health Authority, is actively pursuing additional funding and aviation support to facilitate these operations during a future implementation phase planned for 2026.

Logistics and Supply Chain Management

The programme followed established National Malaria Control Programme supply chain procedures, with LLINs transported from national storage facilities through provincial, district, health facility, and community distribution points. LLIN stocks were progressively pre-positioned at district warehouses, health centres, aid posts, and community distribution sites prior to implementation to ensure adequate stock availability and minimise operational delays.

Due to Oro Province's diverse geographical environment, transportation arrangements utilised a combination of road transport, four-wheel-drive vehicles, coastal vessels, boats, and foot patrols. Distribution teams worked closely with District Health Services, health facilities, Local Level Governments, and community leaders to ensure the safe and timely movement of LLINs throughout the province.

The successful implementation of the logistics and distribution system enabled LLINs to reach 280,983 people residing in 53,281 households across 779 villages, ensuring broad provincial coverage and strengthening malaria prevention efforts throughout Oro Province. The programme demonstrated the importance of coordinated logistics planning, strong community participation, and effective collaboration between OPHA, NMCP, RAM, District Health Services, health facilities, and village volunteers in delivering malaria prevention services across diverse and challenging operational environments.

Results and Analysis of LLIN Distributions in Oro Province

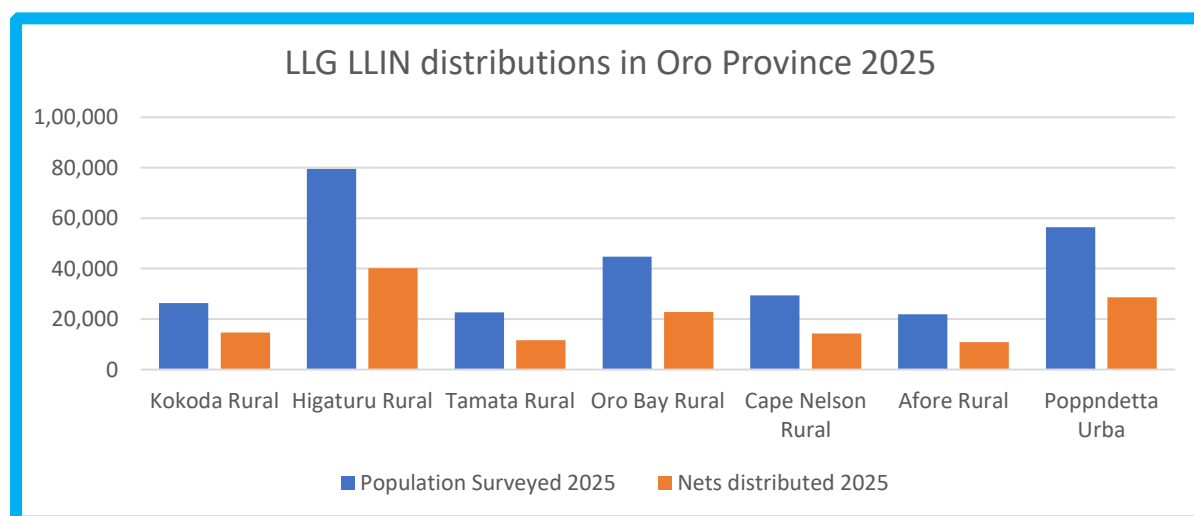


Figure 10 Graph LLIN distributions in Oro Province

The 2025 Oro Province Long-Lasting Insecticidal Net (LLIN) Family-Level Survey and Distribution Programme was implemented across Sohe and Ijivitari Districts. It was preceded by a comprehensive household survey and population verification exercise designed to establish accurate beneficiary numbers, allocation of LLINs based on verified household composition and sleeping arrangements.

The survey successfully recorded a total population of 280,983 people residing in 53,281 households across 779 villages throughout Oro Province. Based on the verified household survey results, a total of 143,135 LLINs were distributed, achieving an overall distribution rate of 50.9 LLINs per 100 people surveyed. This distribution ratio is consistent with National Malaria Control Programme (NMCP) allocation guidelines and demonstrates that the programme successfully achieved its objective of maintaining universal household access to LLINs throughout the province.

Clarification on Kira LLG Coverage

Kira LLG was not included in the 2025 LLIN household survey and distribution programme because the area forms part of the proposed remote fly-off operations scheduled for 2026. Due to its remoteness and the requirement for helicopter or fixed-wing aircraft access, Kira LLG was deferred and will be implemented together with other outstanding remote health facility catchment areas under the planned 2026 fly-off distribution programme.

Consequently, villages within Kira LLG, including Gobe, Upupure, Ovesaipu, Oivo, and other surrounding villages, are intentionally excluded from the 2025 village distribution list. These communities will be covered during the proposed 2026 remote area operations once the necessary aviation logistics and funding have been secured.

District-Level Results

<i>District</i>	<i>Population Surveyed 2025</i>	<i>House Holds Surveyed 2025</i>	<i>Nets distributed 2025</i>	<i>Nets Distributed Per 100 People</i>
<i>Sohe</i>	1,28,438	24,356	66,456	51.7
<i>Ijivitari</i>	1,52,545	28,925	76,679	50.3
<i>Totals</i>	2,80,983	53,281	1,43,135	50.9

Sohe District accounted for 128,438 people residing in 24,356 households across 389 villages, representing approximately 45.7 percent of the provincial population surveyed. A total of 66,456 LLINs were distributed throughout the district, resulting in a distribution rate of 51.7 LLINs per 100 people, equivalent to approximately one LLIN for every 1.93 persons. The district covered Kokoda Rural, Higaturu Rural, and Tamata Rural Local Level Governments and included a combination of plantation communities, lowland settlements, forest villages, and remote mountainous communities associated with the Kokoda region.

Ijivitari District recorded a surveyed population of 152,545 people residing in 28,925 households across 390 villages, accounting for approximately 54.3 percent of the provincial population

surveyed. A total of 76,679 LLINs were distributed, achieving a distribution rate of 50.3 LLINs per 100 people, equivalent to approximately one LLIN for every 1.99 persons. The district covered Oro Bay Rural, Cape Nelson Rural, Afore Rural, and Popondetta Urban Local Level Governments and included urban, peri-urban, coastal, plantation, and remote inland communities.

The consistency in LLIN distribution rates between the two districts demonstrates that allocation procedures were applied equitably throughout the province and that LLINs were distributed according to verified household needs rather than population estimates alone.

Local Level Government Analysis

At the Local Level Government (LLG) level, Higaturu Rural LLG recorded the largest surveyed population in Sohe District, with 79,491 people residing in 15,185 households. A total of 40,179 LLINs were distributed, achieving a distribution rate of 50.5 LLINs per 100 people.

Kokoda Rural LLG surveyed 26,321 people residing in 5,320 households and received 14,650 LLINs, achieving the highest distribution rate in the province at 55.7 LLINs per 100 people. The higher allocation reflects household composition and sleeping arrangements identified during the household survey.

Tamata Rural LLG recorded 22,626 people residing in 3,851 households and received 11,627 LLINs, resulting in a distribution rate of 51.4 LLINs per 100 people.

Within Ijivitari District, Popondetta Urban LLG recorded the largest population in the province, with 56,462 people residing in 10,499 households. A total of 28,591 LLINs were distributed, achieving a distribution rate of 50.6 LLINs per 100 people.

Oro Bay Rural LLG surveyed 44,719 people residing in 9,177 households and received 22,852 LLINs, achieving a distribution rate of 51.1 LLINs per 100 people.

Cape Nelson Rural LLG recorded 29,457 people residing in 5,435 households and received 14,311 LLINs, achieving a distribution rate of 48.6 LLINs per 100 people, the lowest distribution ratio among all LLGs but still within acceptable allocation parameters.

Afore Rural LLG surveyed 21,907 people residing in 3,814 households and received 10,925 LLINs, achieving a distribution rate of 49.9 LLINs per 100 people.

Kira LLG was not included in the 2025 LLIN household survey and distribution programme as it is part of the proposed 2026 remote fly-off operations. Consequently, villages including Gobe, Upupure, Ovesaipu, Oivo, and other Kira LLG communities are excluded from the 2025 village distribution list and will be covered during the 2026 fly-off programme.

Overall, LLIN distribution rates across the seven LLGs ranged from 48.6 to 55.7 LLINs per 100 people, demonstrating a high degree of consistency in the application of NMCP allocation guidelines throughout the province.

Population Analysis

Comparison with previous household survey data indicates that Oro Province's surveyed population increased from 274,303 people in 2022 to 280,983 people in 2025, representing an increase of 6,680 people or approximately 2.4 percent over the three-year period.

<i>LLG</i>	<i>Population Surveyed 2025</i>	<i>House Holds Surveyed 2025</i>	<i>Nets distributed 2025</i>
<i>Kokoda Rural</i>	26,321	5,320	14,650
<i>Higaturu Rural</i>	79,491	15,185	40,179
<i>Tamata Rural</i>	22,626	3,851	11,627
<i>Oro Bay Rural</i>	44,719	9,177	22,852
<i>Cape Nelson Rural</i>	29,457	5,435	14,311
<i>Afore Rural</i>	21,907	3,814	10,925
<i>Poppndetta Urba</i>	56,462	10,499	28,591
	2,80,983	53,281	1,43,135

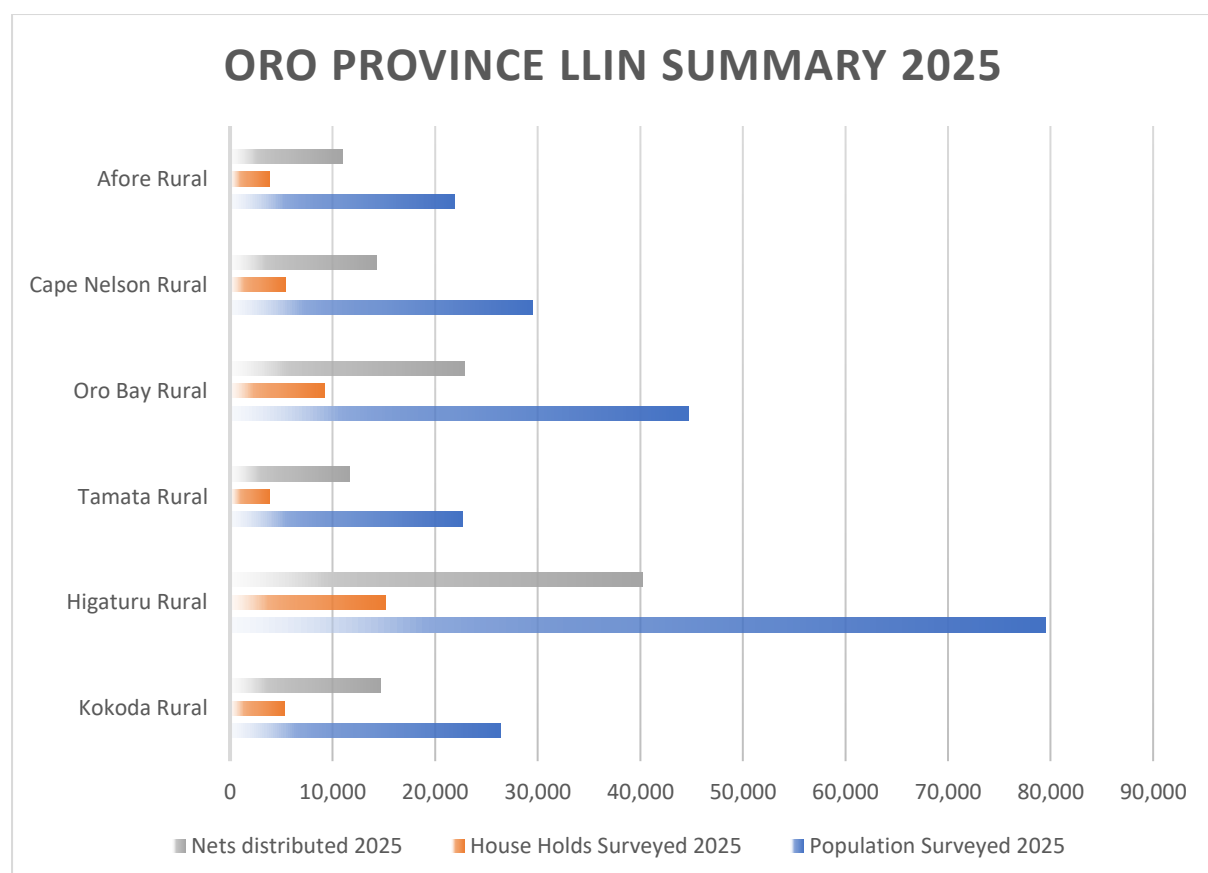


Figure 10 Graph - LLIN distributions in LLGs

Household Coverage Analysis

The programme distributed 143,135 LLINs to 53,281 households, resulting in an average allocation of approximately 2.69 LLINs per household throughout Oro Province. Sohe District recorded an average allocation of approximately 3 LLINs per household, while Ijivitari District recorded approximately 2 LLINs per household. The similarity in household allocation rates indicates consistent application of LLIN allocation guidelines across both districts.

Despite the successful completion of the programme, several remote fly-off communities within the Safia, Emo, and Kira Health Centre catchment areas could not be covered during the reporting period due to the exceptionally high cost of helicopter and fixed-wing aircraft charter services. Subject to the availability of alternate funding and aviation support, these communities will be incorporated into a future phase of LLIN operations planned for 2026.

Overall Programme Performance

Overall, the programme distributed 143,135 LLINs throughout Oro Province, achieving an overall distribution rate of 50.9 LLINs per 100 people surveyed, equivalent to approximately one LLIN for every 1.96 persons. The programme successfully reached the vast majority of targeted communities and demonstrated strong performance in household verification, beneficiary registration, stock management, and equitable LLIN allocation.

The findings demonstrate that the 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was successfully implemented, achieving high household coverage, effective beneficiary verification, and equitable LLIN distribution throughout the province. The combination of household-level population verification, Survey books data collection, community participation, strong logistical coordination, and effective collaboration between OPHA, NMCP, RAM, health facilities, and village volunteers enabled the programme to reach both accessible and remote populations. The successful distribution of 143,135 LLINs across 779 villages provides a strong foundation for malaria prevention and is expected to contribute significantly to reducing malaria transmission and protecting vulnerable populations throughout Oro Province.

Nets Donated to Health Facilities

Table 4: LLIN Donations by Health Facility

District	LLG	Health Facility	LLINs Donated
Sohe	Higaturu Rural	Sangara Health Centre	18
Sohe	Tamata Rural	Manau Health Centre	49
Ijivitari	Cape Nelson Rural	Wanigela Health Centre	50

District	LLG	Health Facility	LLINs Donated
Ijivitari	Cape Nelson Rural	Tufi Health Centre	50
Ijivitari	Popondetta Urban	Popondetta Urban Clinic	44
Total			211

Following completion of household distribution activities, 211 residual Long-Lasting Insecticidal Nets (LLINs) that were surplus to household requirements or unsuitable for redistribution within the household distribution programme were donated to selected health facilities throughout Oro Province to support ongoing malaria prevention activities. These LLINs were allocated for use by pregnant women attending antenatal clinics, hospital patients, vulnerable households, emergency replacement requirements, outreach activities, and routine malaria prevention initiatives within health facility catchment areas.

The largest allocations were made to Wanigela Health Centre and Tufi Health Centre in Cape Nelson Rural LLG, each receiving 50 LLINs, followed by Manau Health Centre in Tamata Rural LLG, which received 49 LLINs, and Popondetta Urban Clinic, which received 44 LLINs. An additional 18 LLINs were donated to Sangara Health Centre in Higaturu Rural LLG to support ongoing malaria prevention services within the catchment population.

The donation of these LLINs ensured that all remaining stocks continued to support malaria prevention efforts and remained available for populations most vulnerable to malaria infection, including pregnant women, children under five years of age, patients admitted to health facilities, and households requiring emergency net replacement. This approach maximised the utilisation of available LLIN stocks while strengthening the capacity of health facilities to provide ongoing malaria prevention services throughout Oro Province.

The allocation of residual LLINs to health facilities further demonstrates the programme's commitment to accountability, efficient stock management, and the continued protection of vulnerable populations against malaria transmission beyond the completion of the household distribution campaign.

Budget Performance Analysis-

Table 5

Oro Province LLIN OPS 2025			
Expense Types	Budget	Actual	Variance
Training	11,780	9,360	2,420
Human Resources	1,35,860	1,36,808	-948
Fuel	61,520	82,832	-21,312

<i>Vehicle Hire</i>	1,76,400	1,95,649	-19,249
<i>Boat Hire</i>	56,700	47,160	9,540
<i>Aircraft Hire</i>	24,000	-	24,000
<i>Stationary</i>	3,000	1,445	1,555
<i>5% Contingency</i>	23,463	14,234	9,229
<i>Totals</i>			
<i>PGK</i>	4,92,723	K4,87,488	K5,235

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was implemented with an approved operational budget of PGK 492,723. Total actual expenditure amounted to PGK 487,488, resulting in an overall saving of PGK 5,235 and a budget utilisation rate of 98.9 percent. The programme therefore achieved its operational objectives while remaining within the approved budget allocation, demonstrating strong financial management and effective utilisation of resources. However, the air craft budget of K24,000 unutilised, as the fly off distributions are put on hold.

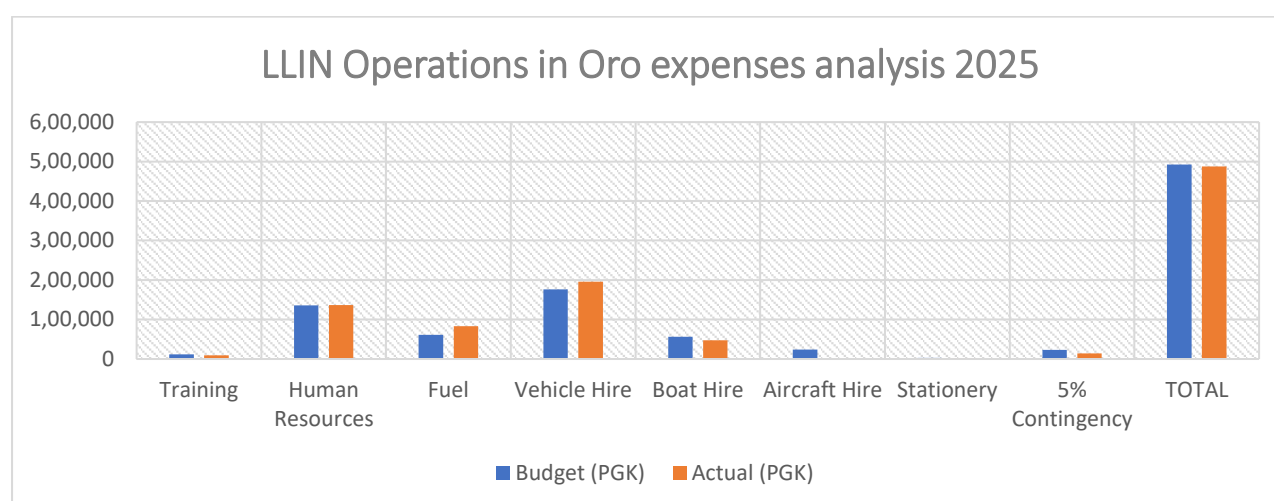


Figure 11 Graph showing budget vs actuals analysis

Human Resources

Human resource expenditure was budgeted at PGK 135,860, while actual expenditure reached PGK 136,808, representing a minor overspend of PGK 948. The slight increase was primarily attributable to additional field supervision requirements, extended deployment of survey and distribution teams in remote communities, and additional support provided by health workers and community volunteers during implementation. Despite the marginal variance, expenditure remained largely in line with the approved budget.

Fuel

Fuel recorded the largest operational variance during the programme. Actual expenditure totalled PGK 82,832 against a budget allocation of PGK 61,520, resulting in an overspend of PGK 21,312

(135%). To minimise fuel costs, RAM procured bulk petrol (Zoom) from Niugini Oil Company in Lae at a negotiated price of PGK 4.12 per litre, and transported it to Oro Province together with the LLIN bales in shipping containers. However, due to limited container space, only 30 drums of petrol could be shipped, compared to the 43 drums originally budgeted for the operation. The remaining 13 drums had to be purchased locally in Popondetta at a substantially higher price of PGK 5.52 per litre.

Diesel requirements were procured through existing drawdown arrangements in Lae to obtain more competitive pricing, as bulk fuel suppliers were not available in Oro Province. Despite these cost-saving measures, fuel prices remained significantly higher than the original budget assumptions of PGK 3.80 per litre for petrol (Zoom) and PGK 3.50 per litre for diesel. The combination of increased market fuel prices and the need to procure part of the petrol requirement locally contributed to the overall increase in fuel expenditure.

The experience highlights the importance of securing sufficient container space for bulk fuel transportation during future LLIN campaigns, as transporting larger quantities of fuel from Lae would significantly reduce operational fuel costs in remote provincial operations.

Vehicle Hire

Vehicle hire expenditure totalled PGK 195,649 against a budget allocation of PGK 176,400, resulting in an overspend of PGK 19,249. Although the programme utilised only 11 vehicles compared to the 14 vehicles originally budgeted, daily vehicle hire rates increased substantially during implementation. Budget estimates were based on vehicle hire costs of approximately PGK 600 per day, whereas actual rates ranged between PGK 650 and PGK 800 per day due to increased transport demand, fuel costs, and vehicle availability constraints. The higher daily rental rates offset savings generated through the reduced number of vehicles utilised.

Boat Hire

Boat hire expenditure amounted to PGK 47,160 compared to a budget allocation of PGK 56,700, resulting in savings of PGK 9,540 (83%). The savings were achieved through efficient route planning, favourable weather conditions during implementation, and greater utilisation of road transport networks than initially anticipated. Close coordination with local communities and health facilities also reduced the number of boat movements required throughout the programme.

Aircraft Hire

A budget allocation of PGK 24,000 was reserved for aircraft hire; however, no aircraft operations were undertaken during the reporting period, resulting in a saving of PGK 24,000 (100%). The planned aviation-supported operations for the remote Safia, Emo, and Kira Health Centre catchments were postponed due to the high cost of helicopter and fixed-wing aircraft charter services and limited availability of operational funding. These activities are planned for implementation during a future operational phase subject to the availability of additional resources and aviation support.

Training

Training expenditure totalled PGK 9,360 against a budget allocation of PGK 11,780, resulting in savings of PGK 2,420 (79%). Savings were achieved through efficient utilisation of existing health facility training venues, integration of multiple training activities into single workshops, and effective use of RAM and District Health Services personnel to facilitate training activities.

Stationery and Office Supplies

Stationery expenditure amounted to PGK 1,445 against a budget allocation of PGK 3,000, resulting in savings of PGK 1,555 (48%). The lower expenditure reflects the extensive use of Survey books data collection systems, which significantly reduced the need for printed forms, survey materials, and paper-based reporting requirements.

Contingency

The programme utilised PGK 14,234 from the contingency budget allocation of PGK 23,463, resulting in savings of PGK 9,229 (61%). The lower utilisation reflects effective operational planning, strong logistical coordination, and the absence of major unforeseen operational disruptions during implementation.

Overall Financial Performance

Overall, the Oro Province LLIN Family-Level Survey and Distribution Programme demonstrated strong financial performance and effective budget management. While fuel and vehicle hire costs exceeded original estimates due primarily to increased fuel prices and higher transport costs, these overruns were fully offset by savings achieved in boat hire, training, stationery, and contingency expenditures. The programme successfully surveyed 280,983 people, registered 53,281 households, distributed 143,135 LLINs, and achieved an overall budget utilisation rate of 99 percent, while remaining within the approved operational budget. The results demonstrate effective stewardship of Global Fund resources and the successful delivery of malaria prevention services throughout Oro Province despite challenging operational conditions and rising transportation costs.

Outstanding Fly-Off Operations and Impact on Budget Performance

Although the 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was completed within the approved budget, several remote fly-off communities located within the Safia, Emo, and Kira Health Centre catchment areas remain outstanding and will be covered during a subsequent phase of operations in 2026. These areas comprise 83 villages with an estimated population of 9,966 people, requiring approximately 4,950 LLINs to achieve full coverage. The communities are located within rugged mountainous terrain and dense rainforest environments where access is only possible through helicopter or fixed-wing aircraft support followed by extensive trekking. Due to the exceptionally high cost of aviation services, limited aircraft availability, and funding constraints, the planned aviation-supported operations were deferred. Once additional funding and aviation support are secured, these fly-off operations will

be implemented in 2026 and are expected to increase overall operational costs due to aircraft charter requirements, fuel logistics, personnel deployment, and extended field operations necessary to reach these isolated communities.

Communication Infrastructure Analysis

Table6: Communication Infrastructure Survey Results – Oro Province, 2025

District	Villages	Households Surveyed	Digicel Coverage	Bmobile Coverage	Households with Phones	Households with Radios	Villages with Radio Networks
Sohe	389	24,356	293	5	4,811	2,443	339
Ijivitari	390	28,925	306	67	6,291	2,044	356
Total	779	53,281	599	72	11,102	4,487	695

The 2025 Oro Province LLIN Family-Level Survey collected communication infrastructure information from 779 villages and 53,281 households across Sohe and Ijivitari Districts. The survey identified 599 villages with Digicel coverage and 72 villages with Bmobile coverage, confirming that Digicel remains the dominant telecommunications provider throughout the province.

A total of 11,102 households reported owning mobile phones, while 4,487 households owned radios. In addition, 695 villages reported access to radio communication networks, highlighting the continued importance of radio communication, particularly in remote and isolated communities where mobile network coverage remains limited or unreliable.

Ijivitari District recorded higher mobile phone ownership (6,291 households) compared to Sohe District (4,811 households). However, communication access remains relatively low compared to the total number of households surveyed, indicating that traditional communication channels such as village leaders, churches, schools, health facilities, and community volunteers continue to play a critical role in disseminating public health information.

The findings demonstrate that both mobile phones and radio networks provide valuable opportunities for strengthening malaria prevention messaging, promoting consistent LLIN use, supporting future distribution campaigns, and improving community engagement. Future health communication strategies should utilise a combination of mobile messaging, radio broadcasts, health facilities, community volunteers, and local leadership structures to maximise outreach and improve malaria prevention outcomes throughout Oro Province.

Challenges Encountered During Implementation

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme was implemented across the geographically diverse districts of Sohe and Ijivitari, covering coastal communities, riverine settlements, plantation areas, urban centres, mountainous villages, and remote

rainforest communities. Although the programme successfully surveyed 280,983 people in 779 villages and distributed 143,135 LLINs, several operational challenges affected implementation timelines, logistics, and operational efficiency.

Geographic Access and Transportation

The greatest operational challenge was reaching remote communities spread across the health centre catchments of Kokoda, Saiho, Sangara, Afore, Itokama, Sakarina, Ako, Ambasi, Manau, Tufi, Wanigela, Oro Bay, Safia, Emo, and Kira. Many villages were accessible only after several hours or days of trekking, river travel, or sea transport.

Within the Saiho Health Centre catchment, prolonged heavy rainfall severely damaged roads serving Barevoturu, Sasembata, Kendata, Kiorota, and surrounding communities near Mt. Lamington, delaying both household surveys and LLIN distributions. Similar road deterioration affected operations around Afore, Itokama, Sakarina, Ambasi, and Manau, where washed-out river crossings and poor road conditions increased travel times, fuel consumption, and vehicle maintenance costs.

At Wanigela and Tufi, strong winds and rough sea conditions delayed dinghy transport to island communities, while villages located along the Musa River within the Ako Health Centre catchment became difficult to access because of flooding and continuous rainfall.

Remote Fly-Off Communities

The most significant logistical challenge involved the remote fly-off health centre catchments of Safia, Emo, and Kira. These isolated mountainous communities can only be accessed by helicopter or fixed-wing aircraft followed by extended trekking.

Due to the exceptionally high cost of aviation services and limited operational funding, these areas could not be included during the 2025 implementation period. Consequently, Kira LLG, including villages such as Gobe, Upupure, Ovesaipu, Oivo, and other surrounding communities, was excluded from the 2025 survey and distribution programme. Together with the Safia and Emo catchments, these locations comprising approximately 83 villages with an estimated 9,966 people requiring approximately 4,950 LLINs are scheduled for the proposed 2026 remote fly-off operations.

Weather and Environmental Challenges

Persistent rainfall throughout much of the implementation period affected almost every health centre catchment. Heavy rain caused flooding, landslides, road washouts, and river erosion, particularly around Kokoda, Saiho, Afore, Ako, Ambasi, Manau, and Sakarina, while rough seas delayed boat movements to Wanigela, Tufi, and surrounding island communities.

These weather conditions frequently required distribution schedules to be revised and significantly increased transportation costs and travel times.

Telecommunications and Data Collection

Limited mobile network coverage remained a major challenge across remote areas, particularly within the Kokoda, Ambasi, Ako, Wanigela, and mountainous catchments. Poor connectivity delayed communication between RAM field officers, District Health Teams, and provincial supervisors, affecting the timely submission of survey data and operational reporting.

In several trekking locations, RAM officers had to wait for volunteers to return from remote villages with completed household survey books before LLIN allocations could be finalised.

Security and Community Challenges

Security incidents also affected programme implementation. During operations around the Oro Bay catchment, RAM personnel experienced an attempted robbery and maintained heightened security precautions throughout the programme. Several health facility catchments also experienced petty crime risks, requiring staff to remain vigilant during field activities.

Localised tribal fighting and ethnic clashes disrupted operations within the Saiho and Tufi catchments and temporarily prevented access to several villages. In addition, tribal conflicts and killings along the Popondetta–Kokoda Highway resulted in roadblocks that delayed survey and distribution teams for several days until security conditions improved.

Logistics and Operational Challenges

Transport and logistics presented continuous challenges throughout the programme. Vehicle hire rates in Oro Province were substantially higher than the rates budgeted by RAM, delaying vehicle mobilisation in several operational areas. Accommodation shortages in Popondetta during provincial events also increased operational costs.

The larger size and weight of LLIN bales required additional vehicle and dinghy trips, particularly in Wanigela, Tufi, Oro Bay, and other coastal catchments, increasing fuel consumption and transport costs. Fuel supply disruptions at local service stations also delayed field movements, requiring staff to source empty fuel drums and make alternative refuelling arrangements.

Overall, despite these considerable geographical, logistical, weather-related, and security challenges, the programme successfully achieved high household coverage across accessible areas of Oro Province while establishing a clear operational plan to complete the outstanding Safia, Emo, and Kira fly-off communities during the proposed 2026 remote area operations.

Lessons Learned

The 2025 Oro Province LLIN Family-Level Survey and Distribution Programme reinforced the importance of adopting flexible implementation strategies that can be adapted to the province's diverse geographical, logistical, and operational conditions.

A key lesson from the programme was the importance of completing transport and logistics planning before field teams arrive in the province. Delays in securing hired vehicles during the early stages of implementation resulted in approximately two weeks of lost operational time, affecting the timely deployment of LLIN teams to health facility catchments. Future LLIN campaigns would benefit from closer coordination between RAM and the Oro Provincial Health Authority to identify, negotiate, and secure vehicle hire arrangements well in advance of programme commencement. Early confirmation of transport providers, together with pre-positioning of vehicles and drivers, would improve implementation efficiency, reduce operational delays, and minimise programme costs.

The programme also highlighted the importance of securing aviation support and funding early in the planning process for remote fly-off operations. Strong collaboration with the Oro Provincial Government, Oro Provincial Health Authority, District Health Services, local leaders,

churches, and village volunteers was essential for resolving operational challenges, mobilising communities, and supporting implementation. Strengthening these partnerships will be critical for completing the outstanding Safia, Emo, and Kira Health Centre catchments during the next phase of operations.

Most importantly, the successful completion of household surveys and LLIN distributions across 779 villages demonstrated the commitment, resilience, and adaptability of RAM staff, health workers, volunteers, and partner organisations. The experience gained during the 2025 programme provides a strong operational foundation for completing the remaining remote fly-off communities in 2026 and for strengthening future LLIN distribution campaigns throughout Oro Province.

Acknowledgements

On behalf of Rotarians Against Malaria (RAM) and the LLIN Household Distribution Team who worked throughout Ijivitari and Sohe Districts, we would like to sincerely acknowledge and thank the National Malaria Control Program (NMCP), Oro Provincial Health Authority (OPHA) and the District Health Services for their outstanding support, cooperation, and commitment during the implementation of the 2025 Oro Province Long-Lasting Insecticidal Net (LLIN) Family-Level Survey and Distribution Programme.

At the provincial level, we extend our sincere appreciation to Dr Titus Stanley Mokuta, Chief Executive Officer, and his leadership team for their continued guidance and support throughout the programme. We would also like to express our special thanks to Mr Champion Sagiribo (Director Public Health), Ms Grace Rahua (Provincial Disease Control Officer), Mr Henry Safoe (Former Provincial Malaria Supervisor), and Mr Mou Basa (Former HMM Officer) for their technical guidance, coordination, and invaluable assistance during the planning and implementation phases of the programme.

We would also like to acknowledge the dedication and commitment of the District Health Services staff, health facility managers, and health workers who provided local leadership, operational support, and technical expertise throughout the programme.

Ijivitari District

Special recognition is extended to:

- Mr James Yangano – District Health Manager, Ijivitari District
- Mr Jeff Ubin – Officer in Charge, Oro Bay Health Centre
- Ms Daisy Hovuga – Community Health Worker, Gona Health Centre
- Mr George Dauwa – Officer in Charge, Ambasi Health Centre
- Mr Martin Kindada – Officer in Charge, Wanigela Health Centre
- Ms Margaret Hite – Officer in Charge, Tufi Health Centre

- Mr Jim Konemba – Officer in Charge, Ako Health Centre
- Mr Alphaeus Uiari – Officer in Charge, Afore Health Centre
- Mr Gideon Bariana – Officer in Charge, Sakarina Health Centre
- Mr Lester Dona – Officer in Charge, Itokama Health Centre

Sohe District

Special recognition is extended to:

- Mr Kendall Wasiripa – District Health Manager, Sohe District
- Ms Florence Tubari – Officer in Charge, Kokoda Health Centre
- Mr Guy Nelson – Community Health Worker, Kokoda Health Centre
- Mr Harold Korina – Officer in Charge, Saiho Health Centre
- Mr Philip Taihima – Officer in Charge, Barevoturu Aid Post
- Ms Rogeal Bambi – Officer in Charge, Sangara Health Centre

Rotarians Against Malaria would also like to acknowledge the invaluable logistical support provided by Bismarck Maritime Limited for transporting thirteen shipping containers from Lae to Oro Province. The support provided ensured the timely movement and secure storage of LLIN stocks and operational supplies at the Oro Provincial Health Authority yard, significantly contributing to the successful implementation of the programme.

We further extend our appreciation to No.1 Hire Cars, Islands Mobile Hire Cars, local vehicle owners, dinghy operators, and transport providers who supported field operations throughout the province. Their commitment and flexibility enabled survey and distribution teams to reach many remote and difficult-to-access communities. Special thanks are also extended to Y&C Enterprise for the reliable supply of bulk fuel throughout the operation.

RAM would also like to sincerely thank the Anglican Church Health Services, other church-run health facilities, and all government-operated health facilities that generously released staff to support programme activities. Their collaboration and willingness to work alongside RAM teams were critical to the success of the household survey and LLIN distribution programme.

Finally, and most importantly, we extend our deepest gratitude to the hundreds of village volunteers, ward councillors, community leaders, church leaders, local trekkers, and community members who worked tirelessly to ensure that every household was surveyed and that LLINs reached eligible families throughout Oro Province. Their local knowledge, commitment, and dedication were instrumental in the successful completion of the programme.

The success of the 2025 Oro Province LLIN Family-Level Survey and Distribution Programme reflects the strength of partnerships between communities, health workers, government agencies, churches, development partners, and volunteers. Rotarians Against Malaria sincerely thanks everyone who contributed their time, expertise, and support towards protecting the people of Oro Province from malaria and strengthening the province's malaria prevention efforts.

RAM sincerely acknowledges the valuable contribution of Mr Mou Basa, former Home-Based Malaria Management (HMM) Officer, for coordinating the deployment of Community Malaria Volunteers (CMVs) to support the LLIN programme across Kokoda, Saiho, Oro Bay, Gona, Wanigela, Tufi, and Ako Health Centre catchments in Oro Province. The CMVs played a vital role in supporting RAM LLIN officers with community mobilisation, household surveys, beneficiary registration, and LLIN distribution activities. Their established relationships within the communities also strengthened community participation and are expected to continue supporting post-distribution monitoring, particularly by promoting correct and consistent LLIN use among households.

Rotarians Against Malaria and Provincial Implementation Team

Rotarians Against Malaria would like to extend special recognition and appreciation to the RAM field officers, Provincial Health Authority staff, and implementation personnel whose dedication, commitment, and hard work were instrumental in the successful completion of the 2025 Oro Province LLIN Family-Level Survey and Distribution Programme.

<i>Officer</i>	<i>LLINs Managed</i>	<i>Arrival in Province</i>		<i>Arrival at Health Centre</i>		<i>Left Health Centre</i>		<i>Operations Completed</i>	<i>Operational Days</i>	<i>Total Days in Field</i>
<i>Peter Dama</i>	14,650	11	Aug 2025	15	Aug 2025	30	Aug 2025	31 Aug 2025	15	20
<i>Peter Dama (Kokoda Deployment)</i>	–	2	Oct 2025	3	Oct 2025	17	Oct 2025	19 Oct 2025	14	17
<i>Job Kemi</i>	20,650	11	Aug 2025	15	Aug 2025	30	Sep 2025	30 Sep 2025	46	50
<i>Job Kemi (Additional Deployment)</i>	5,267	30	Sep 2025	1	Oct 2025	18	Oct 2025	23 Oct 2025	17	23
<i>Kila Tom</i>	19,547	11	Aug 2025	15	Aug 2025	30	Sep 2025	5 Oct 2025	46	55
<i>Kila Tom (Additional Deployment)</i>	3,653	5	Oct 2025	5	Oct 2025	14	Oct 2025	15 Oct 2025	9	10

<i>Greg Yaku</i>	4,609	11 2025	Aug	15 2025	Aug	28 2025	Sep	1 Oct 2025	44	51
<i>Greg Yaku (Additional Deployment)</i>	3,143	1 2025	Oct	1 2025	Oct	10 2025	Oct	15 Oct 2025	9	14
<i>Bernard (OPHA)</i>	1,800	27 2025	Sep	27 2025	Sep	1 2025	Oct	2 Oct 2025	4	5
<i>Anthony</i>	16,125	11 2025	Aug	11 2025	Aug	26 2025	Sep	27 Sep 2025	46	47
<i>Anthony (Additional Deployment)</i>	10,925	27 2025	Sep	27 2025	Sep	25 2025	Oct	25 Oct 2025	28	28
<i>Ali Jordan</i>	4,250	11 2025	Aug	11 2025	Aug	12 2025	Sep	13 Sep 2025	32	33
<i>David Nul</i>	5,642	22 2025	Sep	26 2025	Sep	13 2025	Oct	14 Oct 2025	17	22
<i>Nixon</i>	4,450	26 2025	Sep	29 2025	Sep	17 2025	Oct	18 Oct 2025	18	22
<i>Joyce</i>	28,635	11 2025	Aug	11 2025	Aug	18 2025	Sep	19 Sep 2025	38	39
<i>Mr Oa Marai – Provincial Team Leader (Administration & Logistics)</i>	Provincial Coordination	11 2025	Aug	–		–		19 Sep 2025	–	39

These officers worked tirelessly throughout the planning, household survey, logistics coordination, supervision, monitoring, data management, and LLIN distribution phases of the programme. Their professionalism, commitment, and willingness to operate in challenging field environments significantly contributed to the successful distributions of LLINs villages throughout Oro Province.

ORO PROVINCE LLINs DISTRIBUTION IN PICTURES 2025

Meeting the Provincial Heads

Meeting with PHA:

Microplanning

Microplanning at:

Anthony Pidian – Afore HC, Itokama HC & Sakarina HC



Job Kemi – Sangara HC



Kila Tom – Tufi HC



Training & Survey

Survey Volunteer Training at:

Anthony Pidian – Oro Bay HC



Anthony Pidian – Afore HC, Itokama HC & Sakarina HC



Greg Yaku - Ambasi HC



Job Kemi – Manau HC



Kila Tom – Saiho HC (Higaturu LLG)



Kila Tom – Tufi HC



Verification

Survey Verification:

Distribution

Distribution of LLINS:

Anthony Pidian – Afore HC, Itokama HC & Sakarina HC



David Nul – Wanigela HC



Job Kemi – Manau HC



Job Kemi – Sangara HC



Kila Tom – Tufi HC



Peter Dama – Kokoda HC



Transportation & Storage

Transportation & Storage of LLINS:

Greg Yaku – Ambasi HC



Greg Yaku – Saiho HC (Tamata LLG)



Job Kemi – Manau HC



Kila Tom – Saiho HC (Higaturu LLG)



Oa Marai – Oro Operations



Happy Faces

Happy Recipients of LLINS:

Greg Yaku – Ambasi HC



Greg Yaku – Saiho HC (Tamata LLG)



Job Kemi – Manau HC



Donation

Donation of LLINS:

ANNEXURE 2
Rotarians Against Malaria
Oro Province: Sohe Distict
LLIN Distribution Summary Sheet

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
SOHE DISTRICT			1,40,909	1,40,909				1,28,438	24,356	67,138	66,456		389	293	5	4,811	2,443	339	
Kokoda Rural			34,053	31,972				26,321	5,320	14,637	14,650		100	100	0	1,587	2	102	
1	Asimba		1,082	1,006				950	138	507	507		5	5	0	0	0		
	1	Asimba	197	152	Kokoda HC	Yes	19.08.25	134	19	70	70	11.10.25	1	1				93.7 FM	
	2	Kanga	349	568	Kokoda HC	Yes	19.08.25	513	73	275	275	11.10.26	1	1				93.7 FM	
	3	Karukaru	128	153	Kokoda HC	Yes	19.08.25	130	24	71	71	11.10.27	1	1				93.7 FM	
	4	Korogo	117	33	Kokoda HC	Yes	19.08.25	48	8	26	26	11.10.28	1	1				93.7 FM	
	5	Sungeina	292	100	Kokoda HC	Yes	19.08.25	125	14	65	65	11.10.29	1	1				93.7 FM	
2	Kovelo		1,370	2,277				2109	349	1135	1135		12	12	0	106	0		
	1	Kovelo	303	389	Kokoda HC	Yes	19-20.08.25	430	68	229	229	13.10.25	1	1		27		93.7 FM	Mop-up 2HH. 5 nets fpr 12 population
	2	Koiasi	102	125	Kokoda HC	Yes	22.08.25	75	14	43	43	15.10.25	1	1		4		93.7 FM	
	3	Ebea	229	392	Kokoda HC	Yes	19.08.25	312	50	165	165	11.10.25	1	1		34		93.7 FM	
	4	Savaia	245	139	Kokoda HC	Yes	19.08.26	183	29	98	98	15.10.25	1	1		2		93.7 FM	
	5	Kovelo 2	100	91	Kokoda HC	Yes	20.08.25	81	11	44	44	13.10.25	1	1		3		93.7 FM	
	6	Savaia Sttlmnt	35	288	Kokoda HC	Yes	20.08.25	139	27	75	75	14.10.25	1	1				93.7 FM	
	7	Yoda	74	154	Kokoda HC	Yes	21.08.25	121	15	65	65	11.10.25	1	1		8		NBC	
	8	Koma	41	491	Kokoda HC	Yes	23 - 24.08.25	432	68	233	233	14 - 15.10.25	1	1		18		93.7 FM	
	9	Muduiui	113	67	Kokoda HC	Yes	19.08.25	60	11	33	33	13.10.25	1	1		5		93.7 FM	
	10	Soa	30	34	Kokoda HC	No	20.08.25	32	8	17	17	13.10.25	1	1		2		93.7 FM	
	11	Foka	100	0	Kokoda HC	Yes	20.08.25	120	22	63	63	13.10.25	1	1				93.7 FM	
		Horona		106	Kokoda HC	Yes	25.08.25	124	26	70	70	15.10.25	1	1		3		93.7 FM	
3	Saga		1,829	2,357				1716	377	937	937		7	7	0	240	0		
	1	Amada	286	438	Kokoda HC	Yes	20.08.25	350	49	184	184	14.10.25	1	1		18		93.7 FM	
	2	Fala	216	164	Kokoda HC	No	21.08.25	115	24	64	64	12.10.25	1	1		4		93.7 FM	
	3	Botue	608	691	Kokoda HC	Yes	20.08.25	539	150	295	295	11.10.25	1	1		126		93.7 FM	
	4	Saga	169	245	Kokoda HC	Yes	19.08.25	210	50	123	123	10.10.25	1	1		11		93.7 FM	
	5	Kokoda Vllge	351	290	Kokoda HC	Yes	19.08.26	54	9	29	29	11.10.25	1	1				93.7 FM	
	6	Botue Sttlment	199	197	Kokoda HC	Yes	19.08.25	157	45	86	86	12.10.25	1	1		45		93.7 FM	
		Manua/Kendasogu		332	Kokoda HC	Yes	08.08.25	291	50	156	156	09.10.25	1	1		36		93.7 FM	
4	Ioro Lss Blocks		1,093	1,190				1279	254	705	705		3	3	0	69	0		
	1	Kokoda Pltn Portion	253	220	Kokoda HC	Yes	19.08.25	272	47	147	147	10.10.25	1	1	0	33		93.7 FM	
	2	Kokoda Blck	381	419	Kokoda HC	Yes	19-21.08.25	421	98	236	236	10.10.25	1	1	0	36		93.7 FM	
	3	Iora Blcks	459	551	Kokoda HC	Yes	19-20.08.25	586	109	322	322	11.10.25	1	1	0			93.7 FM	Mop-up. 9 HH. 22 nets for 37 population
5	Kebara		2,946	2,709				2552	438	1400	1400		7	7	0	100	0		
	1	Kamondo	292	518	Kokoda HC	Yes	19.08.25	502	87	280	280	09.10.25	1	1	0	20		93.7 FM	
	2	Kanandara	357	233	Kokoda HC	Yes	22.08.25	185	29	102	102	10.10.25	1	1	0	7		93.7 FM	
	3	Kapara	375	286	Kokoda HC		20.08.25	428	72	242	242	10.10.25	1	1	0			93.7 FM	Mop-up. 22 HH. 72 nets for 118 population
	4	Perive	706	548	Kokoda HC	Yes	20.08.25	420	72	230	230	09.10.25	1	1	0	19		93.7 FM	
	5	Sengi	797	593	Kokoda HC	Yes	19.08.25	540	100	290	290	09.10.25	1	1	0	28	-	93.7 FM	
	6	Manekari	318	365	Kokoda HC	Yes	19.08.25	291	49	157	157	09.10.25	1	1	0	19		NBC NORTHERN	
	7	Kaumo	102	166	Kokoda HC	Yes	19.08.25	186	29	99	99	09.10.25	1	1	0	7		93.7 FM	
6	Abuari		507	501				466	95	258	258		4	4	0	0	0		
	1	Abuari	115	153	Kokoda HC	Yes	19.08.25	137	28	75	75	15.10.25	1	1	0			93.7 FM	
	2	Hagutava	76	60	Kokoda HC	Yes	19.08.25	58	14	33	33	15.10.25	1	1	0			93.7 FM	
	3	Kyile	69	82	Kokoda HC	Yes	19.08.25	83	18	46	46	15.10.25	1	1	0			93.7 FM	
	4	Pelai	247	206	Kokoda HC	Yes	19.08.25	188	35	104	104	15.10.25	1	1	0			93.7 FM	
7	Alola		216	266				234	40	130	130		2	2	0	0	0		
	1	Alola	119	106	Kokoda HC	Yes	19.08.25	149	24	82	82	14.10.25	1	1	0			93.7 FM	
	2	Isurava	97	160	Kokoda HC	Yes	19.08.25	85	16	48	48	14.10.25	1	1	0			93.7 FM	
8	Waju		2,137	2,466				2220	457	1233	1232		6	6	0	213	2		
	1	Havaki	203	347	Kokoda HC	No	18.08.25	252	49	137	137	15.10.25	1	1	0	40	2	93.7 FM	
	2	Sirireta	546	551	Kokoda HC	No	19.08.25	337	99	201	201	14.10.25	1	1	0	55		93.7 FM	
	3	Waju	567	682	Kokoda HC	Yes	19 - 20.08.25	705	141	389	388	06 - 08.10.25	1	1	0	39		NBC NORTHERN	Mop-up. 4 HH. 7 nets for 14 population
	4	Hovea	370	264	Kokoda HC	Yes	18.08.25	247	50	134	134	15.10.25	1	1	0	34		93.7 FM	
	5	Gorari	58	292	Kokoda HC	Yes	18.08.25	374	68	208	208	07.10.25	1	1	0	15		NBC NORTHERN	Moop-up. 18 HH. 51 nets for 89 population
	6	Wasara	392	330	Kokoda HC	Yes	18.08.25	305	50	164	164	10.10.25	1	1	0	30		93.7 FM	
9	Hanjiri		866	956				804	181	458	458		4	4	0	87	0		
	1	Hanjiri	530	499	Kokoda HC	Yes	19.08.25	441	94	250	250	06.10.25	1	1	0	57		93.7 FM	
	2	Maju	113	179	Kokoda HC	Yes	19.08.25	107	28	64	64	06.10.25	1	1	0	9	-	93.7 FM	
	3	Ingi	149	169	Kokoda HC	Yes	18.08.25	171	40	95	95	06.10.25	1	1	0	17	-	93.7 FM	
	4	Ifafu	74	110	Kokoda HC	Yes	19.08.25	85	19	49	49	05.10.25	1	1	0	4	-	93.7 FM	
10	Ambene		961	878				680	129	360	374		1	1	0	45	0		
	1	Ambene	961	878	Kokoda HC	Yes	18 - 19.08.25	680	129	360	374	06-07.10.25	1	1	0	45	-	90.7 FM	
11	Ilimo		2,132	1,867				1731	337	988	988		3	3	0	118	0		

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
	1	Hojavahambo	572	419	Kokoda HC	Yes	18.08.25	400	74	252	252	05.10.25	1	1	0	9	-	90.7 FM	
	2	Ilimo	654	639	Kokoda HC	Yes	18 - 21.08.25	609	113	333	333	06.10.25	1	1	0	33	-	93.7 FM	
	3	Papaki	907	809	Kokoda HC	Yes	18 -- 19.08.25	722	150	403	403	05 - 07.10.25	1	1	0	76	-	NBC NORTHERN	
12		Hamara	1,238	1,052				964	191	544	544		4	4	0	60	0		
	1	Haki 1	344	253	Kokoda HC	Yes	19.08.25	207	46	122	122	06.10.25	1	1	0	18	-	93.7 FM	
	2	Haki 2	245	198	Kokoda HC	Yes	18.08.25	231	40	128	128	06.10.25	1	1	0	8	-	93.7 FM	
	3	Hamara	357	357	Kokoda HC	Yes	18.08.25	278	55	155	155	06.10.25	1	1	0	15	-	93.7 FM	Mop-up. 5 HH. 9 nets for 16 population
	4	Hojaki	292	244	Kokoda HC	Yes	18.08.25	248	50	139	139	06.10.25	1	1	0	19	-	90.7 RADIO NORTHERN	
13		Ajeka	1,909	1,847				1737	415	1001	1001		4	4	0	70	0		
	1	Ajeka	585	470	Kokoda HC	Yes	18 -19.08.25	402	94	231	231	06.10.25	1	1	0	26	-	93.7 FM	
	2	Ombisusu	914	779	Kokoda HC	Yes	18.08.25	777	197	458	458	06.10.25	1	1	0	30	-	93.7 FM	
	3	Tara	411	397	Kokoda HC	Yes	19.08.25	373	74	205	205	07.10.25	1	1	0	14		90.7 FM /NBC	
		Warina		201	Kokoda HC	Yes	19.08.25	185	50	107	107	07.10.25	1	1	0			93.7 FM	
14		Evasusu	1,180	1,085				1012	212	562	562		3	3	0	34	0		
	1	Boru	463	415	Kokoda HC	Yes	18.08.25	262	50	144	144	10.10.25	1	1	0	18		93.7 FM	
	2	Evasusu	533	443	Kokoda HC	Yes	18.08.25	557	116	308	308	08.10.25	1	1	0	8		93.7 FM	mop-up. 21 HH. 57 nets for 106 population
	3	Sorape	184	227	Kokoda HC	Yes	18.08.25	193	46	110	110	07.10.25	1	1	0	8		93.7 FM	
15		Asilsil	1,299	1,101				936	239	553	553		8	8	0	53	0		
	1	Asisi	398	245	Kokoda HC	Yes	19.08.25	315	85	186	186	05.10.25	1	1	0	12	-	93.7 FM	Mop-up. 35HH 68 nets for 110 population
	2	Sirorata	422	305	Kokoda HC	Yes	19.08.25	252	50	144	144	07.10.25	1	1	0	16	-	93.7 FM	
	3	Siawa	123	136	Kokoda HC	Yes	19.08.25	121	30	70	70	08.10.25	1	1	0	6	-	93.7 FM	
	4	Kuru	45	0	Kokoda HC	Yes									0			93.7 FM	Included Under Ifon
	5	Ifoin	41	24	Kokoda HC	Yes	21.08.25	22	6	14	14	06.10.25	1	1	0	4	-	93.7 FM	
	6	Sangata	28	58	Kokoda HC										0			93.7 FM	Included Under Ifon
	7	Warangota	17	0	Kokoda HC	Yes	21.08.25	12	3	6	6		1	1	0			93.7 FM	
	8	Siewatumo	24	0	Kokoda HC	Yes	21.08.25	11	5	7	7		1	1	0			93.7 FM	
	9	Siwari	30	63	Kokoda HC										0				Included Under Siewatumo
	10	Homape	78	156	Kokoda HC	Yes	18.08.25	47	15	29	29	05.10.25	1	1	0	8	-	RADIO NORTHERN	
	11	Foeko	91	113	Kokoda HC	Yes	19.08.25	156	45	97	97	05.10.25	1	1	0	7		NBC NORTHERN	
16		Sairope	1,695	1,379				1197	276	676	676		4	4	0	45	0		
	1	Warina	214	0	Kokoda HC														Abandoned
	2	Ambarakowari	132	186	Kokoda HC	Yes	20.08.25	176	46	101	101	07.10.25	1	1	0	13	-	93.7 FM	
	3	Fambe	258	292	Kokoda HC	Yes	19.08.25	167	50	100	100	07.10.25	1	1	0	19	-	93.7 FM	
	4	Sairope	827	730	Kokoda HC	Yes	18 -20.08.25	635	130	352	352	07.10.25	1	1	0	11	-	93.7 FM	Mop-up. 1 HH. 7 nets for 14 population
	5	Somara	264	172	Kokoda HC	Yes	18.08.25	219	50	123	123	06.10.25	1	1	0	2	-	NBC RADIO	

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
17	Putembo		1,214	1,289				1052	310	620	620		9	9	0	45	0		
	1	Maujeta	253	184	Kokoda HC	Yes	19.08.25	147	50	90	90	10.10.25	1	1	0	11		90.7FM	
	2	Putembo	106	136	Kokoda HC	Yes	20.08.25	140	34	80	80	10.10.25	1	1	0			93.7 FM	mop-up. 2 HH. 5 nets for 10 population
	3	Osara	45	101	Kokoda HC	Yes	20.08.25	41	14	24	24	10.10.25	1	1	0			93.7 FM	
	4	Butipe	227	245	Kokoda HC	Yes	21.08.25	210	50	116	116	07.10.25	1	1	0	11		93.7 FM	
	5	Maire Corner	97	182	Kokoda HC	Yes	19.10.25	159	50	95	95	07.10.25	1	1	0	6		93.7 FM	
	6	Majara	123	185	Kokoda HC	No	19.08.25	124	35	75	75	14.10.25	1	1	0	3		90.7 FM	
	7	Perobibassusu	56	73	Kokoda HC	Yes	19.08.25	59	18	35	35	14.10.25	1	1	0	6		90.7 FM	
	8	Pugahembo	182	146	Kokoda HC	Yes	20.08.25	123	43	76	76	14.10.25	1	1	0	7		90.7 FM	
	9	Sasere	123	37	Kokoda HC	Yes	20.08.25	49	16	29	29	14.10.25	1	1	0	1		93.7 FM	
18	Asafa		1,312	1,209				1266	271	700	700		4	4	0	0	0		
	1	Asafa	561	687	Kokoda HC	Yes	19-10.08.25	606	121	336	336	12.10.25	1	1	0			93.7 FM	
	2	Jaiapa	225	88	Kokoda HC	Yes	19.08.25	201	50	114	114	12.10.25	1	1	0			93.7 FM	
	3	Enjoro	178	155	Kokoda HC	Yes	20.08.25	215	50	132	132	12.10.25	1	1	0			93.7 FM	
	4	Godibeth	349	278	Kokoda HC	Yes	20.10.25	244	50	118	118	12.10.25	1	1	0			93.7 FM	
19	Wora		1,208	748															
	1	Onuaba	182	112	Emo HC														Air/Trek
	2	Waribia	132	142	Emo HC														Air/Trek
	3	Managube	351	186	Emo HC														Air/Trek
	4	Namanaia (Wora)	381	308	Emo HC														Air/Trek
	5	Wora	162	0	Emo HC														Air/Trek
20	Emo		1,279	947															
	1	Emo 1	271	103	Emo HC														Air/Trek
	2	Emo 2	136	70	Emo HC														Air/Trek
	3	Urambosi	147	222	Emo HC														Air/Trek
	4	Ijaro 1	225	163	Emo HC														Air/Trek
	5	Ijaro 2	225	187	Emo HC														Air/Trek
	6	Rumara	167	140	Emo HC														Air/Trek
	7	Emo Station	108	62	Emo HC														Air/Trek
21	Awomo		1,314	553															
		Wasaro		0	Emo HC														Air/Trek
	1	Awoma	684	251	Emo HC														Air/Trek
	2	Tetebedi	325	166	Emo HC														Air/Trek
	3	Muni	305	136	Emo HC														Air/Trek
22	Kovio		626	399															
		Duau		102	Emo HC														Air/Trek
	1	Kovio 1	288	215	Emo HC														Air/Trek
	2	Kovio 2	338	82	Emo HC														Air/Trek
23	Kokoda Urban		1,182	1,115				1189	236	656	656		5	5	0	92	0		
	1	Kokoda Station	208	95	Kokoda HC	Yes	21.08.25	211	40	113	113	09.10.25	1	1	0	1		93.7 FM	Mop-up. 4 HH. 11 nets for 23 population
	2	Kokoda Station	554	447	Kokoda HC	Yes	19.08.25	531	100	295	295	09.10.25	1	1	0	54	-	93.7 FM	
	3	Kokoda Station	165	267	Kokoda HC	Yes	20.08.25	211	50	117	117	09.10.25	1	1	0	8		93.7 FM	
	4	CRC/SDA Area	143	129	Kokoda HC	Yes	20.08.25	111	24	62	62	09.10.25	1	1		18		93.7 FM	
	5	Golala compound	113	177	Kokoda HC	Yes	19.08.25	125	22	69	69	09.10.25	1	1		11		93.7 FM	
24	Mamba Urban		3,455	2,774				2227	375	1214	1214		5	5	0	210	0		
	1	Konea	1,139	1,009	Kokoda HC	Yes	19.08.25	723	119	396	396	13.10.25	1	1		44		93.7 FM	
	2	Komo	1,403	834	Kokoda HC	Yes	19.08.25	792	125	425	425	11.10.25	1	1		46		93.7 FM	
	3	Old Mamba (Asisi)	54	243	Kokoda HC	Yes	22.08.25	154	26	84	84	13.10.25	1	1		21		93.7 FM	
	4	Mamba Village	756	500	Kokoda HC	Yes	20.08.25	534	100	295	295	13.10.25	1	1		95		93.7 FM	
	5	Ove Place	104	188	Kokoda HC	Yes	20.08.25	24	5	14	14	14.10.25	1	1		4		93.7 FM	
				0															

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
Higaturu Rural			76,202	82,440				79491	15185	40934	40179		211	164	5	3197	2343	164	
	1	New Warisota	587	1,211				1093	205	551	551		4	4	0	37	53		
		1 New Warisota Village	147	329	Sangara HC	Yes	18.08.25	388	78	195	195	07.09.25	1	1	0	19	28	NBC	Road
		Manuta		279	Sangara HC	Yes	18.08.25	123	20	59	59	08.09.25	1	1	0	4	7	NBC	Road
		Garepa & Ese		161	Sangara HC	Yes	18.08.25	288	50	141	141	07.09.25	1	1	0	1	5	NBC	Road
		2 New Warisota VOP Blo	439	441	Sangara HC	Yes	18.08.25	294	57	156	156	07.09.25	1	1	0	13	13	NBC	Road
	2	Hohorita	2,520	3,255				2810	624	1465	1465		7	7	0	122	138		
		Dipotutu		247	Sangara HC	Yes	18.08.25	161	49	93	93	08.09.25	1	1	0	3	4	NBC	Road
		1 Hohorita Village	892	876	Sangara HC	Yes	18.08.25	1128	205	560	560	09.09.25	1	1	0	16	29	NBC	Road
		2 Irihambo	507	408	Sangara HC	Yes	18.08.25	278	97	162	162	11.09.25	1	1	0	17	26	NBC	Road
		3 Kakita	351	784	Sangara HC	Yes	18.08.25	509	120	271	271	10.09.25	1	1	0	37	31	NBC	Road
		4 Sombou	188	225	Sangara HC	Yes	19.08.25	76	23	39	39	12.09.25	1	1	0	1	1	NBC	Road
		5 Hohorita VOP blocks	526	657	Sangara HC	Yes	19.08.25	493	98	252	252	09.09.25	1	1	0	34	31	NBC	Road
		6 Hohorita Com School	56	58	Sangara HC	Yes	18.08.25	165	32	88	88	09.09.25	1	1	0	14	16	NBC	Road
	3	Igora Oil Palm Blocks	3,905	3,428				3487	588	1681	1681		3	3	0	125	339		
		1 Igora Oil palm Block	2,992	2,919	Sangara HC	Yes	19.08.25	2901	480	1413	1413	10.09.25	1	1	0	63	273	NBC	Road
		2 Igora Primary School	420	328	Sangara HC	Yes	19.08.25	368	58	159	159	10.09.25	1	1	0	37	41	NBC	Road
		3 OPIC	494	181	Sangara HC	Yes	19.08.25	218	50	109	109	10.09.25	1	1	0	25	25	NBC	Road
	4	Koipa	1,715	1,517				1,714	289	857	848		8	5	0	184	0		
		1 Koipa	671	819	Saiho HC	Yes/No	22.08.25	650	124	325	316	14.09.25	1	1	0	39	0	NBC	Road
		2 Pusahambo	320	0	Saiho HC			0	0	0		0	1	0	0	0	0		Surveyed Under Higaturu Vocational
		3 Samba	182	251	Saiho HC	Yes/No	22.08.25	288	50	144	144	21.09.25	1	1	0	23	0	NBC	Road
		4 Kevana	162	0	Saiho HC	Yes/No	26.08.25	154	26	77	77	14.09.25	1	1	0	28	0	NBC	Road
		5 Higaturu Vocational Ce	91	108	Saiho HC	Yes/No	22.08.25	372	50	186	186	15.09.25	1	1	0	56	0	NBC	Road
		6 Martyrs Secondary Sc	288	339	Saiho HC	Yes/No	22.08.25	250	39	125	125	14.09.25	1	1	0	38	0	NBC	Road
		Endege			Saiho HC			0	0	0	0	0	1	0	0	0	0		Surveyed Under Samba Village
		Hamoni			Saiho HC			0	0	0	0	0	1	0	0	0	0		Surveyed Under Higaturu Vocational
	5	Kiorota	3,762	2,933				2,743	514	1,378	1,379		12	6	0	150	54		
		1 Siriri	171	264	Saiho HC	Yes/No	21.08.25	152	30	81	76	21.09.25	1	1	0	13	3	NBC	Road
		2 Hamumuta	97	216	Saiho HC	Yes/No	21.08.25	250	50	125	125	11.09.25	1	1	0	14	26	NBC	Road
		3 Eveka	186	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Surveyed Under Hamumuta
		4 Garata	160	239	Saiho HC	Yes/No	22.08.25	255	50	128	127	14.09.24	1	1	0	8	2	NBC	Road
		5 Ijivene	240	109	Saiho HC	Yes/No	22.08.25	163	34	82	81	14.09.25	1	1	0	12	3	NBC	Road
		6 Kongota	89	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Kiorota Village
		7 Tambore (Egaturu)	113	196	Saiho HC	Yes/No	21.08.25	352	60	176	176	14.09.25	1	1	0	18	8	NBC	Road
		8 Aura Hambo	201	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Kiorota Village
		9 Gijiri	52	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Kiorota Village
		10 Kiorota	2,299	1,908	Saiho HC	Yes/No	22.08.25	1571	300	786	794	14.09.25	1	1	0	85	12	NBC	Road
		11 Kamusa	89	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Surveyed Under Kiorota
		12 Kiorota Com School	65	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Surveyed Under Kiorota
	6	Barevoturu	2,914	2,637				2,487	488	1,242	1,240		7	3	0	111	11		
		1 Barevaturu	1,069	1,019	Saiho HC	Yes/No	22.08.25	1084	221	542	540	15.09.25	1	1	0	32	0	NBC	Road
		2 Eusi No.1	100	0	Saiho HC			0	0	0			1	0	0	0	0		Surveyed Under Barevoturu
		3 Eusi No.2	78	0	Saiho HC			0	0	0			1	0	0	0	0		Surveyed Under Barevoturu
		4 Hogoruturu	236	290	Saiho HC	Yes/No	21.08.25	222	50	111	111	17.09.25	1	1	0	15	3	NBC	Road
		5 Kisesehambo	102	0	Saiho HC			0	0	0			1	0	0	0	0		Survired Under Barevoturu
		6 Timbeki	1,292	1,327	Saiho HC	Yes/No	22.08.25	1181	217	589	589	22.09.25	1	1	0	64	8	NBC	Road
		7 Barevaturu Com school	37	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Survired Under Timbeki
	7	Kendata	1,550	1,720				1,774	359	888	891		4	4	0	44	2		
		1 Kendata	660	686	Saiho HC	Yes/No	25.08.25	722	136	361	360	21.09.25	1	1	0	5	0	NBC	Road
		2 Ururu	433	300	Saiho HC	Yes/No	23.08.25	343	73	172	172	21.09.25	1	1	0	9	2	NBC	Road
		3 Sigoreturu	191	274	Saiho HC	Yes/No	23.08.25	265	50	133	132	22.09.25	1	1	0	19	0	NBC	Road
		4 Savarituru	266	459	Saiho HC	Yes/No	26.08.25	444	100	222	227	21.09.25	1	1	0	11	0	NBC	Road

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
8	Duve		2,591	2,166				2,326	392	1,166	1,160		11	9	0	95	13		
	1	Peretambari	104	96	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Duve Village
	2	Duve	688	247	Saiho HC	Yes/No	25.08.25	648	100	324	324	12.09.25	1	1	0	33	0	NBC	Road
	3	Nomota	203	279	Saiho HC	Yes/No	25.08.25	75	14	38	37		1	1	0	1	0	NBC	Distributed but yet to collect the book
	4	Janguta	82	124	Saiho HC	Yes/No	25.08.25	175	32	88	87	12.09.25	1	1	0	8	11	NBC	Road
	5	Singite	160	181	Saiho HC	Yes/No	27.08.25	155	26	78	77	12.09.25	1	1	0	8	0	NBC	Road
	6	Hirususu	175	187	Saiho HC	Yes/No	26.08.25	185	30	93	92	16.09.25	1	1	0	4	0	NBC	Road
	7	Singi	524	170	Saiho HC	Yes/No	26.08.25	320	50	160	160	18.09.25	1	1	0	13	0	NBC	Road
	8	Urarituru	305	304	Saiho HC	Yes/No	23.08.25	317	70	159	158	11.09.25	1	1	0	15	0	NBC	Road
	9	Hevapa	245	277	Saiho HC	Yes/No	23.08.25	301	47	151	150	12.09.25	1	1	0	11	2	NBC	Road
	10	Savarituru	104	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Ward 7 Kendata
		Puri		300	Saiho HC	Yes/No	27.08.25	150	23	75	75	18.09.25	1	1	0	2	0	NBC	Road
9	Kongohambo		1,948	1,711				1,706	284	853	853		5	5	0	88	6		
	1	Sasembata	608	498	Saiho HC	Yes/No	27.08.25	601	108	300	299	10.09.25	1	1	0	15	2	NBC	Road
	2	Torogota	331	368	Saiho HC	Yes/No	24.08.25	334	50	167	171	11.09.25	1	1	0	30	0	NBC	Road
	3	Kongohambo	271	266	Saiho HC	Yes/No	25.08.25	272	50	136	136	10.09.25	1	1	0	12	0	NBC	Road
	4	Sasembata Com Scho	154	169	Saiho HC	Yes/No	23.08.25	70	11	35	35	10.09.25	1	1	0	11	2	NBC	Road
	5	Hamburata	585	410	Saiho HC	Yes/No	28.08.25	429	65	215	212	10.09.25	1	1	0	20	2	NBC	Road
10	Binduta		2,347	2,263				2,190	422	1,100	1,082		5	5	0	161	0		
	1	Garombi	439	551	Saiho HC	Yes/No	23.08.25	476	82	238	235	20.09.25	1	1	0	23	0	NBC	Road
	2	Sambahuta	195	273	Saiho HC	Yes/No	24.08.25	188	40	94	94	11.09.25	1	1	0	17	0	NBC	Road
	3	Isoge	892	633	Saiho HC	Yes/No	28.08.25	679	129	340	337	10.09.25	1	1	0	76	0	NBC	Road
	4	Sivepi	455	397	Saiho HC	Yes/No	23.08.25	387	78	198	189	10.09.25	1	1	0	24	0	NBC	Road
	5	Binduta	366	409	Saiho HC	Yes/No	07.09.25	460	93	230	227	10.09.25	1	1	0	21	0	NBC	Road
11	Handarituru		4,637	5,078				4752	843	2376	2395		12	9	0	269	19		
	1	Agenahambo	807	1,098	Saiho HC	Yes/No	21.08.25	895	142	448	448	23.09.25	1	1	0	31	0	NBC	Road
	2	Ivindari	331	0	Saiho HC	Yes/No	22.08.25	292	50	146	151	22.09.25	1	1	0	6	7	NBC	Road
	3	Peromba	268	92	Saiho HC	Yes/No	22.08.25	192	34	96	95	23.09.25	1	1	0	25	0	NBC	Road
	4	Bago	251	0	Saiho HC					0			1						Included under Sarimbo
	5	Handarituru	686	1,073	Saiho HC	Yes/No	21.08.25	588	111	294	293	21.09.25	1	1	0	37	10	NBC	Road
	6	Sarimbo	273	713	Saiho HC	Yes/No	21.08.25	540	100	270	269	22.09.25	1	1	0	35	0	NBC	Road
	7	Eundu	351	251	Saiho HC	Yes/No	21.08.25	292	50	146	146	15.09.25	1	1	0	5	0	NBC	Road
	8	Soroputa	805	837	Saiho HC	Yes/No	21.08.25	866	150	433	434	22.09.25	1	1	0	55	2	NBC	Road
	9	Uhita	771	800	Saiho HC	Yes/No	21.08.25	854	169	427	442	15.09.25	1	1	0	62	0	NBC	Road
	10	Agenahambo Com Sch	93	0	Saiho HC			0	0	0		0	1	0	0	0	0		Survey Under Agenahambo
		Jungata		214	Saiho HC	Yes/No	21.08.25	233	37	116	117	14.09.25	1	1	0	13	0	NBC	Road
		Haruru		0	Saiho HC			0	0	0		0	1	0	0	0	0		Surveyed Under Agenahambo Village
12	Awala		2,717	2,716				2,321	450	1,161	1,159		6	3	0	137	4		
	1	Awala	1,520	571	Saiho HC	Yes/No	22.08.25	744	150	372	373	18.09.25	1	1	0	33	0	NBC	Road
	2	Awala VOP Block	476	595	Saiho HC	Yes/No	21.08.25	735	150	368	366	19.25.09	1	1	0	47	0	NBC	Road
	3	Saiho Health Centre	167	1,279	Saiho HC	Yes/No	21.08.25	842	150	421	420	11.09.25	1	1	0	57	4	NBC	Road
	4	Awala Com Sch	67	271	Saiho HC								1	0	0	0	0		Surveyed Under Awala Village
	5	Saiho Police Station	61	0	Saiho HC								1	0	0	0	0		Surveyed Under Saiho HC
	6	Serahambo VOP Block	426	0	Saiho HC								1	0	0	0	0		Surveyed Under Awala VOP Block
13	Sui		2,340	1,802				1,950	363	975	988		3	3	5	6	0		
	1	Tandeti	247	130	Saiho HC	Yes/No	28.08.25	298	50	149	149	15.09.25	1	1	0	0	0	NBC	Road
	2	Sui	1,331	763	Saiho HC	Yes/No	31.08.25	799	150	400	413	14.09.25	1	1	0	6	0	NBC	Road
	3	Tunana	762	909	Saiho HC	Yes/No	28.08.25	853	163	426	426	14.09.25	1	1	5	0	0	NBC	Road
14	Boru		2,271	1,791				1,888	391	944	947		5	4	0	80	1		
	1	Angorota	595	522	Saiho HC		0	0	0	0	0	0	1	0	0	0	0		Survey Under Waseta Village
	2	Waseta	292	267	Saiho HC	Yes/No	27.08.25	854	150	427	427	13.09.27	1	1	0	48	0	NBC	Road
	3	Boro + Boru Vop Bick	647	452	Saiho HC	Yes/No	28.08.25	526	128	263	264	25.09.25	1	1	0	9	0	NBC	Road
	4	Waseta C/Sch	115	95	Saiho HC	Yes/No	25.08.25	82	13	41	42	12.09.25	1	1	0	10	1	NBC	Road
	5	Waseta Vop Bick	621	453	Saiho HC	Yes/No	25.08.25	426	100	213	214	12.09.25	1	1	0	13	0	NBC	Road

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digital	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
15	Mumuni		1,600	1,832				2,117	443	1,057	1,056		3	3	0	109	2		
	1	Mumuni	1,165	992	Saiho HC	Yes/No	24.08.25	1073	214	536	536	11.09.25	1	1	0	69	2	NBC	Road
	2	Mumunipe	435	399	Saiho HC	Yes/No	25.08.25	553	131	275	275	11.09.25	1	1	0	14	0	NBC	Road
		Dapari	440		Saiho HC	Yes/No	25.08.25	491	98	246	245	14.09.25	1	1	0	26	0	NBC	
16	Koropata		3,338	2,693				2,721	473	1,360	1,355		6	5	0	235	5		
	1	Honai	136	0	Saiho HC			0	0	0		0	1	0	0	0	0		Surveyed Under Koropata 2
	2	Koropata 1	987	595	Saiho HC	Yes/No	25.08.25	537	86	268	268	12.09.25	1	1	0	68	2	NBC	Road
	3	Koropata 2	1,925	935	Saiho HC	Yes/No	27.08.25	1015	192	507	504	12.09.25	1	1	0	90	1	NBC	Road
	4	Bata	268	290	Saiho HC	Yes/No	25.08.25	281	47	141	140	12.09.25	1	1	0	48	2	NBC	Road
	5	Harange C/Sch	22	275	Saiho HC	Yes/No	25.08.25	254	50	127	127	20.09.25	1	1	0	9	0	NBC	Road
		Harange		598	Saiho HC	Yes/No	25.08.25	634	98	317	316	20.09.25	1	1	0	20	0	NBC	
17	Sirembi		2,881	2,836				2,324	432	1,164	1,157		12	4	0	23	0		
	1	Nahihisu	284	477	Saiho HC	Yes/No	25.08.25	330	62	166	164	22.09.25	1	1	0	19	0	NBC	Road
	2	Homape	435	0	Saiho HC			0	0	0	0		1	0	0	0	0		Under Mengothuti
	3	Keuri	134	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Hujavasusu
	4	Hujavasusu	318	551	Saiho HC	Yes/No	25.08.25	207	37	104	100	22.09.25	1	1	0	2	0	NBC	Road
	5	Uhoru	281	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Serembe
	6	Siporosusu	238	0	Saiho HC					0			1						Surveyed Under Sirembi 1
	7	Sirembi 1	385	1,439	Saiho HC	Yes/No	27.08.24	1316	253	658	657	21.09.25	1	1	0	2	0	NBC	Road
	8	Sirembi 2	132	0	Saiho HC			0	0	0			1	0	0	0	0		Surveyed Under Sirembi 1
	9	Mengothuti	113	369	Saiho HC	Yes/No	27.08.25	471	80	236	236	23.09.25	1	1	0	0	0	NBC	Road
	10	Hujavasusu Vop Bick	193	0	Saiho HC			0	0	0	0		1	0	0	0	0		Surveyed Under Hujavasusu
	11	Anjagoro CRC C/Group	305	0	Saiho HC			0	0	0	0		1	0	0	0	0		Surveyed Under Sirembi 1
	12	Sirembi Com sch	63	0	Saiho HC			0	0	0	0		1	0	0	0	0		Surveyed Under Sirembi 1
18	Hungiri		2,111	2,509				2357	385	1185	1183		12	8	0	63	0		
	1	Divinokovari	130	89	Saiho HC	Yes/No	25.08.25	183	26	99	99	20.09.25	1	1	0	7	0	NBC	Road
	2	Hungiri	463	667	Saiho HC	Yes/No	27.08.25	654	121	327	326	27.09.25	1	1	0	0	0	Nii	Road
	3	Uarisusu	195	304	Saiho HC	Yes/No	26.08.25	197	32	98	98	23.09.25	1	1	0	7	0	NBC	Road
	4	Jambu	208	308	Saiho HC	Yes/No	26.08.25	245	45	122.5	122	22.09.25	1	1	0	11	0	NBC	Road
	5	Onota	288	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Hungiri
	6	Jordanpe	121	150	Saiho HC	Yes/No	26.08.25	86	14	43	43	21.09.25	1	1	0	11	0	NBC	Road
	7	Ariho	143	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included Under Kumusi Village
	8	Kumusi	169	333	Saiho HC	Yes/No	26.08.25	331	49	165	165	22.09.25	1	1	0	12	0	NBC	Road
	9	Dapa	201	410	Saiho HC	Yes/No	27.08.25	374	58	187	187	22.09.25	1	1	0	10	0	NBC	Road
	10	Aisehe	175	161	Saiho HC	Yes/No	26.08.25	287	40	144	143	22.09.25	1	1	0	5	0	NBC	Road
	11	Hungiri C/Sch	17	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included under Hungiri
		Konganata		88	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included under Aisehe
19	Sakita		4,029	4,082				3,620	617	1,808	1,854		11	5	0	90	33		
	1	Poha 1 & 2	1,137	1,180	Saiho HC	Yes/No	25.08.25	1183	200	590	590	23.09.25	1	1	0	25	0	NBC	Road
	2	Sakita 2	152	580	Saiho HC	Yes/No	25.08.25	880	140	440	486	23.09.25	1	1	0	23	0	NBC	Road
	3	Isemba	191	336	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included under Sakita
	4	Togaho	550	773	Saiho HC	Yes/No	26.08.25	559	100	279	279	22.09.25	1	1	0	0	33	NBC	Road
	5	Tunana	643	771	Saiho HC	Yes/No	26.08.25	762	137	381	381	23.09.25	1	1	0	33	0	NBC	Road
	6	Kangoaho	197	91	Saiho HC			0	0	0	0	0	1	0	0	0	0		Included under Tunana
	7	Sakita 1	704	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Inclueed under Sakita VOP Bick
	8	Sakita VOP Bick	143	353	Saiho HC	Yes/No	30.08.25	236	40	118	118	22.09.25	1	1	0	9	0	NBC	Road
	9	Togaho Com Sch	69	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Inclueed under Togaho village
	10	Sakita Com Sch	30	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Inclueed under Sakita VOP Bick
	11	Sakita Last Vop Bick	214	0	Saiho HC			0	0	0	0	0	1	0	0	0	0		Inclueed under Sakita VOP Bick
20	Papoga		4,111	6,047				6218	1299	3876	3088		12	10	0	56	136		
	1	Iwore	297	312	Sangara HC	Yes	19.08.25	540	114	264	264	14.09.25	1	1	0	28	30	NBC	Road
	2	Gigisesusu	91	261	Sangara HC	Yes	19.08.25	64	11	32	32	14.09.25	1	1	0	0	3	NBC	Road
	3	Ijikata	310	569	Sangara HC	Yes	19.08.25	309	64	148	148	15.09.25	1	1	0	0	0	NBC	Road
	4	Jajau	623	696	Sangara HC	Yes	23.09.25	1058	221	552	553	15.09.25	1	1	0	1	12	NBC	Road
	5	Kanari	273	443	Sangara HC	Yes	19.09.25	238	75	210	210	27.09.25	1	1	0	0	0	NBC	Road
	6	Papoga	903	1,874	Sangara HC	Yes	23.08.25	1959	415	1629	833	13.09.25	1	1	0	6	28	NBC	Road
	7	Begahambo	331	235	Sangara HC								1						covered underPapoga
	8	Maneneta	349	228	Sangara HC	Yes	21.09.25	252	50	128	128	15.09.25	1	1	0	0	7	NBC	13 pages without white receipts but net issued by volunteers.
	9	Puhemo	448	0	Sangara HC	Yes	25.09.25	250	50	125	132	17.09.25	1	1	0	0	0	NBC	Held in trust net
	10	Isuga	487	0	Sangara HC	Yes	25.09.25	240	50	122	122	17.09.25	1	1	0	20	0	NBC	Held in trust net
		Taubender		415	Sangara HC								1						covered under Jajau village
		Waru		1,014	Sangara HC	Yes	23.09.25	1308	249	666	666	14.09.25	1	1	0	1	56	NBC	16 pages without white receipts but net issued by volunteers.

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
21	Ongoho		2,379	3,508		Yes		4713	950	2476	2476		10	10	0	38	87		
	1	Ondahare	346	243	Sangara HC	Yes	24.09.25	421	100	214	214	14.09.25	1	1	0	22	19	NBC	Road
	2	Girigirita	621	625	Sangara HC	Yes	24.09.25	521	100	283	283	15.09.25	1	1	0	0	12	NBC	Volunteer did the distribution without collecting white receipts
	3	Oere	359	529	Sangara HC	Yes	24.08.25	505	100	255	255	14.09.25	1	1	0	3	11	NBC	Road
	4	Ongoho	498	731	Sangara HC	Yes	24.08.25	747	150	389	389	15.09.25	1	1	0	0	12	NBC	Road
	5	Ihriya	162	470	Sangara HC	Yes	24.08.25	447	100	256	256	15.09.25	1	1	0	0	1	NBC	Road
	6	Totogata	113	365	Sangara HC	Yes	24.08.25	499	100	258	258	15.09.25	1	1	0	9	8	NBC	Road
	7	Hunjeke	50	0	Sangara HC	Yes	24.08.25	275	50	139	139	14.09.25	1	1	0	0	7	NBC	Road
	8	Sasovi	80	377	Sangara HC	Yes	24.08.25	217	50	107	107	14.09.25	1	1	0	3	13	NBC	Road
	9	Girigirita Hamlet	149	169	Sangara HC	Yes	19.08.25	532	100	278	278	15.09.25	1	1	0	1	1	NBC	Volunteer did the distribution without collecting white receipts
		Hongarata		0	Sangara HC	Yes	19.08.25	549	100	297	297	15.09.25	1	1	0	0	3	NBC	10 page without receipt but net issued by volunteers
22	Ehu		1,474	3,211				2338	450	1247	1247		12	12	0	112	100		
	1	Sehoro 1 & 2	375	725	Sangara HC	Yes	18.08.25	412	71	220	220	07.09.25	1	1	0	1	1	NBC	Road
	2	Sarukata	76	346	Sangara HC	Yes	18.08.25	470	83	232	232	09.09.25	1	1	0	67	67	NBC	Road
	3	Gombususu	128	248	Sangara HC	Yes	18.08.25	281	50	101	101	06.09.25	1	1	0	5	14	NBC	Road
	4	Paugu	193	0	Sangara HC	Yes	18.08.25	123	23	66	66	06.09.25	1	1	0	1	2	NBC	Road
	5	Kipore	139	228	Sangara HC	Yes	18.08.25	139	23	70	70	06.09.25	1	1	0	0	0	NBC	Road
	6	Ehu	162	392	Sangara HC	Yes	18.08.25	179	59	154	154	06.09.25	1	1	0	1	0	NBC	8 page without white receipts but volunteer issued net
	7	Senani	262	278	Sangara HC	Yes	18.08.25	208	43	130	130	06.09.25	1	1	0	35	8	NBC	Road
	8	Ponsusu VOP Bick	80	210	Sangara HC	Yes	18.08.25	84	17	48	48	06.09.25	1	1	0	2	2	NBC	Road
		Bore		145	Sangara HC	Yes	18.08.25	102	22	54	54	06.09.25	1	1	0	0	0	NBC	Road
		Hamba # 1		251	Sangara HC	Yes	18.08.25	85	16	44	44	06.09.25	1	1	0	0	4	NBC	Road
		Hamba # 2		244	Sangara HC	Yes	18.08.25	193	33	96	96	06.09.25	1	1	0	0	2	NBC	Road
	9	Kipore VOP Bick	61	143	Sangara HC	Yes	18.08.25	62	10	32	32	06.09.25	1	1	0	0	0	NBC	Road
23	Ahora & Beuru		2,472	2,681				2323	465	1213	1213		7	7	0	63	76		
	1	Darata	201	114	Sangara HC	Yes	18.08.25	236	50	124	124	09.09.25	1	1	0	5	4	NBC	Road
	2	Beuru	388	655	Sangara HC	Yes	18.08.25	644	131	348	348	09.09.25	1	1	0	19	23	NBC	Road
	3	Ahora	448	364	Sangara HC	Yes	18.08.25	333	68	175	175	09.09.25	1	1	0	9	6	NBC	Road
	4	Ahora VOP Bick	613	514	Sangara HC	Yes	18.08.25	331	76	174	174	09.09.25	1	1	0	2	3	NBC	Road
	5	Darata VOP Bick	329	438	Sangara HC	Yes	18.08.25	357	47	171	171	09.09.25	1	1	0	0	7	NBC	Road
	6	Ahora Com School	89	22	Sangara HC	Yes	18.08.25	227	50	122	122	09.09.25	1	1	0	26	11	NBC	Road
	7	Beuru Blocks	405	573	Sangara HC	Yes	18.08.25	195	43	99	99	09.09.25	1	1	0	2	22	NBC	Road
24	West Ambogo		2,964	4,412		Yes	18.08.25	5333	1040	2685	2685		7	7	0	243	362		
	1	West Ambogo Block	2,645	2,240	Sangara HC	Yes	18.08.25	3048	572	1535	1535	09.09.25	1	1	0	90	179	NBC	7+6+17=30 receipt without white receipts but net issued by volunteers
	2	Sangara Com School	97	606	Sangara HC	Yes	18.08.25	680	150	337	337	08.09.25	1	1	0	51	54	NBC	10 receipt without white receipts but volunteer issued net
	3	Sangara Missn Station	22	241	Sangara HC	Yes	18.08.25	298	50	150	150	07.09.25	1	1	0	36	36	NBC	6 receipt without white receipts but volunteer issued net
	4	Sangara Police Station	65	124	Sangara HC	Yes	18.08.25	143	19	72	72	07.09.25	1	1	0	0	13	NBC	Road
	5	Sangara Health Centre	87	214	Sangara HC	Yes	18.08.25	260	50	116	116	08.09.25	1	1	0	1	26	NBC	Road
	6	Sangara Voc Centre	48	255	Sangara HC	Yes	18.08.25	201	41	111	111	08.09.25	1	1	0	15	15	NBC	Road
	7	Monge 1/2/3/485		732	Sangara HC	Yes	18.08.25	703	158	364	364	08.09.25	1	1	0	50	39	NBC	Road
25	Sangara 1		6,904	7,714				5805	1267	3005	3005		12	10	0	335	551		
	1	Siroga	2,992	2,117	Sangara HC	Yes	18.08.25	1398	249	676	676	08.09.25	1	1	0	55	122	NBC	7+10+8+6=31 receipt without white receipts but volunteer issued net
	2	Epa (Incl Oil Palm Village)		503	Sangara HC								1						
	3	Irigi Oil Palm Village (Irigi/Ambogo)		752	Sangara HC								1						
	4	Javuni	801	953	Sangara HC	Yes	18.08.25	630	140	419	419	08.09.25	1	1	0	88	101	NBC	21 page without white receipts but volunteer issued net
	5	Arehe Block	416	883	Sangara HC	Yes	18.08.25	926	250	515	515	08.09.25	1	1	0	55	109	NBC	Road
	6	The Ridge	346	259	Sangara HC	Yes	18.08.25	109	26	60	60	08.09.25	1	1	0	8	8	NBC	Road
	7	Lutheran Area	245	349	Sangara HC	Yes	18.08.25	564	113	237	237	08.09.25	1	1	0	34	39	NBC	Road
	8	Irihambo Village	238	0	Sangara HC	Yes	18.08.25	690	161	365	365	10.09.25	1	1	0	24	68	NBC	7 page without white receipts but volunteer issued net
	9	Irihambo Village	546	680	Sangara HC	Yes	18.08.25	474	118	252	252	08.09.25	1	1	0	15	48	NBC	10+9 19 page without white receipts but volunteer issued net
	10	Sangara Estate	41	149	Sangara HC	Yes	18.08.25	86	22	50	50	08.09.25	1	1	0	20	20	NBC	Road
	11	Sangara Base	273	0	Sangara HC	Yes	18.08.25	114	27	61	61	08.09.25	1	1	0	27	27	NBC	Road
	12	Moale	1,007	1,070	Sangara HC	Yes	18.08.25	814	161	370	370	08.09.25	1	1	0	9	9	NBC	Road
26	Sangara 2		1,764	1,857		Yes	18.08.25	1959	409	1134	1134		3	3	0	92	140		
	1	Lejo	240	0	Sangara HC														Non Existant
	2	Sumbiripa	1,253	1,233	Sangara HC	Yes	18.08.25	1200	259	708	708	19.09.25	1	1	0	79	102	NBC	6 page without white receipts but volunteer issued net
		Eveka		249	Sangara HC	Yes	18.08.25	286	50	190	190	22.09.25	1	1	0	0	25	NBC	
	3	North Sangara Block	271	375	Sangara HC	Yes	18.08.25	473	100	236	236	08.09.25	1	1	0	13	13	NBC	Road
27	Isivini		3,078	3,200				3162	499	1452	1452		5	5	0	111	183		
	1	Isivini Oil Paml Block	2,650	2,110	Sangara HC	Yes	18.09.25	1937	299	843	843	08.09.25	1	1	0	72	92	NBC	7 page without white receipts but volunteer issued net
	2	Isivini Com Sch	48	317	Sangara HC	Yes	19.08.25	381	50	187	187	11.09.25	1	1	0	4	27	NBC	Road
	3	Isivini Police Station	63	555	Sangara HC	Yes	18.09.25	320	50	160	160	10.09.25	1	1	0	28	28	NBC	Road

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
	4	Isivini OPIC	286	176	Sangara HC	Yes	19.08.25	228	50	114	114	10.09.25	1	1	0	2	18	NBC	Road
	5	Isivini Mission/Station	32	41	Sangara HC	Yes	20.08.25	296	50	148	148	10.09.25	1	1	0	5	18	NBC	Road
28	Horau		1,292	1,632				1260	244	635	635		7	5	0	18	28		
	1	Wuwusi	141	134	Sangara HC	Yes	19.08.25	155	33	77	77	30.09.25	1	1	0	5	5	NBC	Road
	2	Agenta	113	128	Sangara HC	Yes	18.09.25	287	49	141	141	02.09.25	1	1	0	3	3	NBC	Road
	3	Horau	260	223	Sangara HC	Yes	18.09.25	227	50	129	129	31.09.25	1	1	0	4	5	NBC	Road
	4	Huhuru	673	581	Sangara HC	Yes	20.08.25	525	100	253	253	07.09..25	1	1	0	6	15	NBC	Road
	5	Barita	78	61	Sangara HC	Yes	19.08.25	66	12	35	35	29.09.25	1	1	0	0	0	NBC	6 page without white receipts but volunteer issued net
	6	Jegarahambo	28	164	Sangara HC	Yes							1						
		Kakisusu		341	Sangara HC	Yes							1						
				0															

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
Tamata Rural			25,420	24,261				22626	3851	11567	11627		78	29	0	27	98	73	
1	Hurata		1,803	2,237				1854	308	953	953		6	0	0	0	0		
	1	Maibasusu	134	145	Saiho HC2		25.08.25	153	27	77	77	11.09.25	1	0	0	0	0	NBC	Road
	2	Hurata	500	672	Saiho HC2		21.08.25	499	83	256	256	11.09.25	1	0	0	0	0	NBC	Road
	3	Sagere	502	759	Saiho HC2		22.08.25	631	99	326	326	11.09.25	1	0	0	0	0	NBC	Road
	4	Aisi	115	83	Saiho HC2		25.08.25	69	11	38	38	11.09.25	1	0	0	0	0	NBC	Road
	5	Toute	327	430	Saiho HC2		21.08.25	340	61	170	170	11.09.25	1	0	0	0	0	NBC	Road
	6	Horusus	225	147	Saiho HC2		22.08.25	162	27	86	86	11.09.25	1	0	0	0	0	NBC	Road
2	Oita Tandi		2,119	2,077				2304	452	1154	1156		9	0	0	0	0		
	1	Iva	167	147	Saiho HC2		27.08.25	146	28	83	83	12.09.25	1	0	0	0	0	NBC	Road/2hrs Boat
	2	Batutu	95	145	Saiho HC2		26.08.25	45	9	22	24	19.09.25	1	0	0	0	0	NBC	Road
	3	Sembasusu	340	268	Saiho HC2		26.08.25	230	42	134	134	19.09.25	1	0	0	0	0	NBC	Road
	4	Oita Tandi	459	421	Saiho HC2		01.09.25	744	150	335	335	11.09.25	1	0	0	0	0	NBC	Road
	5	Siai	528	500	Saiho HC2		22.08.25	418	86	215	215	11.09.25	1	0	0	0	0	NBC	Road
	6	Evida	67	70	Saiho HC2		25.08.25	159	37	79	79	12.09.25	1	0	0	0	0	NBC	Road
	7	Ombo Ragi	106	102	Saiho HC2		27.08.25	133	24	66	66	12.09.25	1	0	0	0	0	NBC	Trek 3hours
	8	Kukuru	130	204	Saiho HC2		07.09.25	130	26	69	69	12.09.25	1	0	0	0	0	NBC	Trek 3hours
	9	Magure Station	227	218	Saiho HC2		25.08.25	299	50	151	151	11.09.25	1	0	0	0	0	NBC	Road
3	Kikinonda		1,728	1,686				1710	307	885	885		7	0	0	0	0		
	1	Dirou	180	175	Saiho HC2		28.08.25	264	50	128	128	12.09.25	1	0	0	0	0	NBC	Trek 2 hours
	2	Orobeari	156	174	Saiho HC2		26.08.25	250	50	130	130	12.09.25	1	0	0	0	0	NBC	Trek 4 Hours
	3	Tambarasisi	216	217	Saiho HC2		08.09.25	148	28	81	81	12.09.25	1	0	0	0	0	NBC	Boat/3 Hr Trek
	4	Usuindari	323	284	Saiho HC2		29.08.25	151	21	79	79	13.09.25	1	0	0	0	0	NBC	Trek 2 hours
	5	Kikinonda	329	313	Saiho HC2		29.08.25	393	65	198	198	13.09.25	1	0	0	0	0	NBC	Trek 2 hours
	6	Poho 1	197	381	Saiho HC2		25.08.25	224	43	121	121	13.09.25	1	0	0	0	0	NBC	Trek 2 hours
	7	Poho 2	119	0	Saiho HC2														Non Existant
	8	Ehenade	208	142	Saiho HC2		26.08.25	280	50	148	148	13.09.25	1	0	0	0	0	NBC	Boat/2 Hr Trek
4	Korisata		1,953	2,194				2186	393	1152	1152		7	0	0	0	0		
	1	Borugasusu	396	424	Saiho HC2		27.08.25	436	62	237	237	13.09.25	1	0	0	0	0	NBC	Road/2 Hr Trek
	2	Sengetari	162	217	Saiho HC2		25.08.25	170	28	91	91	13.09.25	1	0	0	0	0	NBC	Road/2 Hr Trek
	3	Onombasusu	297	276	Saiho HC2		28.08.25	322	55	162	162	12.09.25	1	0	0	0	0	NBC	Road/2 Hr Trek
	4	Korisata	602	657	Saiho HC2		27.08.25	466	98	242	242	12.09.25	1	0	0	0	0	NBC	Boat/2 Hr Trek
	5	Aurita	212	89	Saiho HC2		25.08.25	197	50	104	104	13.09.25	1	0	0	0	0	NBC	Boat/3 Hr Trek
	6	Sevape	139	73	Saiho HC2		26.08.25	62	11	32	32	13.09.25	1	0	0	0	0	NBC	Boat/3 Hr Trek
	7	Osako	145	458	Saiho HC2		26.08.25	533	89	284	284	13.09.25	1	0	0	0	0	NBC	Boat/3 Hr Trek
5	UtuKiari		1,087	1,040				889	172	463	463		5	0	0	0	0		
	1	Ititi	206	164	Saiho HC2		27.08.25	140	27	75	75	13.09.25	1	0	0	0	0	NBC	Boat/4 Hr Trek
	2	Kaiari	281	213	Saiho HC2		27.08.25	160	37	83	83	13.09.25	1	0	0	0	0	NBC	3 Hr Trek
	3	Koninida	143	169	Saiho HC2		27.08.25	152	27	79	79	13.09.25	1	0	0	0	0	NBC	2 Hr Trek
	4	Petikiari	214	225	Saiho HC2		27.08.25	185	34	97	97	13.09.25	1	0	0	0	0	NBC	3 Hr Trek
	5	Utukiari	242	269	Saiho HC2		26.08.25	252	47	129	129	13.09.25	1	0	0	0	0	NBC	4 Hr Trek
6	Kurereda		1,037	921				918	150	470	470		2	0	0	0	0		
	1	Kurereda	615	555	loma HC	Yes	27.09.25	563	85	284	284	01.10.25	1	0	0	0	0	NBC	Boat
	2	Wagadari & Cp-13	91	0	loma HC														Non Exitant
	3	Dabo	331	366	loma HC	Yes	27.09.25	355	65	186	186	30.09.25	1	0	0	0	0	NBC	Boat
7	Jino		2,773	2,698				2680	429	1330	1330		10	0	0	0	0		
	1	Dodove	54	41	loma HC	Yes	27.09.25	94	11	41	41	29.09.25	1	0	0	0	0	NBC	Boat/Trek
	2	Darara	474	339	loma HC	Yes	27.09.25	613	100	289	289	30.09.25	1	0	0	0	0	NBC	Boat/Trek
	3	Aposi	45	211	loma HC	Yes							1						Included Under Barara
	4	Biaga	82	128	loma HC								1						Included Under Barara
	5	Kopatutu	67	72	loma HC	Yes	27.09.25	88	11	44	44	01.10.25	1	0	0	0	0	NBC	Boat/Trek
	6	Iaudari No.1	777	845	loma HC	Yes	27.09.25	783	138	425	425	30.09.25	1	0	0	0	0	NBC	Boat/Trek
	7	Iaudari No.2	699	653	loma HC	Yes	27.09.25	701	114	331	331	01.10.25	1	0	0	0	0	NBC	Boat/Trek
	8	Jino	52	37	loma HC								1						Included Under Dodove
	9	Ginamai	253	237	loma HC	Yes	27.09.25	236	28	114	114	29.09.25	1	0	0	0	0	NBC	Boat/Trek
	10	loma Stn Cp-2,8,9 & 30	268	135	loma HC	Yes	27.09.,25	165	27	86	86	30.09.25	1	0	0	0	0	NBC	Boat/Trek
8	Sia		1,429	1,298				1179	224	621	621		3	3	0	26	0		
	1	Ombarere	39	71	Manau HC														
	2	Bebewa	84	121	Manau HC	Yes	06.10.25	159	32	81	81	17.10.25	1	1	0	0	0	NBC	Boat
	3	Sia	831	687	Manau HC	Yes	04.10.25	642	119	331	331	17.10.25	1	1	0	7	0	NBC	Boat
	4	Taututu	388	419	Manau HC	Yes	04.10.25	378	73	209	209	17.10.25	1	1	0	19	0	NBC	due to time factor we did not collect the white reciept but net was distribute using summary sheets
	5	Boto Com School	87	0	Manau HC														Non Existant
9	Manau		1,401	1,074				1073	213	542	542		3	3	0	0	22		
	1	Mambututu	751	603	Manau HC	Yes	04.10.25	624	131	313	313	12.10.25	1	1	0	0	12	NBC	Boat
	2	Manau	610	471	Manau HC	Yes	05.10.25	414	77	211	211	12.10.25	1	1	0	0	5	NBC	Boat
	3	Manau Anglican Mssn	39	0	Manau HC	Yes	05.10.25	35	5	18	18	12.10.25	1	1	0	0	5	NBC	Boat
10	Deboin		1,082	839				771	128	379	384		1	0	0	0	9		
	1	Deboin, CP 6 & 402	1,059	839	Manau HC	Yes	06.10.25	771	128	379	384	11.10.25	1	0	0	0	9	NBC	Boat
	2	Dewade Com Sch	24	0	Manau HC														Included Under Deboin
11	Kotaure		1,009	1,210				970	175	507	515		4	3	0	0	19		
	1	Kotaure	448	589	Manau HC	Yes	07.10.25	437	89	237	239	11.10.25	1	1	0	0	0	NBC	Boat

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
	2	Yajiwari	184	227	Manau HC	Yes	05.10.25	188	39	103	103	11.10.25	1	1	0	0	3	NBC	due to time factor we did not collect the white reciept but net was distribute using summary sheets
	3	Jingada Cp 2 & 3	375	394	Manau HC	Yes	04.10.25	345	47	167	173	11.10.25	1	1	0	0	16	NBC	Boat
	4	Kotaure Com Sch	2	0	Manau HC								1						Included Under Kotaura

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
12	Tubi		1,085	982				996	160	512	512		5	4	0	0	0		
	1	Tabara	511	248	Manau HC	Yes	10.10.25	193	25	96	96	14.10.25	1	1	0	0	0	NBC	Boat
	2	Taire	93	606	Manau HC	Yes	08.10.25	683	117	355	355	11.10.25	1	1	0	0	0	NBC	Boat
	3	Baiari	372	0	Manau HC								1	1	0	0	0	NBC	Boat
	4	Tubi	104	128	Manau HC	Yes	10.10.25	120	18	61	61	14.10.25	1	1	0	0	0	NBC	Boat
	5	Tabara Com Sch	4	0	Manau HC								1						Included Under Tabara
13	Ainsi		1,264	771				539	84	283	289		3	3	0	0	0		
	1	Ainsi	489	185	Manau HC	Yes	05.10.25	152	22	79	85	10.10.25	1	1	0	0	0	NBC	Boat
	2	Karude	388	351	Manau HC	Yes	05.10.25	201	32	109	109	10.10.25	1	1	0	0	0	NBC	Boat
	3	Onombatutu	331	234	Manau HC	Yes	05.10.25	186	30	95	95	10.10.25	1	1	0	0	0	NBC	Boat
	4	Peio	56	0	Manau HC														Non Existant
14	Nindewari		1,050	1,214				901	146	474	476		3	3	0	1	10		
	1	Nindewari	446	700	Manau HC	Yes	04.10.25	552	89	281	281	11.10.25	1	1	0	1	7	NBC	Boat
	2	Wade	188	256	Manau HC	Yes	11.10.25	175	27	108	108	11.10.25	1	1	0	0	3	NBC	Boat
	3	Wagadari	388	258	Manau HC	Yes	08.10.25	174	30	85	87	11.10.25	1	1	0	0	0	NBC	Boat
	4	Nindewari Statn	28	0	Manau HC														Non Existant
15	Ewore		1,645	1,636				1494	197	729	751		4	4	0	0	11		
	1	Ewore No.2	520	509	Manau HC	Yes	08.10.25	547	75	273	275	09.10.25	1	1	0	0	0	NBC	Boat
	2	Usibe	197	156	Manau HC	Yes	11.10.25	174	28	83	87	11.10.25	1	1	0	0	0	NBC	Boat
	3	Warawagi	102	309	Manau HC	Yes	08.10.25	329	35	155	164	10.10.25	1	1	0	0	0	NBC	Boat
	4	Mopide	149	0	Manau HC														Non Existant
	5	Ewore No.1	678	662	Manau HC	Yes	08.10.25	444	59	218	225	10.10.25	1	1	0	0	11	NBC	Boat
16	Bovera		1,658	1,301				1140	132	579	591		3	3	0	0	23		
	1	Bovera	656	572	Manau HC	Yes	14.10.25	519	53	263	263	15.10.25	1	1	0	0	0	NBC	Boat
	2	Kaiware/Yeni	474	0	Manau HC	Yes	14.10.25	260	28	134	141	15.10.25	1	1	0	0	8	NBC	Boat
	3	Dautami & CP 05	288	380	Manau HC	Yes	14.10.25	361	51	182	187	15.10.25	1	1	0	0	15	NBC	Boat
	4	Kaiware/Gabu	156	348	Manau HC														
	5	Maji Comp Base	84	0	Manau HC														
17	Tave		1,297	1,082				1022	181	534	537		3	3	0	0	4		
	1	Boke	212	275	Manau HC														Non Existant
	2	Baba	115	0	Manau HC														Non Existant
	3	Wavei	15	0	Manau HC														Non Existant
	4	Ina	58	0	Manau HC	Yes	14.10.25	215	45	116	116	15.10.25	1	1	0	0	0	NBC	Boat
	5	Tave	643	603	Manau HC	Yes	14.10.25	589	106	307	310	15.10.25	1	1	0	0	0	NBC	Boat
	6	Dabari	152	0	Manau HC	Yes													Non Existant
	7	Waude	102	204	Manau HC	Yes	13.10.25	218	30	111	111	15.10.25	1	1	0	0	4	NBC	Boat
				0															
Kira Rural			5,235	2,236				0	0	0	0		0	0	0	0	0	0	
	1	Peperware	829	0															
		1 Agutami	498	0	Kira HC														Air/Trek
		2 Pepeware	247	0	Kira HC														Air/Trek
		3 Inowa	84	0	Kira HC														Air/Trek
	2	Gobe	1,173	0															
		1 Gobe	413	0	Kira HC														Air/Trek
		2 Iema	548	0	Kira HC														Air/Trek
		3 Tube	193	0	Kira HC														Air/Trek
		4 Buri	19	0	Kira HC														Air/Trek
	3	Upupure	1,201	855															
		1 Uno	104	67	Kira HC														Air/Trek
		2 Bakadu	173	123	Kira HC														Air/Trek
		3 Gimine	165	79	Kira HC														Air/Trek
		4 Kira	214	177	Kira HC														Air/Trek
		5 Avero	171	84	Kira HC														Air/Trek
		6 Jongendwa	154	61	Kira HC														Air/Trek
		7 Takere	154	137	Kira HC														Air/Trek
		8 Kira Govt Station 31	67	126	Kira HC														Air/Trek
	4	Ovasupu	1,321	874															
		1 Sekare	56	90	Kira HC														Air/Trek
		2 Repanage	147	93	Kira HC														Air/Trek
		3 Aroba	234	136	Kira HC														Air/Trek
		4 Juwera	219	108	Kira HC														Air/Trek
		5 Eroma	78	63	Kira HC														Air/Trek
		6 Avihase	117	58	Kira HC														Air/Trek
		7 Orouba	136	79	Kira HC														Air/Trek
		8 Dapeoba	93	109	Kira HC														Air/Trek
		9 Girei	74	63	Kira HC														Air/Trek
		10 Salasala	167	75	Kira HC														Air/Trek
	5	Oibo	710	508															
		1 Oibo	165	104	Kira HC														Air/Trek
		2 Sedema	234	118	Kira HC														Air/Trek
		3 Sigilehari	165	152	Kira HC														Air/Trek
		4 Baharu	113	134	Kira HC														Air/Trek
		5 Gagaipo	35	0	Kira HC														Air/Trek

ANNEXURE 3
Oro Province: Ijivitari District
LLIN Distribution Summary Sheet 2025

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
Ijivitari District			1,63,215	1,63,215				1,52,545	14,984	37,925	38,011		259	180	0	1,746	139	217	
Oro Bay Rural			47,903	48,402				44,719	9,177	22,812	22,852		125	73	0	1,426	125	107	
1	Sariri Village		1,500	1,567				1777	335	864	869		11	0	0	0	0		
	1	Gobera	118	265	Oro Bay HC	Yes	30.08.25	320	64	150	150	14.09.25	1	0	0	0	0	NBC	Road/Boat/Trekking
	2	Iwuji	252	294	Oro Bay HC	Yes	29.08.25	381	76	185	187	14.09.25	1	0	0	0	0	NBC	Road/Boat/Trekking
	3	Nembadi	209	201	Oro Bay HC	Yes	30.08.25	184	30	90	90	14.09.25	1	0	0	0	0	NBC	Road/Boat/Trekking
	4	Sariri	79	238	Oro Bay HC	Yes	01.09.25	358	65	174	177	14.09.25	1	0	0	0	0	NBC	Road/Boat/Trekking
	5	Ginei	91	0	Oro Bay HC								1					NBC	Included Under Sariri
	6	Wai-E	62	135	Oro Bay HC	Yes	29.08.25	140	33	69	69	14.09.25	1	0	0	0	0	NBC	Road/Boat/Trekking
	7	Ungada	53	78	Oro Bay HC	Yes	01.09.25	56	13	30	30	14.09.25	1	0	0	0	0	NBC	Road/Boat/Trekking
	8	Gora	158	0	Oro Bay HC								1					NBC	Included Under Sariri
	9	Voika	206	0	Oro Bay HC								1					NBC	Included Under Sariri
	10	Yapani	82	0	Oro Bay HC								1					NBC	Included Under Bareji School
	11	Bareji School	190	356	Oro Bay HC	Yes	29.08.25	338	54	166	166	14.09.25	1	0	0	0	0	NBC	Road/Boat/Trekking
2	Gunimba Village		1,174	1,101				1956	351	960	963		5	0	0	12	0		
	1	Gunimba	94	114	Oro Bay HC	Yes	29.08.25	253	49	126	128	14.09.25	1	0	0	0	0	NBC	Road
	2	Pongani	495	317	Oro Bay HC	Yes	29.08.25	1004	174	485	486	14.09.25	1	0	0	12	0	NBC	Road
	3	Seboda	228	242	Oro Bay HC	Yes	29.08.25	302	50	150	150	14.09.25	1	0	0	0	0	NBC	Road
	4	Songade	235	264	Oro Bay HC	Yes	29.08.25	220	46	111	111	14.09.25	1	0	0	0	0	NBC	Road
	5	Gave	122	164	Oro Bay HC	Yes	28.08.25	177	32	88	88	14.09.25	1	0	0	0	0	NBC	Road
3	Jegerakambo Village		1,328	1,297				476	93	259	264		7	3	0	21	2		
	1	Jeburugaiai	106	0	Oro Bay HC													NBC	Non Existent
	2	Jegarakambo	82	142	Oro Bay HC								1					NBC	Included Under Pongani
	3	Mengade	120	205	Oro Bay HC								1					NBC	Included Under Pongani
	4	Puin	98	122	Oro Bay HC								1					NBC	Included Under Pongani
	5	Basada	142	348	Oro Bay HC								1					NBC	Included Under Pongani
	6	Kevi	151	64	Oro Bay HC	Yes	07.09.25	62	12	32	32	19.09.25	1	1	0	5	0	NBC	Road
	7	Doro Musa	233	0	Oro Bay HC														Non Existant
	8	Kari Kambo	139	226	Oro Bay HC	Yes	15.09.25	262	49	145	150	17.09.25	1	1	0	0	0	NBC	Road
	9	Mopide	50	190	Oro Bay HC	Yes	07.09.25	152	32	82	82	19.09.25	1	1	0	16	2	NBC	Road
	10	Asinde	70	0	Oro Bay HC														Non Existant
	11	Peresa	137	0	Oro Bay HC														Non Existant
4	Emo Village		2,125	1,839				1515	272	723	724		3	3	0	8	0		
	1	Emo	667	596	Oro Bay HC	Yes	28.08.25	476	88	230	230	17.09.25	1	1	0	6	0	NBC	Road
	2	Endaduru	557	555	Oro Bay HC	Yes	28.08.25	305	50	143	143	17.09.25	1	1	0	0	0	NBC	Road
	3	Reibai	900	687	Oro Bay HC	Yes	27.08.25	734	134	350	351	17.09.25	1	1	0	2	0	NBC	Road
5	Banderi Village		1,599	1,394				1154	231	561	565		6	3	0	8	1		
	1	Banderi	290	204	Oro Bay HC	Yes	26.08.25	198	42	104	104	11.09.25	1	1	0	1	0	NBC	Road
	2	Sigara	259	265	Oro Bay HC	Yes	27.08.25	241	44	118	118	11.09.25	1	0	0	0	0	NBC	Road/Trekking
	3	Beamatu	254	157	Oro Bay HC	Yes	26.08.25	133	22	66	66	11.09.25	1	1	0	4	1	NBC	Road/Trekking
	4	Boreara	91	98	Oro Bay HC	Yes	26.08.25	56	12	28	30	11.09.25	1	0	0	1	0	NBC	Road/Trekking
	5	Kohara	627	583	Oro Bay HC	Yes	26.08.25	471	97	216	218	11.09.25	1	0	0	0	0	NBC	Road/Trekking
	6	Togofu	77	86	Oro Bay HC	Yes	27.08.25	55	14	29	29	11.09.25	1	1	0	2	0	NBC	Road/Trekking
6	Waiwa Village		1,469	1,391				1317	247	653	657		5	5	0	40	8		
	1	Borou	365	256	Oro Bay HC	Yes	26.08.25	232	41	115	115	11.09.25	1	1	0	4	0	NBC	Road
	2	Waiwa	533	446	Oro Bay HC	Yes	28.08.25	449	83	218	219	11.09.25	1	1	0	11	2	NBC	Road
	3	Ngemeno	82	144	Oro Bay HC	Yes	28.08.25	90	16	45	47	12.09.24	1	1		1	0	NBC	Road
	4	Parama	367	329	Oro Bay HC	Yes	27.08.25	413	78	205	206	11.09.25	1	1	0	18	6	NBC	Road
	5	Beramboro	122	216	Oro Bay HC	Yes	27.08.25	133	29	70	70	11.09.25	1	1	0	6	0	NBC	Road
7	Beama Village		2,370	2,714				2149	544	1172	1151		5	5	0	118	0		
	1	Beama	1,335	1,527	Oro Bay HC	Yes	26.08.25	1297	288	706	685	09.09.25	1	1	0	88	0	NBC	Road
	2	Kopure	766	664	Oro Bay HC	Yes	29.08.25	417	142	237	237	09.09.25	1	1	0	0	0	NBC	Road
	3	Katereda H/C	158	110	Oro Bay HC	Yes	28.08.25	59	13	31	31	09.09.25	1	1	0	11	0	NBC	Road
	4	PNG Ports	46	414	Oro Bay HC	Yes	27.08.25	318	86	170	170	09.09.25	1	1	0	10	0	NBC	Road
	5	DPI Station	65	0	Oro Bay HC	Yes	26.08.25	58	15	28	28	09.09.25	1	1	0	9	0	NBC	Road

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
8		Baberada Village	1,993	1,697				1536	339	795	796		4	4	0	77	5		
	1	Baberada/Natatu	1,143	704	Oro Bay HC	Yes	27.08.25	580	115	304	302	09.09.25	1	1	0	40	0	NBC	Road
	2	Busega	567	609	Oro Bay HC	Yes	28.08.25	264	55	135	137	09.09.25	1	1	0	22	0	NBC	Road
	3	Arugasusu	173	114	Oro Bay HC	Yes	27.08.25	118	18	57	57	09.09.25	1	1	0	3	1	NBC	Road
	4	Eroro Com Sch	110	271	Oro Bay HC	Yes	27.08.25	574	151	299	300	09.09.25	1	1	0	12	4	NBC	Road
9		Dombada Village	2,401	2,447				1846	354	915	921		3	3	0	56	0		
	1	Domdaba	1,104	1,022	Oro Bay HC	Yes	25.08.25	774	181	388	390	07.09.25	1	1	0	35	0	NBC	Road
	2	Embogo	1,188	1,355	Oro Bay HC	Yes	26.08.25	1031	165	508	511	07.09.25	1	1	0	16	0	NBC	Road
	3	Embogo H Sch	108	70	Oro Bay HC	Yes	26.08.25	41	8	19	20	07.09.25	1	1	0	5	0	NBC	Road
10		Hanakiro Village	2,598	2,663				2474	584	1274	1276		7	7	0	74	0		
	1	Warisota	874	960	Oro Bay HC	Yes	26.08.25	695	149	344	344	07.09.25	1	1	0	43	0	NBC	Road
	2	Embi	408	272	Oro Bay HC	Yes	28.08.25	360	100	193	193	07.09.25	1	1	0	9	0	NBC	Road
	3	Hongarata	283	268	Oro Bay HC	Yes	26.08.25	246	50	119	119	07.09.25	1	1	0	4	0	NBC	Road
	4	Kurumbo	312	333	Oro Bay HC	Yes	27.08.25	324	68	163	163	07.09.25	1	1	0	3	0	NBC	Road
	5	Hanakiro	266	232	Oro Bay HC	Yes	27.08.25	234	50	116	118	07.09.25	1	1	0	3	0	NBC	Road
	6	Hanakiro 2	206	297	Oro Bay HC	Yes	27.08.25	308	67	152	152	07.09.25	1	1	0	2	0	NBC	Road
	7	Haugata	247	302	Oro Bay HC	Yes	26.08.25	307	100	187	187	07.09.25	1	1	0	10	0	NBC	Road
11		Kararata Village	1,923	5,509				5740	1301	2933	2927		8	8	0	483	15		
	1	Urio	387	1,206	Oro Bay HC	Yes	25.08.25	1036	215	542	538	06.09.25	1	1	0	76	0	NBC	Road
	2	Poro	199	640	Oro Bay HC	Yes	25.08.25	487	150	280	278	06.09.25	1	1	0	23	0	NBC	Road
	3	Hombariri	406	623	Oro Bay HC	Yes	25.08.25	822	172	420	420	06.09.25	1	1	0	129	0	NBC	Road
	4	Kararata	351	755	Oro Bay HC	Yes	25.08.25	707	149	372	372	06.09.25	1	1	0	22	9	NBC	Road
	5	Sori	168	309	Oro Bay HC	Yes	25.08.25	689	150	341	341	06.09.25	1	1	0	54	0	NBC	Road
	6	Guguma	315	621	Oro Bay HC	Yes	25.08.25	748	174	376	376	06.09.25	1	1	0	57	0	NBC	Road
	7	Embi Blocks	98	160	Oro Bay HC	Yes	25.08.25	224	50	114	114	06.09.25	1	1	0	26	6	NBC	Road
		Sambogo Estate		1,195	Oro Bay HC	Yes	25.08.25	1027	241	488	488	06.09.25	1	1	0	96	0	NBC	Road
12		Dobuduru Village	1,731	1,707				1913	380	945	949		4	4	0	54	0		
	1	Ango	471	582	Oro Bay HC	Yes	26.08.25	641	132	309	313	10.09.25	1	1	0	22	0	NBC	Road
	2	Dobuduru	367	371	Oro Bay HC	Yes	26.08.25	505	84	252	252	10.09.25	1	1	0	12	0	NBC	Road
	3	Penubata	122	208	Oro Bay HC	Yes	25.08.25	213	35	103	103	10.09.25	1	1	0	0	0	NBC	Road
	4	Parahe Block	771	545	Oro Bay HC	Yes	25.08.25	554	129	281	281	11.09.25	1	1	0	20	0	NBC	Road
13		Barisara Village	3,133	3,524				3373	724	1716	1718		5	5	0	155	38		
	1	Barisari	1,570	1,635	Oro Bay HC	Yes	25.08.25	1509	348	782	784	13.09.25	1	1	0	92	0	NBC	Road
	2	Garuro	653	718	Oro Bay HC	Yes	25.08.25	822	150	409	409	13.09.25	1	1	0	29	22	NBC	Road
	3	Hanao	247	193	Oro Bay HC	Yes	25.08.25	101	30	59	59	13.09.25	1	1	0	0	0	NBC	Road
	4	Sorodigari	252	485	Oro Bay HC	Yes	25.08.25	491	100	231	231	13.09.25	1	1	0	29	15	NBC	Road
	5	Tanese	411	492	Oro Bay HC	Yes	25.08.25	450	96	235	235	13.09.25	1	1	0	5	1	NBC	Road
14		Siremi Village	2,113	2,322				2135	384	1048	1050		5	5	0	20	2		
	1	Boreo	209	262	Oro Bay HC	Yes	28.08.25	215	37	108	110	10.09.25	1	1	0	5	2	NBC	Road
	2	Harigo	451	327	Oro Bay HC	Yes	27.08.25	474	86	230	230	10.09.25	1	1	0	0	0	NBC	Road
	3	Kendata	439	501	Oro Bay HC	Yes	27.08.25	410	72	199	199	10.09.25	1	1	0	6	0	NBC	Road
	4	Siremi	660	700	Oro Bay HC	Yes	28.08.25	628	127	319	319	10.09.25	1	1	0	7	0	NBC	Road
	5	Onagedataki	353	532	Oro Bay HC	Yes	27.08.25	408	62	192	192	10.09.25	1	1	0	2	0	NBC	Road
15		Buna Village	2,362	2,241				2218	382	1091	1104		2	2	0	82	11		
	1	Buna	1,294	1,468	Oro Bay HC	Yes	28.08.25	1286	220	619	629	11.09.25	1	1	0	41	11	NBC	Road
	2	Sanananda	1,068	773	Gona HC	Yes	28.08.25	932	162	472	475	10.09.25	1	1	0	41	0	NBC	Road
16		Killerton Village	1,316	990				549	140	298	298		2	1	0	9	0		
	1	Garara	216	173	Gona HC	Yes	28.08.25	191	48	101	101	10.09.25	1	0	0	3	0	Radio Northerr	Boat
	2	Killerton	663	381	Gona HC	Yes	27.08.25	358	92	197	197	10.09.25	1	1	0	6	0	Radio Northerr	Boat
	3	Bagou	437	436	Gona HC	Yes													Covered in Urban Ward 6
17		Otobejari Village	1,856	1,763				1539	372	848	848		7	2	0	63	14		
	1	Ononda	586	507	Gona HC	Yes	28.08.25	462	115	246	246	03.09.25	1	0	0	10	0	Radio Northerr	Road
	2	Sebu	214	112	Gona HC	Yes	27.08.25	123	29	68	68	04.09.25	1	0	0	2	0	Radio Northerr	Road
	3	Binjapada	312	193	Gona HC	Yes	27.08.25	225	65	140	140	03.09.25	1	1	0	10	8	Radio Northerr	Road
	4	Mumburada	507	526	Gona HC	Yes	28.08.25	347	86	193	193	03.09.25	1	1	0	31	4	Radio Northerr	Road
	5	Otobejari	38	309	Gona HC	Yes	28.08.25	243	50	130	130	04.09.25	1	0	0	7	2	Radio Northerr	Road
	6	Borida	70	116	Gona HC	Yes	28.08.25	95	19	49	49	04.09.25	1	0	0	2	0	Radio Northerr	Road
	7	Togorosusu	130	0	Gona HC	Yes	28.08.25	44	8	22	22	04.09.25	1	0	0	1	0	Radio Northerr	Road
18		Konje Village	1,585	1,164				1206	264	636	640		7	3	0	47	5		
	1	Konje	992	509	Gona HC	Yes	27.08.25	485	100	254	254	04.09.25	1	1	0	12	2	Radio Northerr	Road
	2	Bepore	384	55	Gona HC	Yes	28.08.25	70	10	31	33	09.09.25	1	0	0	2	0	Radio Northerr	Road
	3	Basabua	31	108	Gona HC	Yes	27.08.25	179	32	94	94	09.09.25	1	1	0	7	0	Radio Northerr	Road
	4	Banumo	103	84	Gona HC	Yes	28.08.25	79	27	42	42	09.09.25	1	0	0	4	0	Radio Northerr	Road
	5	Gombara	74	101	Gona HC	Yes	28.08.25	106	25	55	57	09.09.25	1	0	0	7	0	Radio Northerr	Road
		Saiwa		179	Gona HC	Yes	27.08.25	175	46	99	99	06.09.25	1	0	0	15	3	Radio Northerr	Road
		New Site		129	Gona HC	Yes	28.08.25	112	24	61	61	06.09.25	1	1	0	0	0	Radio Northerr	Road

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
19		Kausada Village	1,553	1,102				1113	281	597	603		3	3	0	49	5		
	1	Gona	420	227	Gona HC	Yes	28.08.25	173	41	92	96	07.09.25	1	1	0	13	5	Radio Northern	Road/Boat
	2	Kausada	778	510	Gona HC	Yes	27.08.25	537	142	288	288	06.09.25	1	1	0	23	0	Radio Northern	Road/Boat
	3	Napapo	355	365	Gona HC	Yes	28.08.25	403	98	217	219	07.09.25	1	1	0	13	0	Radio Northern	Road/Boat
20		Jinanga Village	1,073	1,067				894	184	464	469		4	4	0	23	1		
	1	Kurou	665	675	Gona HC	Yes	29.08.25	580	120	303	303	07.09.25	1	1	0	9	0	Radio Northern	Boat
	2	Jinanga	103	11	Gona HC	Yes	29.08.25	25	4	12	12	06.09.25	1	1	0	0	0	Radio Northern	Boat
	3	Saroda	144	187	Gona HC	Yes	28.08.25	191	41	99	104	06.09.25	1	1	0	3	1	Radio Northern	Boat
	4	Gona Ang Missn	161	193	Gona HC	Yes	29.08.25	98	19	50	50	06.09.25	1	1	0	11	0	Radio Northern	Boat
21		Bakubari Village	1,738	1,753				1751	380	917	917		3	2	0	27	18		
	1	Bakubari	891	838	Gona HC	Yes	28.08.25	840	174	439	439	05.09.25	1	1	0	15	10	Radio Northern	Boat
	2	Fufuda	557	753	Gona HC	Yes	28.08.25	762	166	400	400	04.09.25	1	1	0	10	6	Radio Northern	Road/Boat
	3	Urugari	290	162	Gona HC	Yes	27.08.25	149	40	78	78	05.09.25	1	0	0	2	2	Radio Northern	Boat
22		Batali	2,197	1,773				1580	256	854	854		3	1	0	0	0		
	2	Batari	355	383	Ambasi HC	Yes	07.10.25	349	56	188	188	07.10.25	1	1	0	0	0		Boat
	3	Katuna	1,116	870	Ambasi HC	Yes	07.10.25	795	128	420	420	08.10.25	1	0	0	0	0		Boat
		Kurereda	725	520	Ambasi HC	Yes	07.10.25	436	72	246	246	08.10.25	1	0	0	0	0		Boat
23		Oure Village	1,193	1,151				1022	197	514	514		4	0	0	0	0		
	1	Ope	142	325	Ambasi HC	Yes	02.10.25	311	50	153	153	04.10.25	1	0	0	0	0		Boat/Walk
	2	Jinena	173	207	Ambasi HC	Yes	02.10.25	168	36	90	90	04.10.25	1	0	0	0	0		Boat/Walk
	3	Koira (Beanga)	365	366	Ambasi HC	Yes	02.10.25	295	58	147	147	04.10.25	1	0	0	0	0		Boat/Walk
	4	Todinasi (Mora)	319	253	Ambasi HC	Yes	02.10.25	248	53	124	124	04.10.25	1	0	0	0	0		Boat/Walk
	5	Oure	194	0	Ambasi HC														Non Existant
24		Aure Village	1,925	1,352				1187	256	591	591		3	0	0	0	0		
	1	Aure	821	618	Ambasi HC	Yes	02.10.25	564	56	277	277	04.10.25	1	0	0	0	0		Boat/Walk
	2	Begabari	893	593	Ambasi HC	Yes	02.10.25	474	128	239	239	04.10.25	1	0	0	0	0		Boat/Walk
	3	Jitami/Waitutu	211	141	Ambasi HC	Yes	02.10.25	149	72	75	75	04.10.25	1	0	0	0	0		Boat/Walk
25		Dewatutu Village	1,913	1,491				1120	136	584	584		5	0	0	0	0		
	1	Ambasi	425	429	Ambasi HC	Yes	02.10.25	325	42	168	168	06.10.25	1	0	0	0	0		Boat
	2	Dewatutu	389	287	Ambasi HC	Yes	02.10.25	455	27	228	228	04.10.25	1	0	0	0	0		Walk
	3	Kainde	742	461	Ambasi HC	Yes	02.10.25	272	53	148	148	06.10.25	1	0	0	0	0		Boat/Walk
	4	Baretutu	142	210	Ambasi HC	Yes	02.10.25	0	0	0	0		1	0	0	0	0		Covered under Dewatutu
	5	Ambasi Station	216	104	Ambasi HC	Yes	02.10.25	68	14	40	40	06.10.25	1	0	0	0	0		Boat/Walk
26		Bindari Village	1,736	1,384				1179	190	600	600		4	0	0	0	0		
	1	Bindari	382	281	Ambasi HC	Yes	02.10.25	233	41	116	116	05.10.25	1	0	0	0	0		Boat
	2	Iwaie	816	691	Ambasi HC	Yes	02.10.25	651	94	325	325	05.10.25	1	0	0	0	0		Boat
	3	Ijina	235	175	Ambasi HC	Yes	02.10.25	127	28	66	66	05.10.25	1	0	0	0	0		Boat
	4	Taiya	302	237	Ambasi HC	Yes	02.10.25	168	27	93	93	05.10.25	1	0	0	0	0		Boat
				0															

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
Cape Nelson Rural			34,406	30,118				29,457	5,435	14,265	14,311		127	105	0	257	0	110	
1	Kewansasap Village		1,505	1,242				1138	204	543	543		3	3	0	0	0		
	1	Kewansasap	679	406	Wanigela HC	Yes	30.09.25	333	59	166	166	08.10.25	1	1	0	0	0	NBC	Boat
	2	Reaga	300	325	Wanigela HC	Yes	01.10.25	365	59	174	174	08.10.25	1	1	0	0	0	NBC	Boat
	3	Gegerawa	526	511	Wanigela HC	Yes	30.09.25	440	86	203	203	08.10.25	1	1	0		0	NBC	Boat
2	Marua Village		1,990	1,862				1766	287	887	887		6	6	0	0	0		
	1	Airara	495	228	Wanigela HC	Yes	30.09.25	378	61	191	191	08.10.25	1	1	0	0	0	NBC	Boat
	2	Marua No.2	264	191	Wanigela HC								1	1	0	0	0	NBC	Included Under Airara
	3	Sinapa	295	384	Wanigela HC	Yes	01.10.25	355	55	178	178	08.10.25	1	1	0	0	0	NBC	Boat
	4	Sinapara	509	357	Wanigela HC	Yes	01.10.25	343	57	170	170	08.10.25	1	1	0	0	0	NBC	Boat
	5	Koniasi	281	446	Wanigela HC	Yes	01.10.25	379	65	196	196	08.10.25	1	1	0	0	0	NBC	Boat
	6	Marua	146	256	Wanigela HC	Yes	01.10.25	311	49	152	152	08.10.25	1	1	0	0	0	NBC	Boat
3	Uiaku Village		1,200	853				745	114	369	369		1	0	0	0	0		
	1	Uiaku	1,200	853	Wanigela HC	Yes	01.10.25	745	114	369	369	07.10.25	1	0	0	0	0	NBC	Boat
4	Ganjiga Village		1,167	898				881	154	437	437		2	2	0	0	0		
	1	Ganjiga	754	547	Wanigela HC	Yes	30.09.25	515	90	252	252	07.10.25	1	1	0	0	0	NBC	Boat
	2	Yuaku	413	351	Wanigela HC	Yes	01.10.25	366	64	185	185	07.10.25	1	1	0	0	0	NBC	Boat
5	Rainu Village		3,707	3,038				3112	576	1417	1417		14	14	0	0	0		
	1	Komabun	257	140	Wanigela HC	Yes	30.09.25	126	19	59	59	06.10.25	1	1	0	0	0	NBC	Boat
	2	Oreosan	245	90	Wanigela HC	Yes	28.09.25	90	16	42	42	06.10.25	1	1	0	0	0	NBC	Boat
	3	Rainu	180	122	Wanigela HC	Yes	29.09.25	108	20	50	50	06.10.25	1	1	0	0	0	NBC	Boat
	4	Maffa	185	224	Wanigela HC	Yes	29.09.25	214	33	96	96	06.10.25	1	1	0	0	0	NBC	Boat
	5	Sarad Missn Statn	867	673	Wanigela HC	Yes	29.09.25	673	125	314	314	06.10.25	1	1	0	0	0	NBC	Boat
	6	Waiug	353	235	Wanigela HC	Yes	28.09.25	156	32	72	72	06.10.25	1	1	0	0	0	NBC	Boat
	7	Fofo	218	132	Wanigela HC	Yes	29.09.25	131	21	56	56	06.10.25	1	1	0	0	0	NBC	Boat
	8	Inaram	185	197	Wanigela HC	Yes	28.09.25	208	42	90	90	06.10.25	1	1	0	0	0	NBC	Boat
	9	Dirudadan	634	600	Wanigela HC	Yes	29.09.25	587	99	268	268	06.10.25	1	1	0	0	0	NBC	Boat
	10	Tekwakwan	115	59	Wanigela HC	Yes	28.09.25	76	15	34	34	06.10.25	1	1	0	0	0	NBC	Boat
	11	Utan Plantation	468	420	Wanigela HC	Yes	30.09.25	347	60	148	148	06.10.25	1	1	0	0	0	NBC	Boat
	12	Kikinu		146	Wanigela HC	Yes	01.10.25	125	22	61	61	06.10.25	1	1	0	0	0	NBC	Boat
	13	CUP 5 Camp		NEW	Wanigela HC	Yes	29.09.25	163	39	73	73	06.10.25	1	1	0	0	0	NBC	Boat
	14	Ginogi Camp		NEW	Wanigela HC	Yes	29.09.25	108	33	54	54	06.10.25	1	1	0	0	0	NBC	Boat
6	Koreaf Village		934	879				836	136	384	384		2	2	0	0	0		
	1	Koreaf	317	344	Wanigela HC	Yes	29.09.25	361	61	164	164	09.10.25	1	1	0	0	0	NBC	Boat
	2	Naukwate	617	536	Wanigela HC	Yes	29.09.25	475	75	220	220	06.10.25	1	1	0	0	0	NBC	Boat
7	Ajoa Village		1,719	1,279				1256	239	600	600		4	4	0	0	0		
	1	Ajoa	886	695	Wanigela HC	Yes	01.10.25	692	141	331	331	09.10.25	1	1	0	0	0	NBC	Boat
	2	Kikibator	214	160	Wanigela HC	Yes	01.10.25	188	31	86	86	09.10.25	1	1	0	0	0	NBC	Boat
	3	Ajoa Comm Sch	55	48	Wanigela HC	Yes							1	1	0	0	0	NBC	Comes under AJOA Village
	4	Kepple Point	564	377	Wanigela HC	Yes	01.10.25	376	67	183	183	09.10.25	1	1	0	0	0	NBC	Boat
8	Itoto Village		1,301	1,158				1057	175	511	511		3	3	0	0	0		
	1	Gigori	463	294	Wanigela HC	Yes	04.10.25	391	57	183	183	09.10.25	1	1	0	0	0	NBC	Boat
	2	Uwe	473	322	Wanigela HC	Yes	01.10.25	337	63	167	167	09.10.25	1	1	0	0	0	NBC	Boat
	3	Marakof	281	542	Wanigela HC	Yes	02.10.25	329	55	161	161	09.10.25	1	1	0	0	0	NBC	Boat
	4	Goiya	46	0	Wanigela HC	NAD													Not exist
	5	Uwe Comm Sch	38	0	Wanigela HC	NAD													Not exist
9	Giriwa Village		1,220	1,017				884	144	444	444		5	5	0	0	0		
	1	Kabubu	254	201	Wanigela HC	Yes	04.10.25	136	22	68	68	09.10.25	1	1	0	0	0	NBC	Boat
	2	Marasa	531	395	Wanigela HC	Yes	03.10.25	356	55	179	179	09.10.25	1	1	0	0	0	NBC	Boat
	3	Fanebara	182	237	Wanigela HC	Yes	02.10.25	213	33	103	103	09.10.25	1	1	0	0	0	NBC	Boat
	4	Itonomota	62	0	Wanigela HC														Non Existant
	5	Tomomon	50	51	Wanigela HC	Yes	02.10.25	53	9	26	26	09.10.25	1	1	0	0	0	NBC	Boat
	6	Kirakira	139	133	Wanigela HC	Yes	02.10.25	126	25	68	68	09.10.25	1	1	0	0	0	NBC	Boat
10	Managa Village		1,272	1,007				1007	178	505	506		8	6	0	87	0		
	1	Jubadi	74	51	Tufi HC	Yes	08.10.25	209	36	105	105	12.10.25	1	1	0	9	0	NBC	Boat
	2	Bibiyad	72	93	Tufi HC	Yes	09.10.25	100	16	50	50	12.10.25	1	1	0	0	0	NBC	Boat
	3	Jukuwataia	29	41	Tufi HC	0	0	0	0	0	0	0	1	0	0	0	0		Included Under Jubadi
	4	Managa	120	80	Tufi HC	Yes	08.10.25	96	17	48	49	12.10.25	1	1	0	0	0	NBC	Boat
	5	Sinifara	110	52	Tufi HC	Yes	09.10.25	47	9	24	24	12.10.25	1	1	0	0	0	NBC	Boat
	6	Siu	170	164	Tufi HC	Yes	08.10.25	274	50	137	137	12.10.25	1	1	0	37	0	NBC	Boat
	7	Utukwafu	612	450	Tufi HC	Yes	08.10.25	281	50	141	141	12.10.25	1	1	0	41	0	NBC	Boat
	8	Kuna	84	75	Tufi HC	0	0	0	0	0	0	0	1	0	0	0	0		Included Under Jubadi
11	Jebo Village		1,841	1,302				1237	228	618	635		5	5	0	71	0		
	1	Barabara	341	192	Tufi HC	Yes	07.10.25	195	42	96	96	10.10.25	1	1	0	15	0	NBC	Boat
	2	Bauwame	391	193	Tufi HC	Yes	07.10.25	180	35	90	97	09.10.25	1	1	0	21	0	NBC	Boat
	3	Jebo	312	276	Tufi HC	Yes	07.10.25	298	55	149	155	13.10.25	1	1	0	2	0	NBC	Boat
	4	Orotoaba	387	343	Tufi HC	Yes	08.10.25	307	49	154	154	13.10.25	1	1	0	0	0	NBC	Boat
	5	Tainabuna	411	298	Tufi HC	Yes	07.10.25	257	47	129	133	09.10.25	1	1	0	33	0	NBC	Boat

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
12	Baga	Village	1,568	1,163				952	184	477	480		9	5	0	62	0		
	1	Baga	533	348	Tufi HC	Yes	07.10.25	251	50	126	126	10.10.25	1	1	0	21	0	NBC	Boat
	2	Kabuni	194	133	Tufi HC	Yes	07.10.25	188	35	94	94	10.10.25	1	1	0	0	0	NBC	Boat
	3	Karikari	170	78	Tufi HC								1						Included Under Kabuni
	4	Konabu	67	81	Tufi HC								1						Included Under Kuriraka
	5	Leilioa	120	120	Tufi HC	Yes	08.10.25	182	32	91	91	10.10.25	1	1	0	16	0	NBC	Boat
	6	Goodenough	130	70	Tufi HC								1						Included Under Leilioa
	7	Mano	36	69	Tufi HC								1						Included Under Komoa
	8	Komoa	214	175	Tufi HC	Yes	08.10.25	167	36	84	84	10.10.25	1	1	0	19	0	NBC	Boat
	9	Kuririka	103	90	Tufi HC	Yes	08.10.25	164	31	82	85	10.10.25	1	1	0	6	0	NBC	Boat
13	Kwave	Village	1,128	893				886	200	446	446		7	5	0	0	0		
	1	Iagirua	192	96	Tufi HC	Yes	07.10.25	203	53	103	103	09.10.25	1	1	0	0	0	NBC	Boat
	2	Koje	454	414	Tufi HC	Yes	07.10.25	354	75	177	177	10.10.25	1	1	0	0	0	NBC	Boat
	3	Konedobu	65	17	Tufi HC								1						Included Under Iagirua
	4	Kwave	60	39	Tufi HC								1						Included Under Iagirua
	5	Rabade	86	104	Tufi HC	Yes	07.10.25	73	18	37	37	11.10.25	1	1	0	0	0	NBC	Boat
	6	Natade	94	110	Tufi HC	Yes	09.10.25	113	24	57	57	11.10.25	1	1	0	0	0	NBC	Boat
	7	Kofure	178	113	Tufi HC	Yes	07.10.25	143	30	72	72	11.10.25	1	1	0	0	0	NBC	Boat
14	Sefoa	Village	1,224	793				773	132	388	394		8	4	0	6	0		
	1	Bekoiana	161	64	Tufi HC								1						Included Under Foduma No.1
	2	Foduma	137	74	Tufi HC	Yes	07.10.25	263	44	132	132	10.10.25	1	1	0	6	0	NBC	Boat
	3	Kanavetu	163	139	Tufi HC	Yes	07.10.25	138	20	69	74	10.10.25	1	1	0	0	0	NBC	Boat
	4	Kasiawa	209	128	Tufi HC	Yes	07.10.25	169	27	85	86	10.10.25	1	1	0	0	0	NBC	Boat
	5	Kikita	46	35	Tufi HC								1						Included Under Foduma No.1
	6	Foduma No.2	168	98	Tufi HC								1						Included Under Foduma No.1
	7	Jojo	221	166	Tufi HC								1						Included Under Sefoa Mission Stn
	8	Sefoa Mission Stn	120	89	Tufi HC	Yes	07.10.25	203	41	102	102	10.10.25	1	1	0	0	0	NBC	Boat
15	Sinei	Village	1,952	1,814				1737	314	872	885		7	7	0	28	0		
	1	Givide	235	153	Tufi HC	Yes	08.10.25	159	24	79	86	12.10.25	1	1	0	0	0	NBC	Boat
	2	Kato Kato	139	186	Tufi HC	Yes	08.10.25	172	31	86	86	11.10.25	1	1	0	0	0	NBC	Boat
	3	Koruwe	290	340	Tufi HC	Yes	08.10.25	289	50	145	145	11.10.25	1	1	0	0	0	NBC	Boat
	4	Kwafurinai/Kwapulina	408	337	Tufi HC	Yes	10.10.25	330	57	166	166	12.10.25	1	1	0	5	0	NBC	Boat
	5	Sinei	187	179	Tufi HC	Yes	08.10.25	183	43	93	96	11.10.25	1	1	0	23	0	NBC	Boat
	6	Teniaru	245	243	Tufi HC	Yes	08.10.25	217	44	109	111	11.10.25	1	1	0	0	0	NBC	Boat
	7	Tumari	447	376	Tufi HC	Yes	08.10.25	387	65	194	195	11.10.25	1	1	0	0	0	NBC	Boat
16	Berebona	Villages 1 & 2	1,613	1,506				1488	303	721	721		9	5	0	0	0		
	1	Angorogo	245	180	Ako HC	Yes	02.10.25	192	38	95	95	08.10.25	1	1	0	0	0	NBC	Boat
	2	Bambiti	120	167	Ako HC	Yes	02.10.25	196	34	93	93	08.10.25	1	1	0	0	0	NBC	Boat
	3	Berebona 1 & 2	545	496	Ako HC	Yes	02.10.25	463	106	227	227	08.10.25	1	1	0	0	0	NBC	Boat
	4	Fofoma	110	300	Ako HC	Yes	02.10.25	226	47	107	107	08.10.25	1	1	0	0	0	NBC	Boat
	5	Founa	286	363	Ako HC	Yes	02.10.25	411	78	199	199	08.10.25	1	1	0	0	0	NBC	Boat
	6	Ilamaroro	58	0	Ako HC								1						Boat
	7	Kaparuru	67	0	Ako HC								1						Boat
	8	Natukwabo	144	0	Ako HC								1						Boat
	9	Berebona	38	0	Ako HC								1						Boat
17	Ako	Village	2,473	2,688				2227	503	1173	1173		8	8	0	0	0		
	1	Ako	521	543	Ako HC	Yes	02.10.25	494	100	252	252	13.10.25	1	1	0	0	0	NBC	Boat
	2	Gobe	420	477	Ako HC	Yes	02.10.25	415	85	204	204	11.10.25	1	1	0	0	0	NBC	Boat
	3	Kuruaku	187	197	Ako HC	Yes	02.10.25	194	34	94	94	11.10.25	1	1	0	0	0	NBC	Boat
	4	Mafuia	370	283	Ako HC	Yes	02.10.25	282	59	130	130	11.10.25	1	1	0	0	0	NBC	Boat/Trek
	5	Tumina	89	146	Ako HC	Yes	02.10.25	175	34	85	85	13.10.25	1	1	0	0	0	NBC	Boat
	6	Oropu	199	134	Ako HC	Yes	02.10.25	191	37	96	96	11.10.25	1	1	0	0	0	NBC	Boat/Trek
	7	Monganai	394	549	Ako HC	Yes	02.10.25	251	111	204	204	16.10.25	1	1	0	0	0	NBC	Boat/Trek
	8	Gave	233	358	Ako HC	Yes	02.10.25	225	43	108	108	11.10.25	1	1	0	0	0	NBC	Boat/Trek
	9	Mongana Com Sch	36	0	Ako HC														Non Existant
	10	Ako Com Sch	24	0	Ako HC														Non Existant
18	Foru	Village	1,957	2,021				2450	448	1182	1182		8	8	0	0	0		
	1	Bendorode	197	288	Ako HC	Yes	03.10.25	265	45	128	128	09.10.25	1	1	0	0	0	NBC	Boat
	2	Foru No. 1	468	383	Ako HC	Yes	03.10.25	385	72	193	193	14.10.25	1	1	0	0	0	NBC	Boat
	3	Foru No. 2	403	399	Ako HC	Yes	03.10.25	262	55	131	131	14.10.25	1	1	0	0	0	NBC	Boat
	4	Boruba		NEW	Ako HC	Yes	03.10.25	573	103	270	270	15.10.25	1	1	0	0	0	NBC	
	5	Erika	259	249	Ako HC	Yes	03.10.25	243	39	106	106	11.10.25	1	1	0	0	0	NBC	Boat
	6	Sayio	125	0	Ako HC														Non Existant
	7	Karesovu	156	208	Ako HC	Yes	03.10.25	237	27	112	112	11.10.25	1	1	0	0	0	NBC	Boat
	8	Sebaga	348	325	Ako HC	Yes	03.10.25	352	84	172	172	09.10.25	1	1	0	0	0	NBC	Boat
	9	Jobu	New	169	Ako HC	Yes	03.10.25	133	23	70	70	10.10.25	1	1	0	0	0	NBC	Boat

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
19		Karaisa Village	1,546	1,456				1832	315	891	892		5	5	0	3	0		
	1	Badaide	130	143	Ako HC	Yes	04.10.25	134	22	70	70	10.10.25	1	1	0	0	0	NBC	Boat
	2	Karaisa	509	575	Oro Bay HC2	Yes	07.09.25	741	126	372	373	19.09.25	1	1	0	3	0	NBC	Boat
	3	Goworode	206	202	Ako HC	Yes	04.10.25	156	37	88	88	10.10.25	1	1	0	0	0	NBC	Boat
	4	Goworode 2	120	0	Ako HC														Non Existant
	5	Moiavi	168	215	Ako HC	Yes	04.10.25	276	50	139	139	10.10.25	1	1	0	0	0	NBC	Boat
	6	Momoioogo	307	320	Ako HC	Yes	04.10.25	525	80	222	222	15.10.25	1	1	0	0	0	NBC	Boat/Trek
	7	Koipade	106	0	Ako HC														Non Existant
20		Kinjaki Village	823	765				566	135	293	293		4	0	0	0	0		
	1	Kinjaki	387	315	Oro Bay HC2	Yes	05.09.25	265	62	137	137	13.09.25	1	0	0	0	0	NBC	Road/Boat/Treking
	2	Korara	190	162	Oro Bay HC2	Yes	05.09.25	161	35	82	82	13.09.25	1	0	0	0	0	NBC	Road/Boat/Treking
	3	Babaru	74	149	Oro Bay HC2	Yes	05.09.25	46	16	27	27	13.09.25	1	0	0	0	0	NBC	Road/Trek
	4	Botewari	173	140	Oro Bay HC2	Yes	04.09.25	94	22	47	47	13.09.25	1	0	0	0	0	NBC	Road/Boat/Treking
21		Guruguru Village	499	656				617	105	270	270		3	3	0	0	0		
	1	Budorode	146	157	Ako HC	Yes	04.10.25	100	21	47	47	15.10.25	1	1	0	0	0	NBC	Boat/Trek
	2	Guruguru	228	499	Ako HC	Yes	04.10.25	291	47	133	133	15.10.25	1	1	0	0	0	NBC	Boat
	3	Kummoware	125	0	Ako HC	Yes	04.10.25	226	37	90	90	15.10.25	1	1	0	0	0	NBC	Boat/Trek
22		Embessa Village	1,066	1,216				1506	279	585	585		4	4	0	0	0		
	1	Embesa	598	630	Ako HC	Yes	05.10.25	751	148	300	300	15.10.25	1	1	0	0	0	NBC	Boat/Trek
	2	Kakasa	106	164	Ako HC	Yes	05.10.25	309	48	103	103	15.10.25	1	1	0	0	0	NBC	Boat/1 Hr Trek
	3	Taruma	137	292	Ako HC	Yes	05.10.25	270	48	100	100	15.10.25	1	1	0	0	0	NBC	Boat/30m Trek
	4	Musasa	226	131	Ako HC	Yes	05.10.25	176	35	82	82	15.10.25	1	1	0	0	0	NBC	Boat/Trek
23		Tufi Government Station	699	615				504	82	252	257		2	1	0	0	0		
	1	Tufi Govt Station	266	330	Tufi HC	Yes	08.10.25	504	82	252	257	10.10.25	1	1	0	0	0	NBC	Boat
	2	Tufi Govt Station	432	285	Tufi HC								1						Covered under Tufi Gov Stn 1
				0															

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
Afore Rural			33,213	27,457				21,907	3,814	10,908	10,925		71	61	0	622	11	72	
1	Yoivi Village		2,571	2,242				2109	418	1066	1067		9	9	0	34	11		
	1 Bua		233	91	Afore HC	Yes	02.10.25	87	15	43	43	09.10.25	1	1	0	0	0	NBC	Road
	2 Marasi		696	642	Afore HC	Yes	30.09.25	589	120	298	298	10.10.25	1	1	0	3	0	NBC	Road/Trek
	3 Ondoro		178	248	Afore HC	Yes	30.09.25	209	47	98	98	07.10.25	1	1	0	6	1	NBC	Road
	4 Yoivi		516	304	Afore HC	Yes	30.09.25	287	52	146	147	10.10.25	1	1	0	4	0	NBC	Road/Trek
	5 Umbara		305	213	Afore HC	Yes	02.10.25	143	36	76	76	10.10.25	1	1	0	1	1	NBC	Road/Trek
	6 Manusi		394	353	Afore HC	Yes	30.09.25	378	65	187	187	10.10.25	1	1	0	4	1	NBC	Road
	7 Damaral		130	217	Afore HC	Yes	02.10.25	148	25	78	78	10.10.25	1	1	0	3	5	NBC	Road
	8 Bioil		120	102	Afore HC	Yes	01.10.25	132	27	70	70	10.10.25	1	1	0	5	2	NBC	Road/Trek
	9 New Area			72	Afore HC	Yes	30.09.25	136	31	70	70	10.10.25	1	1	0	8	1	NBC	Road/Trek
2	Ninuiiri Village		2,504	1,803				1837	326	919	920		8	7	0	91	0		
	1 Afore		264	322	Afore HC	Yes	30.09.25	263	56	136	136	10.10.25	1	1	0	8		NBC	Road
	2 Niniuri		127	89	Afore HC	Yes	30.09.25	75	13	40	40	10.10.25	1	1	0	1	0	NBC	Road
	3 Semahara		245	197	Afore HC	Yes	30.09.25	198	44	94	94	10.10.25	1	1	0	9	0	NBC	Road/Trek
	4 Korokoro		101	93	Afore HC	Yes	30.09.25	101	17	51	52	10.10.25	1	1	0	2	0	NBC	Road/Trek
	5 Afore Blocks		499	332	Afore HC	Yes	30.09.25	357	60	178	178	09.10.25	1	1	0	17	0	NBC	Road
	6 Ogan 1		108	246	Afore HC	Yes	30.09.25	234	38	117	117	10.10.25	1	1	0	7	0	NBC	Road
	7 Ogan 2		146	0	Afore HC														Non Existant
	8 Basape		254	237	Afore HC	Yes	30.09.25	319	58	156	156	10.10.25	1	1	0	11	0	NBC	Road/Trek
	9 Afore Govt Station		451	287	Afore HC	Yes	30.09.25	290	40	147	147	10.10.25	1		0	36	0	NBC	Road
	10 Boikiki Plantaion		307	0	Afore HC														Non Existant
3	Kawowoki Village		1,064	1,099				1213	200	570	570		2	2	0	28	0		
	1 Kawowoki		1,064	763	Afore HC	Yes	30.09.25	849	137	396	396	10.10.25	1	1	0	19	0	NBC	Road
	Dareki			336	Afore HC	Yes	30.09.25	364	63	174	174	10.10.25	1	1	0	9	0	NBC	Road
4	Kaura Village		1,724	1,355				1256	220	609	609		2	2	0	49	0		
	1 Awaru		778	660	Sakarina HC	Yes	01.10.25	602	111	289	289	16.10.25	1	1	0	13	0	NBC	Road
	2 Kaura		946	695	Sakarina HC	Yes	01.10.25	654	109	320	320	14.10.25	1	1	0	36	0	NBC	Road
5	Siuarani Village		1,815	1,451				1354	251	665	665		3	3	0	41	0		
	1 Wumba/Siyurana		1,815	1,196	Sakarina HC	Yes	01.10.25	1081	198	530	530	14.10.25	1	1	0	34		NBC	Road
	Sigara			155	Sakarina HC	Yes	02.10.25	152	28	75	75	14.10.25	1	1	0	5		NBC	Trek
	Siana			100	Sakarina HC	Yes	02.10.25	121	25	60	60	14.10.25	1	1	0	2	0	NBC	Trek
6	Kowena Village		1,949	1,593				1877	300	940	941		3	3	0	61	0		
	1 Kwen0		1,361	1,067	Sakarina HC	Yes	01.10.25	1294	191	634	634	10.10.25	1	1	0	24	0	NBC	Road
	2 Sila		435	349	Sakarina HC	Yes	02.10.25	376	69	198	199	13.10.25	1	1	0	16		NBC	Road
	3 Yumara		38	0	Sakarina HC														Non Existant
	4 Sakarina Mission Station		115	177	Sakarina HC	Yes	01.10.25	207	40	108	108	11.10.25	1	1	0	21	0	NBC	Road
7	Dea Village		2,358	1,885				1927	327	936	939		4	4	0	62	0		
	1 Dea		610	465	Sakarina HC	Yes	01.10.25	568	91	276	276	13.10.25	1	1	0	16		NBC	Road
	2 Tabuane		920	772	Sakarina HC	Yes	01.10.25	710	128	338	338	13.10.25	1	1	0	25	0	NBC	Road
	3 Ugunomo		768	521	Sakarina HC	Yes	02.10.25	550	91	273	275	13.10.25	1	1	0	12	0	NBC	Road
	4 Dea Comm School		60	128	Sakarina HC	Yes	01.10.25	99	17	49	50	13.10.25	1	1	0	9	0	NBC	Road
8	Siribu Village		1,049	1,023				820	133	400	403		1	1	0	27	0		
	1 Sirubu		1,049	1,023	Sakarina HC	Yes	02.10.25	820	133	400	403	13.10.25	1	1	0	27	0	NBC	Road
9	Natanga Village		1,945	1,491				1395	224	693	693		4	4	0	32	0		
	1 Kiara		571	451	Sakarina HC	Yes	02.10.25	358	68	176	176	13.10.25	1	1	0	6		NBC	Air/Trek
	2 Natanga		771	512	Sakarina HC	Yes	03.10.25	545	82	272	272	13.10.25	1	1	0	4		NBC	Air/Trek
	3 Jorura		557	451	Sakarina HC	Yes	03.10.25	424	62	212	212	14.10.25	1	1	0	19		NBC	Air/Trek
	4 Kajo		46	77	Sakarina HC	Yes	03.10.25	68	12	33	33	20.10.25	1	1	0	3	0	NBC	Air/Trek
10	Gora Village		1,604	1,431				1220	216	616	617		3	2	0	8	0		
	1 Gora		499	488	Sakarina HC	Yes	01.10.25	595	91	291	291	13.10.25	1	1	0	8		NBC	Air/Trek
	2 Gorabuna		555	458	Sakarina HC	Yes	11.10.25	485	100	254	254	13.10.25	1	0	0	0	0	NBC	Air/Trek
	3 Kero		278	486	Sakarina HC	Yes	04.10.25	140	25	71	72	20.10.25	1	1	0	0	0	NBC	Air/Trek
	4 Gora Comm School		271	0	Sakarina HC														Non Existant
11	Tahama Village		1,676	1,288				1322	194	664	664		4	4	0	69	0		
	1 Koruwo		559	477	Itokama HC	Yes	04.10.25	583	80	296	296	21.10.25	1	1	0	40	0	NBC	Road
	2 Tahama		730	534	Itokama HC	Yes	07.10.25	540	85	268	268	21.10.25	1	1	0	20	0	NBC	Road
	3 Jawaee		130	68	Itokama HC	Yes	04.10.25	64	8	33	33	21.10.25	1	1	0	0	0	NBC	Road
	4 Kaivitama		158	143	Itokama HC	Yes	10.10.25	135	21	67	67	21.10.25	1	1	0	9	0	NBC	Road
	5 Bareji		98	67	Itokama HC														Non Existant
12	Umborora Village		1,717	1,437				1359	244	700	702		7	7	0	29	0		
	1 Umbuwara		365	278	Itokama HC	Yes	05.10.25	252	36	122	122	22.10.25	1	1	0	0	0	NBC	Air/Trek
	2 Sagamaisa (Samasi)		223	120	Itokama HC	Yes	04.10.25	149	29	72	72	22.10.25	1	1	0	9	0	NBC	Air/Trek
	3 Araforo		137	157	Itokama HC	Yes	04.10.25	127	24	65	65	22.10.25	1	1	0	8	0	NBC	Air/Trek
	4 Dudoim		226	203	Itokama HC	Yes	04.10.25	199	38	110	110	22.10.25	1	1	0	12	0	NBC	Air/Trek
	5 Anatua 1		132	273	Itokama HC	Yes	05.10.25	240	46	130	130	22.10.25	1	1	0	0	0	NBC	Air/Trek
	6 Anatua 2		295	100	Itokama HC	Yes	05.10.25	110	18	55	57	22.10.25	1	1	0	0	0	NBC	Air/Trek
	7 Gazot		339	306	Itokama HC	Yes	05.10.25	282	53	146	146	22.10.25	1	1	0	0	0	NBC	Air/Trek

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
13	Kokoro Village		1,299	875				864	155	442	444		6	6	0	38	0		
	1	Kokoro	312	244	Itokama HC	Yes	03.10.25	195	36	104	104	22.10.25	1	1	0	13	0	NBC	Air/Trek
	2	Kuai	353	180	Itokama HC	Yes	04.10.25	175	33	87	89	22.10.25	1	1	0	9	0	NBC	Air/Trek
	3	Serepuna	322	235	Itokama HC	Yes	05.10.25	194	38	97	97	22.10.25	1	1	0	0	0	NBC	Air/Trek
	4	Nizui	67	83	Itokama HC	Yes	03.10.25	167	24	87	87	22.10.25	1	1	0	8	0	NBC	Air/Trek
	5	Nibaeba	110	39	Itokama HC	Yes	03.10.25	33	8	17	17	22.10.25	1	1	0	1	0	NBC	Air/Trek
	6	Buabufu	101	94	Itokama HC	Yes	05.10.25	100	16	50	50	22.10.25	1	1	0	7	0	NBC	Air/Trek
	7	Siriafe	34	0	Itokama HC														Non Existant
14	Ufia Village		1,798	1,297				1172	210	609	609		4	4	0	39	0		
	1	Itokama	915	653	Itokama HC	Yes	03.10.25	592	103	300	300	22.10.25	1	1	0	15	0	NBC	Air
	2	Ufia	233	174	Itokama HC	Yes	05.10.25	160	25	86	86	22.10.25	1	1	0	10	0	NBC	Air/Trek
	3	Umuwate	216	175	Itokama HC	Yes	05.10.25	143	28	76	76	21.10.25	1	1	0	4	0	NBC	Air/Trek
	4	Naukuanane	435	295	Itokama HC	Yes	04.10.25	277	54	147	147	21.10.25	1	1	0	10	0	NBC	Air/Trek
15	Tomal Village		1,558	1,601				1724	316	842	843		6	0	0	6	0		
	1	Gewoia	358	492	Afore HC	Yes	04.10.25	402	66	198	198	10.10.25	1	0	0	1	0	NBC	Road/Trek
	2	Toma	55	334	Afore HC	Yes	01.10.25	368	69	174	174	07.10.25	1	0	0	0	0	NBC	Trek
	3	Orara	106	94	Afore HC	Yes	05.10.25	74	16	36	36	12.10.25	1	0	0	0	0	NBC	Road/Trek
	4	Manana	250	227	Afore HC	Yes	04.10.25	218	37	105	106	12.10.25	1	0	0	0	0	NBC	Road/Trek
	5	Bariri	648	312	Afore HC	Yes	01.10.25	256	56	129	129	07.10.25	1	0	0	5	0	NBC	Trek
	6	Babarobo	142	142	Afore HC	Yes	05.10.25	406	72	200	200	12.10.25	1	0	0	0	0	NBC	Road/Trek
16	Airi Village		286	204				195	32	104	104		1	0	0	4	0	NBC	
	1	Aiari	286	204	Itokama HC	Yes	04.10.25	195	32	104	104	22.10.25	1	0	0	4	0	NBC	Trek
17	Yaure Village		483	299				263	48	133	135		4	3	0	4	0		
	1	Yaure	228	92	Itokama HC	Yes	05.10.25	97	16	49	49	21-23.10.25	1					NBC	Trek
	2	Suwari	122	65	Itokama HC	Yes	05.10.25	54	12	27	27	21-23.10.25	1	1	0	2	0	NBC	Trek
	3	Baratana	74	84	Itokama HC	Yes	04.10.25	80	13	38	40	21-23.10.25	1	1	0	0	0	NBC	Trek
	4	Anei	58	58	Itokama HC	Yes	05.10.25	32	7	19	19	21-23.10.25	1	1	0	2	0	NBC	Trek
18	Namundi Village		711	587															
	1	Sibia	247	216	Safia HC														Air/Trek
	2	Namundi	351	339	Safia HC														Air/Trek
	3	Marude	113	31	Safia HC														Air/Trek
19	Sinua Village		682	446															
	1	Awala (Kaera)	120	143	Safia HC														Air/Trek
	2	Sinua (Moikodi)	158	84	Safia HC														Air/Trek
	3	Part Imuwake	175	54	Safia HC														Air/Trek
	4	Liana (Omudi)	134	93	Safia HC														Air/Trek
	5	Ariari (Baruwake)	94	71	Safia HC														Air/Trek
20	Moro Village		1,313	1,623															
	1	Koira	300	437	Safia HC														Air/Trek
	2	Moro (Urodi)	293	230	Safia HC														Air/Trek
	3	Umauma	161	208	Safia HC														Air/Trek
	4	Urumbai (Uriobo)	218	134	Safia HC														Air/Trek
	5	Fiodubo	110	118	Safia HC														Air/Trek
	6	Oure	65	126	Safia HC														Air/Trek
	7	Dibau	166	155	Safia HC														Air/Trek
	8	Asanga		215	Safia HC														Air/Trek
21	Jari Village		804	610															
	1	Kasirawa No.2	86	84	Safia HC														Air/Trek
	2	Aimare	192	101	Safia HC														Air/Trek
	3	Auwake (Douwa 2)	146	60	Safia HC														Air/Trek
	4	Vovosi	199	45	Safia HC														Air/Trek
	5	Doma	89	160	Safia HC														Air/Trek
	6	Boinono	91	93	Safia HC														Air/Trek
		Jari		67	Safia HC														Air/Trek
22	Tutuwarawu Village		444	387															
	1	Bibira No.2	247	200	Safia HC														Air/Trek
	2	Fonotaima (Yauri)	197	187	Safia HC														Air/Trek
23	Safia Village		960	813															
	1	Bibira No.1	214	198	Safia HC														Air/Trek
	2	Domara	187	164	Safia HC														Air/Trek
	3	Safia	353	269	Safia HC														Air/Trek
	4	Bare	146	113	Safia HC														Air/Trek
	5	Waira	60	68	Safia HC														Air/Trek
24	Obea Village		900	618															
	1	Obea	487	230	Safia HC														Air/Trek
	2	Silididi	158	159	Safia HC														Air/Trek
	3	Ubo	168	143	Safia HC														Air/Trek
	4	Abuabi	86	86	Safia HC														Air/Trek

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
				0															

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
Popondetta Urban			47,694	57,238				56,462	10,499	28,505	28,591		67	67	67	3,986	1,908	67	
1	Gewoto		6,304	6,973				5333	987	2674	2674		9	9	9	627	549		
		Higa st Sect 22	691	383	PHA	Yes	21.08.25	265	50	131	128	09.09.25	1	1	1	17	16	90.7 FM	Road
		Boruga Plaza Sect 1/12	53	0	PHA														Closed
		Popondo Avenue sect 2/4	715	837	PHA	Yes	21.08.25	823	113	427	427	10.09.25	1	1	1	100	100	90.7 FM	Road
		Koropa Crescent sect 2/7	543	412	PHA	Yes	21.08.25	323	48	170	170	09.09.25	1	1	1	50	50	90.7 FM	Road
		Bangoho Creek	670	1,269	PHA	Yes	21.08.25	1556	352	778	779	09.09.25	1	1	1	173	157	90.7 FM	Road
		Bangoho Camp	197	0	PHA														Closed
		Sesenaga/Osari St Sect(3/5)	1,047	1,365	PHA	Yes	21.08.25	535	85	274	274	09.09.25	1	1	1	99	99	90.7 FM	Road
		Gasara st Sect 8/52	459	0	PHA														Closed
		New Guinea Compound	874	1,935	PHA	Yes	22.08.25	1052	219	513	514	09.09.25	1	1	1	107	98	90.7 FM	Road
		Waria Compund	408	529	PHA	Yes	22.08.25	197	33	96	97	10.09.25	1	1	1	15	0	90.7 FM	Road
		Street: Christopher Station	216	0	PHA	Yes	01.09.25	257	35	132	132	09.09.25	1	1	1	37	0	90.7 FM	Road
		Garaina Compund	139	0	PHA														Closed
		Manus/Tufi/Raikos Compund	293	243	PHA	Yes	21.08.25	325	52	153	153	10.09.25	1	1	1	29	29	90.7 FM	Road
2	Sewa		845	2,500				3684	563	1838	1842		2	2	2	390	326		
		Popndtta Gen Hospital Area	178	1,772	PHA	Yes	21.08.25	3294	492	1636	1640	08.09.25	1	1	1	386	322	90.7 FM	Road
		Hongori Avenue Sect 18-20/	667	728	PHA	Yes	21.08.25	390	71	202	202	08.09.25	1	1	1	4	4	90.7 FM	Road
3	Isuga		7,574	6,156				6515	977	3190	3169		8	8	8	546	255		
		Isivi St	1,001	926	PHA	Yes	21.08.25	770	122	380	378	09.09.25	1	1	1	93	70	90.7 FM	Road
		Hira St (51)	322	0	PHA														Closed
		Penderata St Sect(53/54/55/	965	653	PHA	Yes	21.08.25	904	132	449	440	09.09.25	1	1	1	110	91	90.7 FM	Road
		Barevo Ave Sect(59/60)	1,260	2,231	PHA	Yes	25.08.25	1961	346	933	917	09.09.25	1	1	1	103	10	90.7 FM	Road
		Police Barracks	401	313	PHA	Yes	28.08.25	277	50	130	130	09.09.25	1	1	1	47	2	90.7 FM	Road
		Kaperi St. Popndtta Sch Area	689	503	PHA	Yes	21.08.25	1156	140	575	577	09.09.25	1	1	1	64	7	90.7 FM	Road
		Goruta st Sect 51	1,092	483	PHA	Yes	22.08.25	486	62	236	237	09.09.25	1	1	1	58	58	90.7 FM	Road
		Pandanus st sect 56-59	1,229	1,047	PHA	Yes	24.08.25	720	85	376	376	09.09.25	1	1	1	71	17	90.7 FM	Road
		Niusagere Village	615	0	PHA														Closed
		Golf		NEW	PHA	Yes	05.09.25	241	40	111	114	09.09.25	1	1	1			90.7 FM	Road
4	Dobuduro		2,002	1,948				984	150	505	505		2	2	2	158	158		
		Warisota StSect(23/29)	629	1,875	PHA	Yes	26.08.25	755	113	381	381	06.09.25	1	1	1	123	123	90.7 FM	Road
		Jirih St sect 24-28	951	0	PHA														Closed
		DPI Station & Setlemnt	423	73	PHA	Yes	26.08.25	229	37	124	124	06.09.25	1	1	1	35	35	90.7 FM	Road
5	Sorovi		4,732	3,144				3506	565	1790	1792		4	4	4	383	242		
		SBS Uni Compound	1,131	1,163	PHA	Yes	21.08.25	1491	235	770	768	08.09.25	1	1	1	190	55	90.7 FM	Road
		Kakendetta	442	0	PHA														Closed
		Cu 605	12	0	PHA														Closed
		Kainantu Compund	1,092	807	PHA	Yes	21.08.25	1116	179	571	575	08.09.25	1	1	1	108	107	90.7 FM	Road
		Uni of Vudal (Oro Campus)	1,040	794	PHA	Yes	21.08.25	652	104	328	328	06.09.25	1	1	1	42	42	90.7 FM	Road
		Elcom Compound	170	0	PHA														Closed
		Biru: CIS area	845	380	PHA	Yes	25.08.25	247	47	121	121	03.09.25	1	1	1	43	38	90.7 FM	Road
6	East Embogo		3,378	2,979				3403	689	1811	1902		8	8	8	139	40		
		Gewoto	514	483	PHA	Yes	20.08.25	419	91	283	229	03.09.25	1	1	1	16	10	90.7 FM	Road
		Kapurahambo	379	285	PHA	Yes	21.08.25	248	50	140	140	03.09.25	1	1	1	10	3	90.7 FM	Road
		Soputa	658	880	PHA	Yes	20.08.25	698	128	212	357	03.09.25	1	1	1	16	5	90.7 FM	Road
		Kikonda	751	215	PHA	Yes	20.08.25	157	44	86	86	03.09.25	1	1	1	9	3	90.7 FM	Road
		Anzerita	324	193	PHA	Yes	22.08.25	497	99	246	245	03.09.25	1	1	1	27	4	90.7 FM	Road
		Huhura	125	287	PHA	Yes	19.08.25	220	50	114	115	03.09.25	1	1	1	17	6	90.7 FM	Road
		Sopura LTC Blocks	627	635	PHA	Yes	20.08.25	703	133	490	490	03.09.25	1	1	1	17	4	90.7 FM	Road
		Bagou		NEW	PHA	Yes	21.08.25	461	94	240	240	03.09.25	1	1	1	27	5	90.7 FM	Road
7	Popondetta Urban		4,665	5,968				5578	1105	2782	2779		11	11	11	286	37		
		Ajoro	401	511	PHA	Yes	27.08.25	795	169	418	415	03.09.25	1	1	1	16	0	90.7 FM	Road
		Hohota Blocks	1,179	1,112	PHA	Yes	25.08.25	1015	212	524	527	03.09.25	1	1	1	82	7	90.7 FM	Road
		Inonda	48	210	PHA	Yes	20.08.25	305	54	156	156	03.09.25	1	1	1	44	1	90.7 FM	Road
		Hiriju	283	341	PHA	Yes	27.08.25	313	50	139	139	02.09.25	1	1	1			90.7 FM	Road
		Mosou	339	336	PHA	Yes	19.08.25	425	89	206	206	03.09.25	1	1	1	15	0	90.7 FM	Road
		Sewa	317	588	PHA	Yes	27.08.25	480	94	226	226	03.09.25	1	1	1	2		90.7 FM	Road
		Jomota (Dirita)	367	1,048	PHA	Yes	27.08.25	594	104	275	275	02.09.25	1	1	1			90.7 FM	Road
		Pendereta	206	0	PHA														Closed
		Oseta	182	0	PHA														Closed
		Inota	360	568	PHA	Yes	20.08.25	301	67	152	153	03.09.25	1	1	1	4	0	90.7 FM	Road
		Awowota	235	479	PHA	Yes	27.08.25	404	77	186	186	02.09.25	1	1	1	41	10	90.7 FM	Road
		Girua Blocks	667	738	PHA	Yes	26.08.25	695	139	377	373	03.09.25	1	1	1	65	13	90.7 FM	Road
		Ijika Community School	79	38	PHA	Yes	25.08.25	251	50	123	123	03.09.25	1	1	1	17	6	90.7 FM	Road

LLG	Ward	Village	2025 Population Based On 2000 Census	2025 Population Based On 2022 Survey	Health Centre	Volunteer Form Completed	Date Of Survey	Population Surveyed	House Holds Surveyed	LLINs Allocated	Nets Issued	Date Of Distribution	Villages	Digicel	Bmobile	Houses With Phones	Houses With Radios	Radio Networks	Comments
8			6,542	8,525				7926	1633	3937	4016		14	14	14	631	116		
		Kakendetta	655	2,587	PHA	Yes	25.08.25	2164	472	1088	1170	04.09.25	1	1	1	277	22	90.7 FM	Road
		Jegarata	173	0	PHA														Closed
		Jonita	519	960	PHA	Yes	25.08.25	848	154	419	420	04.09.25	1	1	1	36	7	90.7 FM	Road
		Haruro	331	929	PHA	Yes	25.08.25	729	143	386	381	04.09.25	1	1	1	43	2	90.7 FM	Road
		Epa 1	96	516	PHA	Yes	26.08.25	347	84	173	173	03.09.25	1	1	1	13	14	90.7 FM	Road
		Ohiki	274	416	PHA	Yes	25.08.25	472	73	215	215	04.09.25	1	1	1	12	8	90.7 FM	Road
		Ususu	60	0	PHA														Closed
		Epa	920	0	PHA														Closed
		Epa (Incl Oil Palm Village)	53	0	PHA	Yes	20.08.25	440	100	218	218	30.08.25	1	1	1	42	4	90.7 FM	Road
		Dahana Blocks	365	316	PHA	Yes	25.08.25	246	50	118	118	02.09.25	1	1	1	35	17	90.7 FM	Road
		Bahupi Blocks	310	563	PHA	Yes	25.08.25	279	64	128	128	02.09.25	1	1	1			90.7 FM	Road
		Tombata	199	0	PHA	Yes	26.08.25	244	49	112	112	02.09.25	1	1	1	8	3	90.7 FM	Road
		Girua Blocks	94	0	PHA														Closed
		Pohemo Vop Blocks	295	0	PHA														Closed
		Newton College	271	187	PHA	Yes	29.08.25	159	24	76	76	01.09.25	1	1	1	21	0	90.7 FM	Road
		Isuga	214	0	PHA														Closed
		Puhemo	307	702	PHA	Yes	26.08.25	653	121	347	348	04.09.25	1	1	1	1	5	90.7 FM	Road
		Jegarata Anglican Mission	245	0	PHA														Closed
		Hegata	723	723	PHA	Yes	28.08.25	757	158	356	356	03.09.25	1	1	1	110	17	90.7 FM	Road
		Auga	144	215	PHA	Yes	22.08.25	201	49	98	98	04.09.25	1	1	1			90.7 FM	Road
		Sima	295	411	PHA	Yes	25.08.25	387	92	203	203	04.09.25	1	1	1	33	17	90.7 FM	Road
9			2,939	10,464				11900	2246	6169	6098		6	6	6	285	101		
		Dobuduru	634	5,405	PHA	Yes	21.08.25	6208	1129	3211	3138	05.09.25	1	1	1	68	30	90.7 FM	Road
		Huvivi	507	1,746	PHA	Yes	21.08.25	1491	313	784	776	05.09.25	1	1	1	12	2	90.7 FM	Road
		Monge 1/2/3/485	579	0	PHA														Closed
		Kongona	358	1,213	PHA	Yes	21.08.25	1172	250	613	609	08.09.25	1	1	1	91	25	90.7 FM	Road
		Monsota	199	257	PHA	Yes	27.08.25	130	25	64	64	05.09.25	1	1	1	1	2	90.7 FM	Road
		Sigana	187	791	PHA	Yes	21.08.25	928	179	469	470	05.09.25	1	1	1	110	39	90.7 FM	Road
		Hingororutu	475	1,052	PHA	Yes	21.08.25	1971	350	1028	1041	05.09.25	1	1	1	3	3	90.7 FM	Road
10			5,030	5,426				5061	1117	2551	2553		2	2	2	380	62		
		Sorovi Settlement	4,321	4,767	PHA	Yes	23.08.25	4346	987	2238	2222	04.09.25	1	1	1	263	62	90.7 FM	Road
		Sorovi Staiton	377	659	PHA	Yes	23.08.25	715	130	313	331	04.09.25	1	1	1	117	0	90.7 FM	Road
		Haugata	72	0	PHA														Closed
		Angorota	259	0	PHA														Closed
11			3,683	3,154				2572	467	1258	1261		1	1	1	161	22		
		East Embogo	1,539	2,034	PHA														Closed
		Double Cross Settlements	720	1,120	PHA														Closed
		Irigi Oil Palm Village	1,424	0	PHA	Yes	18.08.25	2572	467	1258	1261	30.08.25	1	1	1	161	22	90.7 FM	Road
